

ACC

AC/TN/54/C.E.

10000 | 148 | 1528

RE.
JL

1425

Declassified E.O. 12356 Section 3.3/NND No. 785021

/C.E.

10000 | 148 | 1528

REPORTS LINES 242-245-246
JUNE - NOV. 1945

RAILWAY CONSTRUCTION CONTRACT WORK UNDER CONTROL OF ALLIED COMMISSION

Line 242. Civitanova - Albacina.

State of work as of

All structural work and telephone installations completed. Line in service.

000
000
000

1001

RAILWAY CONSTRUCTION CONTRACT WORK UNDER CONTROL OF ALLIED COMMISSION.

Civitanova - Albacine.

State of work as at 30th November 1945.

1 structural work and telephone installations completed. Line in service.

— 000 —
000
000

RAILWAY CONSTRUCTION CONTRACT WORK UNDER CONTROL OF ALLIED COMMISSION

Line 245. Porto D'Ascoli - Ascoli Picena.

State of work as

All structural work and telephone installation completed. Line in service.

-----0000-----000-----000-----

0392

RAILWAY CONSTRUCTION CONTRACT WORK UNDER CONTROL OF ALLIED COMMISSION.

Ascoli - Ascoli Picena.

State of work as at 30th November 1945

1 structural work and telephone installation completed. Line in service.

-----0000-----000-----000-----

RAILWAYS CONSTRUCTION CONTRACT WORK UNDER CONTROL OF ALLIED COMMISSION.

Line 242. Civitanova - Albacina.

30th Oct

All structural work completed. Line ready for traffic when telephone installations
Work in hand by I.S.R. Signal Office. Estimated line will be operated during second week

5029

RAILWAYS CONSTRUCTION CONTRACT WORK UNDER CONTROL OF ALLIED COMMISSION.

30th October 1945.

Manova - Albacina.

Structural work completed. Line ready for traffic when telephone installations are completed.
by I.S.R. Signal Office. Estimated line will be operated during second week of November.

=====

RAILWAYS CONSTRUCTION CONTRACT WORK UNDER CONTROL OF ALLIED COMMISSION.

Line 245. P: Ascoli - Ascoli Picena.

30th Oct

Job No	Agency	Location	Description	Size	%	Estd. date of compl.	
AC/245/1001			<u>S A M E A S S E P T E M B E R R E P O R T .</u>				
AC/245/1002			<u>S A M E A S S E P T E M B E R R E P O R T .</u>				
AC/245/1003			<u>S A M E A S S E P T E M B E R R E P O R T .</u>				
AC/245/1004			<u>S A M E A S S E P T E M B E R R E P O R T .</u>				
AC/245/1005			<u>S A M E A S S E P T E M B E R R E P O R T .</u>				
AC/245/1006	Contract C. Muratori "Metauro"	Offida	Repair to bridge at Km. 22.28	Build central pier & provide Steel superstructure	100%		Te Br
AC/245/1007	Contract C. Muratori "Metauro"	Ascoli	Repair to bridge	Build 3 piers & provide steel superstructure (R.S.J's)	90%	?	Te co ave R 1w rec
AC/245/1008	I.S.R.	Offida Castel di Lama to Ascoli	Track repairs	11.98 Km. Track maintenance & minor renewals	99%	?	On AC/ all

1433

Declassified E.O. 12356 Section 3.3/NND No. 785021

RAILWAYS CONSTRUCTION CONTRACT WORK UNDER CONTROL OF ALLIED COMMISSION.

Ascoli - Ascoli Picena.30th October 1945.

Location	Description	Size	%	Estd. date of compl.	Remarks.
AS SEPTEMBER REPORT.					
AS SEPTEMBER REPORT.					
AS SEPTEMBER REPORT.					
AS SEPTEMBER REPORT.					
AS SEPTEMBER REPORT.					
Offida	Repair to bridge at Km. 22.28	Build central pier & provide Steel superstructure	100%		Temporary steel work completed. Bridge ready for traffic.
Ascoli	Repair to bridge	Build 3 piers & provide steel superstructure (R.S.J's)	96%	?	Temporary steel work 50% completed. Crane now not available to complete work. Estimated on return of crane 1 week required to make bridge ready for traffic.
Offida Castel di Lama to Ascoli	Track repairs	11.98 Km. Track maintenance & minor renewals	99%	?	Only track over Job N° AC/245/1007 - to complete all work.

RAILWAY CONSTRUCTION CONTRACT WORK UNDER CONTROL OF ALLIED COMMISSION.

Line 246. Giulianova - Teramo.

State of work as at 30th C

All work completed and line open to traffic.

=====

5627

RAILWAY CONSTRUCTION CONTRACT WORK UNDER CONTROL OF ALLIED COMMISSION.

Giulianova - Teramo.




State of work as at 30th October 1945.

All work completed and line open to traffic.

=====

MAPS AND CHARTS TOO LARGE TO FILM
ON ONE EXPOSURE ARE FILMED CLOCKWISE
BEGINNING IN THE UPPER LEFT CORNER,
LEFT TO RIGHT, AND TOP TO BOTTOM.

SEE DIAGRAMS BELOW.




14371


PONTI CON IMPALLATURE PROVVISORIE TIPO MILITARE

LINEA GIULIANA-TERAMO

Pont^{no} in ferro di luce m. 4 (13' $\frac{9}{16}$ ")
Km. 12+547,00

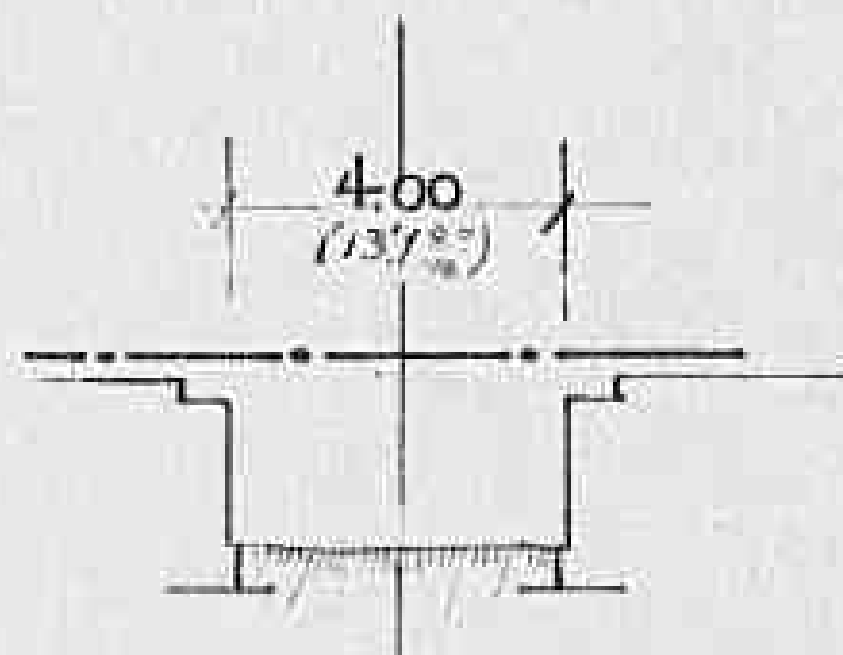


LINEA PO

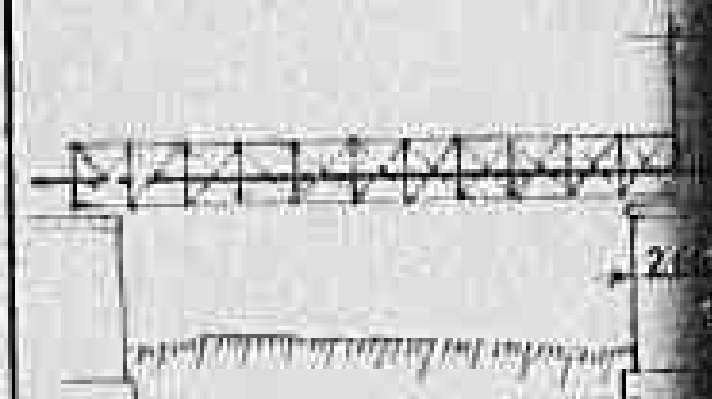


LINEA PORTO D'ASCOLI-ASCOLI P.

Ponte obliquo luce m. 20 ($65'7\frac{1}{8}$) sul retto
 m. 22,65 ($74'3\frac{1}{8}$) sull'obliquo - Km. 22+275,00

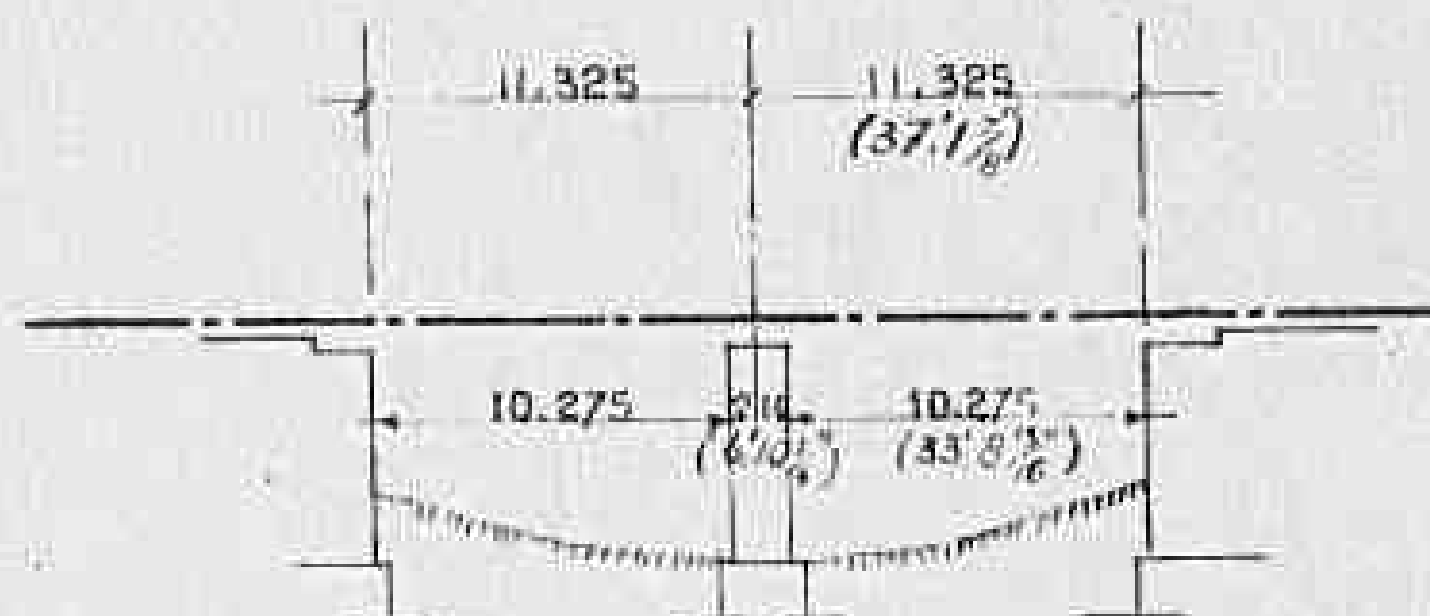


Ponte a 5 campate di luce m. 25 c. ($82'0\frac{1}{4}$)
 sul Fiume Tronto - Km. 25+110

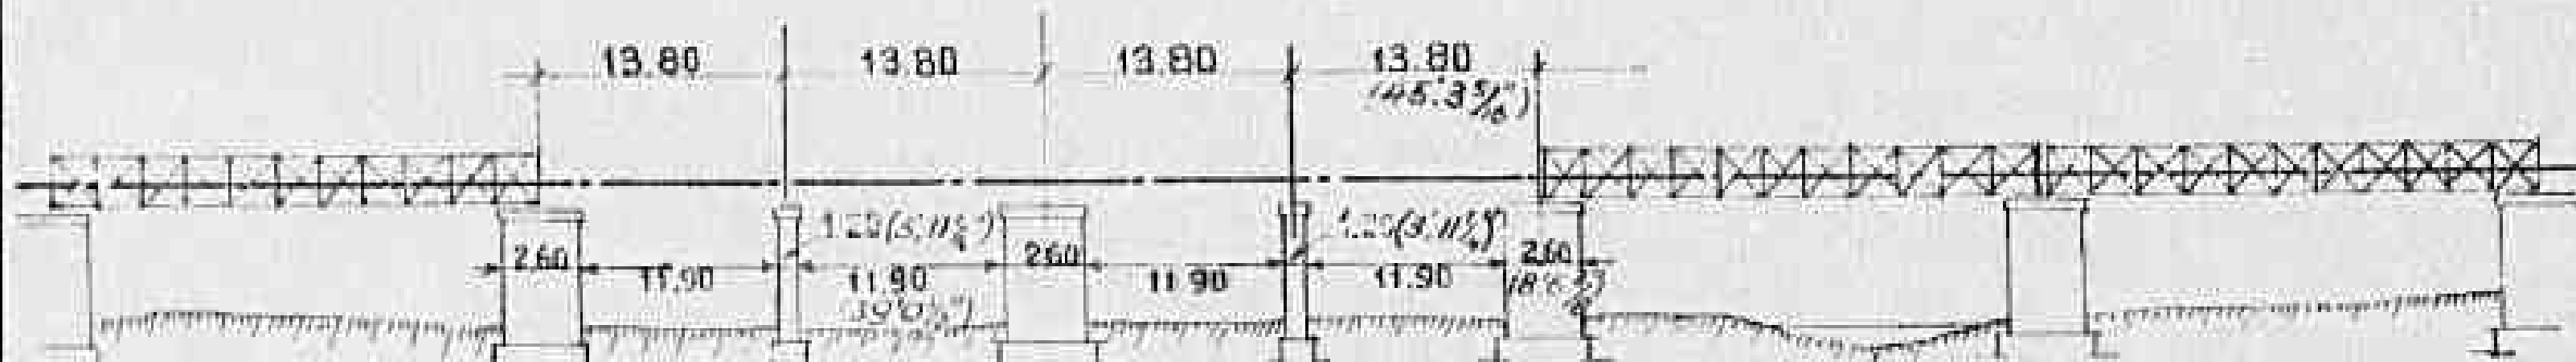


LINEA CIVITANOVA M. - ALBACINA

Pont. ¹¹⁰ obliquo luce m. 5 ($16' 17\frac{3}{8}"$) sul retto
 m. 5,10 ($16' 8\frac{1}{16}"$) sull'obliquo - Km. 12+526,70

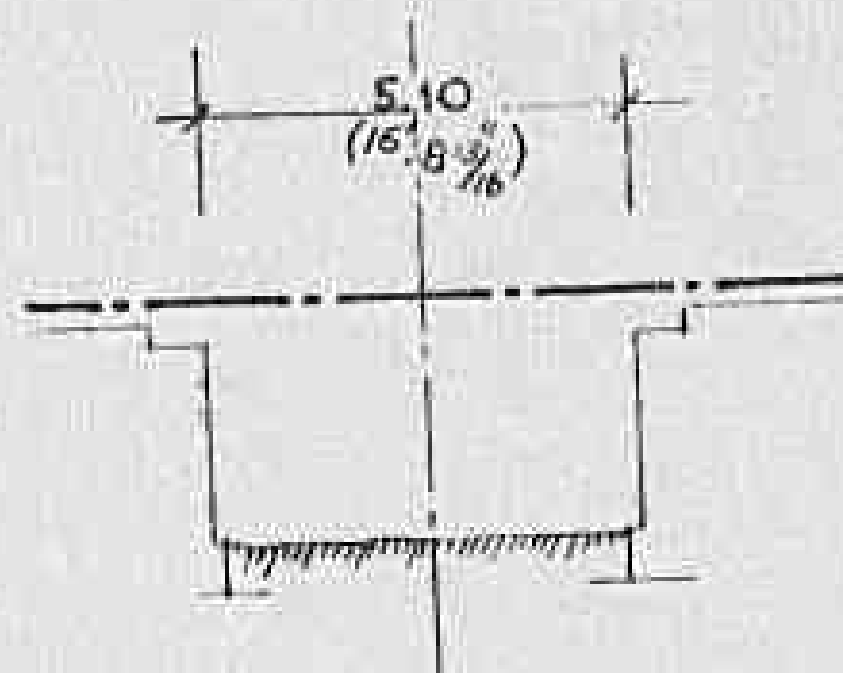


sottop. obliquo luce m. 5,47 ($17' 11\frac{3}{8}"$) sul retto
 m. 11,20 ($36' 8\frac{3}{16}"$) sull'obliquo - Km. 57+278,92

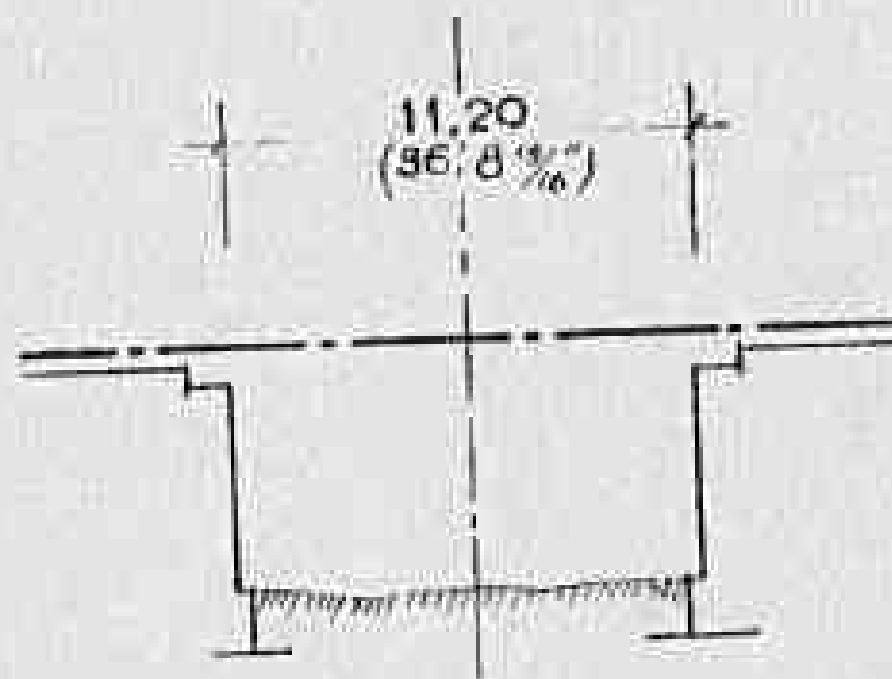

57% sul retto
 275,00

m. 25 c. ($82' 0\frac{1}{2}"$)
 110

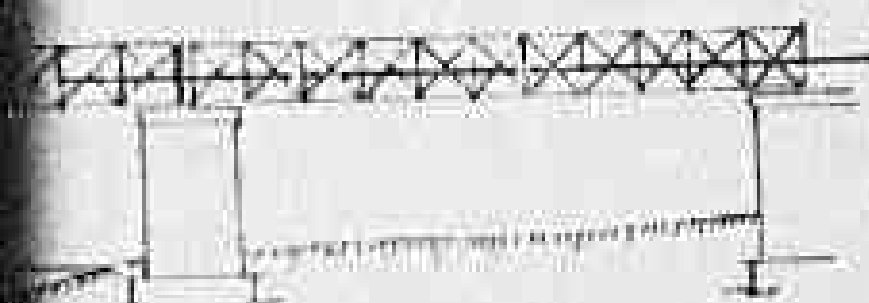

ELENCO TRAVI PROVVISORIE MILITARI
OCCORRENTI PER LE LINEE:
GIULIANOVA - TERAMO
P.D'ASCOLI - ASCOLI P.
CIVITANOVA M. - ALBACINA

Declassified E.O. 12356 Section 3.3/NND No.

785021

Descrizione Ponte	Progressiva	Numero delle travi occorrenti	Lunghezza delle travi	Sezione Travi	Osservazioni
Linea: Giulianova - Teramo 242					
Ponticello in ferro di luce m. 4 (13.19%)	Km. 12+547.00	4	21'0"	12" x 6"	
Linea: Porto d'Ascoli - Ascoli P. 243					
1 Ponte obliquo luce m. 22.65 (74.35%) sull'obliquo compila centrale di m. 2.10 (6'10 3/4")	Km. 22+275.00	12	38'0"	24" x 7 1/2"	
2 Ponte in ferro a 5 luci di m. 25 cias. (82.0%) Per le 2 campate da ri- fare si costruiscono due pile compilate da m. 125 (3'11 1/2")	Km. 25+110.00	24	45'0" standard girders	211" x 6"	
Linea Civitanova M. Albacina 242					
1 Ponte obliquo luce m. 5.10 (16.81%) sull'obli- quo -	Km. 12+526.70	4	24'0"	24" x 7 1/2"	
2 Sottopassaggio obliquo di luce 11.20 (35'8 5/16") sull'obliquo	Km. 57+278.92	6	37'0"	24" x 7 1/2"	

Descrizione Ponte	Progressiva	Travi occorrenti	Travi	Travi
Linea: Giulianova - Teramo 246				
Ponticello in ferro di luce m. 14 (13' 19 1/16")	Km. 12+547.00	4	21' 0"	12" x 6"
Linea: Porto d'Ascoli - Ascoli P. 245				
1 Ponte obliquo luce m. 22.65 (74' 3 5/16") sull'obliquo con pila centrale di m. 2.10 (6' 10 3/4")	Km. 22+275.00	12	38' 0"	24" x 7 1/2"
2 Ponte in ferro a 5 luci di m. 25 c.a.c. (82' 0 1/4") Per le 2 campate da ri- fare si costruiscono due pile compatte da m. 11.6 (3' 11 1/4")	Km. 25+110.00	24	45' 0" standard girders	2' 11" x 6"
Linea Civitanova M. Albacina 242				
1 Ponte obliquo luce m. 5.10 (16' 8 1/16") sull'obli- quo -	Km. 12+526.70	4	24' 0"	24" x 7 1/2"
2 Sottopassaggio obliquo di luce 11.20 (36' 8 1/16") sull'obliquo	Km. 57+278.92	6	37' 0"	24" x 7 1/2"



MINISTERO DEI TRASPORTI

FERROVIE DELLO STATO
DIREZIONE GENERALE

SERVIZIO LAVORI

OGGETTO

Rapporti mensili

Andamento lavori.

ALLEGATI N. 3

Roma

194

N.

L.5/13/61814

Al N.

del

AL SIG. COLONELLO STREET.

SOTTOCOMMISSIONE TRASPORTI

Piano 3° Stanza 52°

S E D E

- 1) A seguito della lettera n°L.5/13/61795 del 3/9/45
- 2) Si trasmette il rapporto relativo al mese di settembre per lo stato dei lavori in corso a Napoli Centrale e sulle linee A.C.291 - Cancellò - Torre Annunziata, A.C. 282 - Torre Annunziata - Castellammare di Stabia ed A.C.279 - Campobasso - Benevento (Galleria Ferrazzano).

IL CAPO DEL SERVIZIO

Lo Deque

*It will be necessary to subdivide
or cut the report, which more than one
file as on a page - the cut off
portion to have a heading date etc
Out on*

QHP

5625

RAILWAY CONSTRUCTION CONTRACT WORK UNDER CONTROL OF ALLIED COMMISSION

state of works 30/

job n.	agency	location	description	size	%	est date of completion	
		<u>Napoli Centrale</u>	<i>Sopra passaggio</i>				Eseguita di volta in volta
	Pomarici C. Napoli C.le		ripristino e sistemazione del sottovia in via Gianturco. <i>underpass</i>	sottovia a 3 luci	65	15/12/45	mazione zione p Cassino Foggia. In corso dei lavori di dissest
	Contardi C. Napoli		lavori occorrenti per la ricostruzione del volto della galleria artificiale fra le staz. Napoli P. Garibaldi e via Gianturco.		43	30/11/45	Eseguita mattoni ficiate Iniziate struttu in corso piede

A.C/291 - Linea Cancellio - Torre Annunziata

A.C/291 1001	<i>Cancellio C.</i>	<i>Bosceraale e S. Giuseppe Vesuviano</i>	ricostruzione "F.V. di Bosceraale e di S. Giuseppe Vesuviano.		40	20/11/45	In corso Bosceraale S. Giuseppe
-----------------	---------------------	---	---	--	----	----------	---------------------------------

RAILWAY CONSTRUCTION CONTRACT WORK UNDER CONTROL OF ALLIED COMMISSION

state of works 30/3/1945

location	description	size	%	est date of completion	remarks
	<i>Sopra passaggio</i>				Eseguita costruzione ml. 30 di volto - Iniziata la sistemazione stradale per la deviazione provvisoria della linea Cassino - Napoli e Napoli - Foggia.
Napoli C.le	ripristino e sistemazione del sottovia in via Gianturco. <i>lavori in corso</i>	sottovia a 3 luci	65	15/12/45	In corso lavori di demolizione dei restanti tratti di volto dissestati.
Napoli	lavori occorrenti per la ricostruzione del volto della galleria artificiale fra le staz. Napoli P. Garibaldi e via Gianturco.		43	30/11/45	Eseguiti ml. 38 di volto in mattoni nella galleria artificiale. Iniziata demolizione delle strutture in c.a. del solaio in corrispondenza del marciapiede di testa.
=====					
Boscereale - Torre Annunziata					
Boscereale e S. Giuseppe Vesuviano	ricostruzione F.V. di Boscereale e di S. Giuseppe Vesuviano.		40	20/11/45	In corso muratura 1° piano a Boscereale e riparazioni a S. Giuseppe Vesuviano.

A.C/291 Linea Canello - Torre Annunziata (continued)

A.C/291 1002	Filetici	km. 1+703	ricostruzione ponte a volte	I luce m.4.40	10	24/11/45	In corso pr
A.C/291 1003		km. 4+308	ricostruzione ponte, già a travata in ferro, a due volti in muratura.	luce m.14.45	15	24/11/45	Si sta cos provvisori cantiere.
A.C.291 1004		km. 5+543	ricostruzione ponte oblique, già a travata in ferro, a volto in muratura	1 luce m.7.90	25	24/11/45	Eseguito a stanno pre
A.C/291 1005		Km. 16+878	ricostruzione ponte oblique, già a travata in ferro, con due volti in muratura.	luce m.13.80	100	24/11/45	Ultimato.
A.C/291 1006		km. 20+145	ricostruzione ponte, già a travata in ferro, in c.a.	I luce m.9.75	30	24/11/45	In prepara ferro e f
A.C/291 1007		km. 21+002	ricostruzione ponte, già a travata in ferro, in c.a.	I luce m.9.85	38	24/11/45	Idem.
A.C/291 1008	Apolloni	km. 12+325	ricostruzione ponte con travata in ferro	I luce m.9.45	38	4/7/45	Il lavoro ritardata occorrent Terni.
A.C/291 1009		km. 18+097	ricostruzione ponte oblique con travata in ferro	1 luce m.11.00	38	24/8/45	Idem.
A.C/291 1010		km. 19+645	ricostruzione ponte oblique con travata in ferro.	1 luce m.7.85	38	24/8/45	Idem.

././.

linea Canello - Torre Annunziata

(continued)

m. 1+703	ricostruzione ponte a volte	I luce m.4.40	10	24/11/45	In corso preparazione centine.
m. 4+308	ricostruzione ponte, già a travata in ferro, a due volti in muratura.	luce m.14.45	15	24/11/45	Si sta costruendo deviazione provvisoria e si allestendo il cantiere.
m. 5+543	ricostruzione ponte oblique, già a travata in ferro, a volte in muratura	1 luce m.7.90	25	24/11/45	Eseguito alzamento binario, si stanno preparando centine.
m. 16+878	ricostruzione ponte oblique, già a travata in ferro, con due volti in muratura.	luce m.13.80	100	24/11/45	Ultimate.
m. 20+145	ricostruzione ponte, già a travata in ferro, in c.a.	I luce m.9.75	30	24/11/45	In preparazione sagomatura ferro e formazione casseforme.
m. 21+002	ricostruzione ponte, già a travata in ferro, in c.a.	I luce m.9.85	38	24/11/45	Idem.
m. 12+325	ricostruzione ponte con travata in ferro	I luce m.9.45	38	4/7/45	Il lavoro va a rilento per la ritardata consegna dei ferri occorrenti da parte della S.A. Terni.
m. 18+097	ricostruzione ponte oblique con travata in ferro	1 luce m.11.00	38	24/8/45	Idem.
m. 19+645	ricostruzione ponte oblique con travata in ferro.	1 luce m.7.85	38	24/8/45	Idem.

././.

A.C/291 linea Cannello - Torre Annunziata (continued)

A.C/291 1011	personale di organico e Grivofer		lavori di ripristino binario		56		Si è armato 15+600 al km zione dipend tà di avere ti.
A.C/282 1001	Giugliano	km. 2+518	ricostruzione ponte sul fiume Sarno		20	22/12/49	Prossimo Eseguito app riali ed impi
A.C.279 1001	Mulinari	Campobasso	riattivazione definiti va della galleria "Con trafforte "Ferrazzano".		60	17/12/45	Eseguiti al ra calotta Iniziati mu l'imbocco.

ea Cannello - Torre Annunziata (continued)

	lavori di ripristino binario	56		Si è armato il binario dal km. 15+600 al km. 16+200 - l'ultima+ zione dipenderà dalla possibilità di avere i materiali occorren- ti.
ea Torren Annunziata C.de - Castellammare di Stabia				
4518	ricostruzione ponte sul fiume Sarne	20	32/12/45	<i>Prossimo inizio dei getti</i> Eseguito approvvigionamento materiali ed impianto cantiere.
mpobasso - Benevento				
asso	riattivazione definiti- va della galleria "Con- trafforte "Ferrazzano".	60	17/22/45	Eseguiti altri 33 m. di muratu- ra calotta e 8 di arcovevoscio Iniziati muri rivestimento al- l'imbocco.

RAILWAY CONSTRUCTION CONTRACT WORK UNDER CONTROL OF
ALLIED COMMISSION

LINE 245 - GIULIANOVA - TERAMO

State of Work as at 25 SEPTEMBER 1945

Job No.	Agency	Location	Description	Size	%	Est'd comple.
AG/246/1001	I.S.R.	Giulianova to Bellante Ripattone	Track repairs	13.61 Km. track maintenance & minor renewals.	100%	
AG/246/1002	Contract Puccini	Bellante Ripattone	Repairs to bridge at 11.61 Km.	Rebuild one brick arch of 15 mt. span.	100%	
AG/246/1003	Contract Puccini	Bellante Ripattone	Repairs to bridge at 12.55 Km.	Rebuild abutments & provide steel superstructure of 4 mt. span. (R.S.J's)	100%	
AG/246/1004	Contract Puccini	Bellante Ripattone	Repairs to bridge at 13.69 Km.	Rebuild one pier & 2 brick arches each of 12 mt. span.	100%	
AG/245/1005	Contract Puccini	Castellalto	Repairs to bridge at 19.12 Km.	Rebuild 4 piers & 5 brick arches each of 8.45 mt. span.	100%	
AG/245/1006	Contract Puccini	Teramo	Repairs to bridge at 23.67 Km.	Rebuild one pier & 5 brick arches each of 20 mt. span.	99%	2 Oct.
AG/246/1007	I.S.R.	Bellante Ripattone to Teramo	Track repairs.	11.47 Km. of track maintenance and minor renewals.	100%	

2595

RAILWAY CONSTRUCTION CONTRACT WORK UNDER CONTROL OF

ALLIED COMMISSION

State of Work as at 26 SEPTEMBER 1945

Location	Description	Size	%	Est'd Comple	Remarks
Giulianova to Bellante Ripattone	Track repairs	13.61 Km. track maintenance & minor renewals.	100%		
Bellante Ripattone	Repairs to bridge	Rebuild one brick arch of 15 mt. span.	100%		Steel handrail to fix. No material available.
Bellante Ripattone	Repairs to bridge	Rebuild abutments & provide steel superstructure of 4 mt. span. (R.S.J's)	100%		
Bellante Ripattone	Repairs to bridge	Rebuild one pier & 2 brick arches each of 12 mt. span.	100%		Steel handrail to fix. No material available.
Castellalto	Repairs to bridge	Rebuild 4 piers & 5 brick arches each of 8.45 mt. span.	100%		Steel handrail to fix. No material available.
Teramo	Repairs to bridge	Rebuild one pier & 5 brick arches each of 20 mt. span.	99%	2 Oct.	Coping only to finish.
Bellante Ripattone to Teramo	Track repairs.	11.47 Km. of track maintenance and minor renewals.	100%		

LINE 242 - CIVITANOVA - ASSASSINA

RAILWAYS CONSTRUCTION CONTRACT WORK UNDER CONTROL
OF ALLIED COMMISSION

State of Work as at 26 SEPTEMBER 1945

Job No.	Agency	Location	Description	Size	%	Est'd compl.	
AC/242/1001	I.S.R.	Civitanova to Nerrovale	Track repairs	12.71 Km. track maintenance & minor renewals	100%		
AC/242/1002	Contract G. Muratori	Nerrovale	Repairs to bridge at 12.55 Km.	Rebuild abut- ment & provide steel super- structure.	100%		Steel R.S.J.'s slaved for this bridge.
AC/242/1003	I.S.R.	Nerrovale to Macerata	Track repairs.	14.47 Km. track maintenance & minor renewals.	100%		
AC/242/1004	Contract G. Muratori	Macerata	Repairs to bridge at 26.35 Km.	Rebuild 7 piers & 8 brick arches each of 13 mt. span.	95%	5 Oct.	Underpinning of 3 completed. Work held by short supply of
AC/242/1005	Contract G. Muratori Metauro	Macerata	Repairs to tunnel 27.81	Rebuild 12 mt. length of brick barrel	100%		
AC/242/1006	I.S.R.	Macerata to Tolentino	Track repairs.	18.53 Km. track maintenance & minor renewals.	100%		

RAILWAYS CONSTRUCTION CONTRACT WORK UNDER CONTROL
OF ALLIED COMMISSION

Sheet 1

State of Work as at 26 SEPTEMBER 1945

Office Copy

Location	Description	Size	%	Est'd comple.	Remarks
Itanova to Provalle	Track repairs	12.71 Km. track	100%		
		maintenance & minor renewals			
Provalle	Repairs to bridge at 12.55 Km.	Rebuild abutment & provide steel super-structure.	100%		Steel R.S.J's salvaged ex Pescara & used for this bridge.
Provalle to Acerata	Track repairs.	14.47 Km. track	100%		
		maintenance & minor renewals			
Acerata	Repairs to bridge at 26.35 Km.	Rebuild 7 piers & 8 brick arches each of 13 mt. span.	95%	5 Oct.	Underpinning of 3 piers still in hand .85% completed. Work has been seriously retarded by short supply of cement.
Acerata	Repairs to tunnel 27.81	Rebuild 12 mt. length of brick barrel	100%		
Acerata to Colatino	Track repairs.	18.53 Km. track	100%		
		maintenance & minor renewals			

LINE 242 - CIVITANOVA - ASBRACINA

Job No.	Agency	Location	Description	Size	%	Est'd comple	
AC/242/1007	Contract Impresa Puccini	Pollenza	Repairs to bridge at 40.85 Km?	Rebuild 2 brick arches each of 10 mt. span.	98%	3 Oct.	Parapet wa Ready for
AC/242/1008	Contract Impresa Puccini	S. Severino	Repairs to bridge at 56.09 Km.	Rebuild 1 brick arch of 17 mt. span.	85%	3 Oct.	Spandrels walls to b
AC/242/1009	Contract Impresa Puccini	S. Severino	Repairs to bridge at 57.28 Km.	Rebuild abutments & provide steel superstructure.	75%	5 Oct.	All masonry structure Marche. En of B.O.E. site. Date arrival at
AC/242/1010	Contract Impresa Puccini	Castel- Raimondo	Repairs to bridge at 58.11 Km.	Rebuild 1 brick arch of 8 mt. span.	99%	2 Oct.	Parapets o
AC/242/1011	I.S.R.	Tolentino to Castel Raimondo	Track repairs	21.54 Km. track maintenance.	98%	7 Oct.	All track structures
AC/242/1012	Contract Impresa Puccini	Castel- Raimondo	Repairs to bridge at 68.59 Km.	Rebuild 1 brick arch of 7 mt. span	100%		
AC/242/1013	Contract Impresa Puccini	Cerreto d'Est	Repairs to bridge at 80.78 Km.	Rebuild 1 brick arch of 7 mt. span.	99%	2 Oct.	Parapets o

Sheet 2

ACINA

Station	Description	Size	%	Test'd comple	Remarks
enza	Repairs to bridge at 40.86 Km.	Rebuild 2 brick arches each of 10 mt. span.	90%	3 Oct.	Parapet walls only to completed work Ready for traffic.
verino	Repairs to bridge at 56.09 Km.	Rebuild 1 brick arch of 17 mt. span.	85%	3 Oct.	Spandrels 90% completed and parapet walls to build to complete work.
verino	Repairs to bridge at 57.28 Km.	Rebuild abutments & provide steel superstructure.	75%	5 Oct.	All masonry work completed. Steel super- structure fabricated at Civitanova del Marche. Erection delayed by non placing of B.O.Z. to transport transport to site. Date of completion subject to arrival at site by 2nd Oct.
stel- mondo	Repairs to bridge at 58.11 Km.	Rebuild 1 brick arch of 8 mt. span.	99%	2 Oct.	Parapets only to complete.
entino to Castel mondo	Track repairs	21.54 Km. track maintenance.	98%	7 Oct.	All track work completed except over xxxx structures not reported as completed.
stel- mondo	Repairs to bridge at 58.59 Km.	Rebuild 1 brick arch of 7 mt. span	100%		
ereto esi	Repairs to bridge at 60.78 Km.	Rebuild 1 brick arch of 7 mt. span.	99%	2 Oct.	Parapets only to complete.

LINE 242 - CIVITANOVA - ALBACINA

Job No.	Agency	Location	Description	Size	%	Est'd comple	Re
AC/242/1014	Contract Impresa Puccini	Carrezo Id'Esti .	Repairs to bridge at 83.12 Km.	Rebuild 1 brick arch of 10 mt.	100%		
AC/242/1015	Contract Impresa Puccini	Albacina	Repairs to bridge at 96.04 Km.	Rebuild 1 brick arch of 15 mt. span.	100%		
AC.242/1016	I.S.A.	Castel- Reino ndo to Albacina	Track repairs.	19.47 Km. track maintenance & minor renewals.	100%		

5619

1456

Sheet 3

BACINA

Location	Description	Size	% Est'd compl	Remarks
Crete	Repairs to bridge	Rebuild 1 brick	100%	
Si .	at 83.12 Km.	arch of 10 mt.		
Bacina	Repairs to bridge	Rebuild 1 brick	100%	
	at 95.04 Km.	arch of 15 mt.		
		span.		
Atel-	Track repairs.	19.47 Km. track	100%	
no ndo		Maintenance &		
Albacina		minor renewals.		

RAILWAY CONSTRUCTION CONTRACT WORK UNDER CONTROL
OF ALLIED COMMISSION

LINE 245 - ASCOLI - PORTO D'ASCOLI

State of work as at 25 SEPTEMBER 1945

Job No.	Agency	Location	Description	Size	% compl.	Remarks
AC/245/1001	Contract G. Muratori "Metauro"	Monnapolo	Repairs to bridge at 13.80 Km.	Rebuild 1 pier & 4 brick arches each of 15 mt. span.	100%	Steel handr fixed. No m Bridge test
AC/245/1002	Contract G. Muratori "Metauro"	Spinnetoli Colli	Repairs to bridge at 17.27 Km.	Rebuild 3 brick arches 1/3 mt. span & 2/4 mt. spans.	100%	Steel handr No material Bridge test
AC/245/1003	Contract G. Muratori "Metauro"	Spinnetoli Colli	Repairs to Bridge at 18.53 Km.	Rebuild 1 brick arch of 10 mt.	100%	Steel handr fixed. No Bridge test
AC/245/1005	Contract G. Muratori "Metauro"	Offida	Repairs to Bridge at 20.45 Km.	Rebuild 3 brick arch spans each of 15 mt.	100%	Steel handr fixed. No Bridge test
AC/245/1006	Contract G. Muratori "Metauro"	Offida	Repairs to Bridge at 22.28 Km.	Build central pier & provide steel superstructure.	75%	20 Oct. All masonry release of Estimated the Metauro
AC/245/1007	Contract G. Muratori "Metauro"	Ascoli	Repairs to Bridge at 25.11 Km.	Build 3 piers & provide steel super- structure (R.S.J's)	75%	20 Oct. 7 All masonry release of Estimated Metauro B
AC/245/1008	I.S.R. CR CO FO	Offida - Castel di Lama to Ascoli	Track repairs.	11.98 Km. track maintenance & minor renewals.	98%	25 Oct All track Don AC/245

RAILWAY CONSTRUCTION CONTRACT WORK UNDER CONTROL

345854

D'ACCOLI

OF ALLIED COMMISSION

State of work as at 26 SEPTEMBER 1945

Location	Description	Size	% compl.	Remarks
Sanampolo	Repairs to bridge at 13.80 Km.	Rebuild 1 pier & 4 brick arches each of 15 mt. span.	100%	Steel handrail to be supplied and fixed. No material at present available. Bridge tested.
Spineto Colli	Repairs to bridge at 17.27 Km.	Rebuild 3 brick arches 1/8 mt. span & 2 1/4 mt. spans.	100%	Steel handrail to be supplied and fixed. No material at present available. Bridge tested.
Spineto Colli	Repairs to Bridge at 18.53 Km.	Rebuild 1 brick arch of 10 mt.	100%	Steel handrail to be supplied and fixed. No material at present available. Bridge tested.
Offida	Repairs to Bridge at 20.05 Km.	Rebuild 3 brick arch spans each of 15 mt.	100%	Steel handrail to be supplied and fixed. No material at present available. Bridge tested.
Offida	Repairs to Bridge at 22.28 Km.	Build central pier & provide steel superstructure.	75%	20 Oct. All masonry work completed. Awaiting release of steelwork from Line 85 North. Estimated this will be released from the Metauro Bridge 10th Oct.
Accoli	Repairs to Bridge at 25.11 Km.	Build 3 piers & provide steel superstructure (R.S.J.'s)	75%	20 Oct.? All masonry work completed. Awaiting release of steelwork from Line 86 North. Estimated this will be released from Metauro Bridge 10th Oct.
Offida - Castel di Lama to Accoli	Track repairs.	11.98 Km. track maintenance & minor renewals.	99%	25 Oct. All track work completed except over Job AC/245/1006 & AC/245/1007.

RAILWAY CONSTRUCTION CONTRACT WORK UNDER CONTROL OF
ALLIED COMMISSION

LINE 245

Office Copy.

State of Work as at 31 AUGUST 1945

Job No.	Agency	Location	Description	Size	% Compl	Est'd Compl	
AC/245/1001	Contract C. Muratori "Metauro"	Monsan- polo	Repairs to Bridge at 13.80 Km.	Rebuild 1 pier & 4 brick arches each of 15 mt. span.	99%		Steel h material ble. Test
AC/245/1002	Contract C. Muratori "Metauro"	Spinetoli Colli	Repairs to Bridge at 17.27 Km.	Rebuild 3 brick arches 1/8 mt. span & 2/4 mt. spans.	99%		Steel h material ble. Test
AC/245/1003	XXXXXX I.S.R.	P. Ascoli to Offida - Castel di Lana.	Track repairs.	20.60 Km. of track maintenance & minor renewals.	100%		
AC/245/1004	Contract C. Muratori "Metauro"	Spinetoli Colli	Repairs to Bridge at 18.33 Km.	Rebuild 1 brick arch of 10 mt.	99%		Steel h train p
AC/245/1005	Contract C. Muratori "Metauro"	Offida	Repairs to Bridge at 20.15 Km.	Rebuild 3 brick arch spans each of 15 mt.	99%		Steel h train p
AC/245/1006	Contract C. Muratori "Metauro"	Offida	Repairs to Bridge at 22.28 Km.	Build central pier & provide Steel super- structure	75%	?	All mat Date of of steel day for P

RAILWAY CONSTRUCTION CONTRACT WORK UNDER CONTROL OF

Sheet 1

ALLIED COMMISSION

State of Work as at 31 AUGUST 1945

Location	Description	Size	% Compl.	Est'd Compl.	Remarks
Monsampolo	Repairs to Bridge at 13.80 Km.	Rebuild 1 pier & 4 brick arches each of 15 mt. span.	99%		Steel handrail only to fix. No material for this at present available. Test train passed over Bridge.
Spinetoli Colli	Repairs to Bridge at 17.27 Km.	Rebuild 3 brick arches 1/8 mt. span & 2/4 mt. spans.	99%		Steel handrail only to fix. No material for this at present available. Test train passed over Bridge.
P. Ascoli to Offida - Castel di Lana.	Track repairs.	20.60 Km. of track maintenance & minor renewals.	100%		
Spinetoli Colli	Repairs to Bridge at 18.33 Km.	Rebuild 1 brick arch of 10 mt.	99%		Steel handrail only to fix. Test train passed over Bridge.
Offida	Repairs to Bridge at 20.15 Km.	Rebuild 3 brick arch spans each of 15 mt.	99%		Steel handrail only to fix. Test train passed over Bridge.
Offida	Repairs to Bridge at 22.28 Km.	Build central pier & provide Steel super-structure	75%	?	All masonry work completed. Date of completion depends on supply of steel superstructure. Estimated 1 day to erect R.S.J's and 1 day for P. Way work.

State of Work as at 31 AUGUST 1945LINE 245

Job No.	Agency	Location	Description	Size	% ! Compl. !	! Est'd ! ! Compl. !	
AC/245/1007	Contract C. Muratori "Metauro"	Ascoli	Repairs to Bridge	Build 3 piers & provide steel superstructure (R.S.J's)	75%	?	All masonry w Date of complete steel work. E R.S.J. check a
AC/245/1008	I.S.R.	Offida - Caste ldi Lama to Ascoli	Track repairs.	11.98 Km. track maintenance & minor renewals.	98%	?	All track wor Job N° AC AC/245/1

5615

1462

State of Work as at 31 AUGUST 1945

Sheet 2

Location	Description	Size	% Est'd		Remarks
			!Compl.!	!Compln!	
Ascoli	Repairs to Bridge	Build 3 piers & provide steel superstructure (R.S.J's)	75%	?	All masonry work completed. . Date of completion depends on supply of steel work. Estimated 3 days to erect R.S.J. deck and 1 day for P.Way work.
Offida - Caste ldi Lama to Ascoli	Track repairs.	11.98 Km. track maintenance & minor renewals.	98%	?	All track work completed except on Job N° AC/245/1006 and AC/245/1007.

RAILWAY CONSTRUCTION CONTRACT WORK UNDER CONTROL

LINE 246

OF ALLIED COMMISSION

State of Work as at 31 A

Job No.	Agency	Location	Description	Size	Comp.	Est'd Compl.	
AC/246/1001	I.S.R.	Giulianova to Ballante Ripattone	Track repairs	13.61 Km. track maintenance & minor repairs	X 100%		
AC/246/1002	Contract Imp. Puccini	Ballante Ripattone	Repairs to Bridge at 11.61 Km.	Rebuild one brick arch of 15 mt. span.	98%		Coping & to comple
AC/246/1003	Contract Imp. Puccini	Ballante Ripattone	Repairs to Bridge at 12.75 Km.	Rebuild abutments & provide steel superstructure of 4 mt. span. (R.S.J's)	100%		Salvaged used.
AC/246/1004	Contract Imp. Puccini	Ballante Ripattone	Repairs to Bridge at 13.69 Km.	Rebuild one pier & 2 brick arches each of 12 mt. span.	98%		Coping & fix to c
AC/246/1005	Contract Imp. Puccini	Castellalto	Repairs to Bridge at 19.12 Km.	Rebuild 4 piers & 5 brick arches each of 8.45 mt. span.	90%		Coping & to fix t
AC/246/1006	Contract Imp. Puccini	Teramo	Repairs to Bridge at 23.57 Km.	Rebuild 1 pier & 5 brick arches each of 20 mt. span.	85%	10 Sept.	Arches & work ret ement.

RAILWAY CONSTRUCTION CONTRACT WORK UNDER CONTROL

Sheet 1

OF ARMED COMMISSION

State of work as at 31 August 45

Location	Description	Size	Comp.	Compn.	Remarks
Giulianova to Ballante Ripattone	Track repairs	13.61 Km. track maintenance & minor repairs	100%		
Ballante Ripattone	Repairs to Bridge at 11.61 Km.	Rebuild one brick arch of 15 mt. span.	98%		Coping & steel handrail to fix to complete all work.
Ballante Ripattone	Repairs to Bridge at 12.55 Km.	Rebuild abutments & provide steel superstructure of 4 mt. span. (R.S.J's)	100%		Salvaged Steel joists (Gosman) used.
Ballante Ripattone	Repairs to Bridge at 13.59 Km.	Rebuild one pier & 2 brick arches each of 12 mt. span.	98%		Coping and steel handrail to fix to complete all work.
Castellalto	Repairs to Bridge at 19.12 Km.	Rebuild 4 piers & 5 brick arches each of 8.45 Mt. span.	98%		Coping stones and steel handr. to fix to complete work.
Teramo	Rebuild 1 pier Repairs to Bridge at 23.57 Km.	Rebuild 1 pier & 5 brick arches each of 20 mt. span.	85%	10 Sept.	Arches completed, spandrels 80% Work retarded by short supply of cement.

State of work as at 31 AUGUST 1945ANCONA
LINE 246

Job No.	Agency	Location	Description	Size	Compl.	at
AC/246/1007	ANCONA	Bellante	Track repairs	11.47 Km. of	98%	10 Sept.
	IMP. I.S.R.	Ripettone		track maintenance		
	IMP. I.S.R.	to Teramo		& minor renewals		

NOTE : The Line from Giulianova to Bridge at 23.67 Km. now is used for ballast trains.

5613

1486

State of work as at 31 AUGUST 1945

Sheet 2

Location	Description	Size	! Compl !	Est'd ! Comp'ng !	Remarks
Bellante	! Track repairs !	11.47 Km. of	!	!	!
Ripettone	! track maintenance !		98%	10 Sept.	!
to Teramo	! & minor renewals !		!	!	!

Giulianova to Bridge at 23.67 Km. now is used for ballast trains.

E. J. M. N. N. N.

MINE 242

RAILWAY CONSTRUCTION WORK UNDER CONTROL OF
ALLIED COMMISSION

State of work as at 31 AUGUST 1945

Job No.	Agency	Location	Description	Size	Comp.	Est'd Comp'n	
AC/242/1001	I.S.R.	Civitavecchia to Murovalle	Track repairs maintenance & minor renewals.	12.7 Km. track	100%		
AC/242/1002	Contract G. Muratori	Murovalle	Repairs to Bridge at 12.55 Km.	Rebuild abutment & provide steel superstructure.	100%		Steel R.S.J. used for
AC/242/1003	I.S.R.	Murovalle to Macerata	Track repairs.	14.47 Km. track maintenance & minor renewals.	100%		
AC/242/1004	Contract G. Muratori Metauro	Macerata	Repairs to Bridge at 26.35 Km.	Rebuild 7 piers & 8 brick arches; each of 13 mt. span.	85%	15 Sept	Coping & original Additional & complete height of Work retar
AC/242/1005	Contract G. Muratori Metauro.	Macerata	Repairs to tunnel 27.81 Km.	Rebuild 12 mt. length of brick barrel.	100%		
AC/242/1006	I.S.R.	Macerata to Tolentino	Track repairs	16.52 Km. track maintenance & minor renewals.	100%		

RAILWAY CONSTRUCTION WORK UNDER CONTROL OF
ALLIED COMMISSION

Sheet 1

State of work as at 31 AUGUST 1945

Location	Description	Size	% Comp.	Est'd Comp'n	Remarks
Civitanova to Morrovalle	Track repairs	12.74 Km. track maintenance & minor renewals.	100%		
Morrovalle	Repairs to Bridge at 12.55 Km.	Rebuild abutment & provide steel superstructure.	100%		Steel R.S.J.'s salvaged ex Pescara used for this Bridge.
Morrovalle to Macerata	Track repairs.	14.47 Km. track maintenance & minor renewals.	100%		
Macerata	Repairs to Bridge at 26.35 Km.	Rebuild 7 piers & 6 brick arches each of 13 mt. span.	85%	15 Sept.	Coping & handrail to fix to complete original contract 98% complete. Additional work underpin 2 arches & completely rebuild 3 piers for a height of 7 mt. 65% complete. Work retarded on account of cement.
Macerata	Repairs to tunnel 27.81 Km.	Rebuild 12 mt. length of brick barrel.	100%		
Macerata to Tolentino	Track repairs	18.52 Km. track maintenance & minor renewals.	100%		

LINE 242

State of work as at 31 AUGUST 45

Job No.	Agency	Location	Description	Size	Compl.	Compl.	Remarks
AG/242/1007	Contract Imp. Puccini	Polignac	Repairs to bridge at 40.85 Km.	Rebuild 2 brick arches each of 10 mt. span.	80%	15 Sept.	Launching, f walls to co
AG/242/1008	Contract Imp. Puccini	S. Severino	Repairs to Bridge at 56. 08 Km.	Rebuild 1 brick arch of 17 mt. span	140%	5 Sept.	Arch & spar on condemned bricks. Th
AG/242/1009	Contract Imp. Puccini	S. Severino	Repairs to Bridge at 57.28 Km.	Rebuild abutments & provide steel superstructure	75%	15 Sept.	Abutments superstruc required salvaged & to be fabri days.
AG/242/1010	Contract Imp. Puccini	Castel - Raimondo	Repairs to Bridge at 68.11 Km.	Rebuild one brick arch of 8 mt. span.	30%	14 Sept.	Show bridge Trouble wi out. Work
AG/242/1011	I.C.R.	Tolentino to Castel- Raimondo	Track repairs.	21.54 Km. track maintenance.	85%	16 Sept.	
AG/242/1012	Contract Imp. Puccini	Castel- Raimondo	Repairs to Bridge at 68.59 Km.	Rebuild one brick arch of 8 mt. span.	98%		Coping to traffic.
AG/242/1013	Contract Imp. Puccini	Correto d'Esse	Repairs to Bridge at 80.78 Km.	Rebuild one brick arch of 7 mt. span.	90%	5 Sept.	Parapet w Ready for

Sheet 2

State of work as at 31 AUGUST 45

Location	Description	Size	Compl.	State	Remarks
Olivenza	Repairs to bridge at 40.85 Km.	Rebuild two brick arches each of 17 mt. span.	80%	15 Sept.	Haunching, filling and parapet walls to complete. awaiting cement.
S. Severino	Repairs to bridge at 56.08 Km.	Rebuild 1 brick arch of 17 mt. span	140%	5 Sept.	Arch & spandrels completed. Bridge on SHW workmanship of 50% of arch condemned owing to bad coursing of bricks. This will cause a delay of 20 days.
S. Severino	Repairs to bridge at 57.28 Km.	Rebuild abutments & provide steel superstructure	75%	15 Sept.	Abutments completed awaiting steel superstructure. Length of steel required 14 mt. Given orders for salvaged German Steel ex Pescara to be fabricated. Time required 15 days.
Casto - Raimondo	Repairs to bridge at 68.11 Km.	Rebuild one brick arch of 8 mt. span.	10%	14 Sept.	Shew bridge. Arch now 50% complete. Trouble with contractor re setting out. Work now satisfactory.
Tolentino to Castel-Raimondo	Track repairs.	21.54 Km. track maintenance.	85%	16 Sept.	
Castel-Raimondo	Repairs to bridge at 68.59 Km.	Rebuild one brick arch of 8 mt. span.	98%		Coping to complete work. Ready for traffic.
Cerreto d'Adda	Repairs to bridge at 80.78 Km.	Rebuild one brick arch of 7 mt. span.	90%	15 Sept.	Parapet walls to complete work. Ready for traffic.

LINE 242

State of work as at 31 AUGUST 1945

Job No.	Agency	Location	Description	Size	Compl.	Est'd Compl.
AC/242/10814	Contract Imp. Puccini	Gerreto d'Essi	Repairs to Bridge at 83.12 Km.	Rebuild 1 brick arch of 10 mt.	100%	11
AC/242/1015	Contract Imp. Puccini	A Labacina	Repairs to Bridge at 86.04 Km.	Rebuild 1 brick arch of 15 mt. span.	100%	
AC/242/1085	I.S.H.	Castel- Raimondo to Albacina	Track repairs.	18.47 Km. track maintenance & minor renewals.	85%	4 Sept.

5611

Sheet 3

E. J. M. de. Nagor

RAILWAY CONSTRUCTION CONTRACT WORK UNDER CONTROL OF
ALLIED COMMISSION

State of Work as at 31 July 45

LINE 245

Job No.	Agency	Location	Description	Size	Compl.	Est'd Compl.	Remarks
AG/245/1001	Contract G. Muratori Metauro	Monsampolo	Repairs to Bridge at 13.30 Km.	Rebuild one pier & 4 brick arches each of 15 mt. span.	90%	10 Aug.	4 Piers compl 1 Pier compl 2 Spandrel w
AG/245/1002	Contract G. Muratori Metauro	Spinetoli Colli	Repairs to Bridge at 17.27 Km.	Rebuild 3 brick arches 1/8 mt. span & 2/4 mt. spans.	195%	10 Aug.	Parapet wa to complete
AG/245/1003	E.S.R.	P. Ascoli to Offida- Castel di LAME	Track repairs.	20.50 Km. of track maintain- ce & minor renewals.	33%	10 Aug.	
AG/245/1004	Contract G. Muratori Metauro	Spinetoli Colli	Repairs to Bridge at 18.53 Km.	Rebuild 1 brick arch of 10 mt. span	85%	10 Aug.	Arch and walls comp
AG/245/1005	Contract G. Muratori Metauro	Offida	Repairs to Bridge at 20.15 Km.	Rebuild 3 brick arch spans each of 15 mt.	30%	10 Aug.	3 Arches completed
AG/245/1006	Contract G. Muratori Metauro	Offida	Repairs to Bridge at 22.28 Km.	Build central pier & provide steel super- structure (E.S.R.)	75%	10 Aug.	Pier com Awaiting

RAILWAY CONSTRUCTION CONTRACT WORK UNDER CONTROL OF
APPLIED COMMISSION

State of Work as at 31 July 45

Sheet 1

Agency	Location	Description	Size	% Compl.	Est'd Compln.	Remarks.
Contract Muratori Sauro	Monsampolo	Repairs to Bridge	Rebuild one pier & 4 brick arches each of 115 mt. span.	90%	10 Aug.	4 Piers completed 1 Pier completed 2 Spandrel walls completed
Contract Muratori Sauro	Spinetoli Colli	Repairs to Bridge	Rebuild 3 brick arches 1/8 mt. span & 2/4 mt. spans.	95%	10 Aug.	Parapet walls only to complete.
S.R.	F. Ascoli to Offida- Castel di Tenne	Track repairs.	20.60 Km. of track maintenance & minor renewals.	35%	10 Aug.	
Contract Muratori Sauro	Spinetoli Colli	Repairs to Bridge	Rebuild 1 brick arch arch of 10 mt. span	85%	10 Aug.	Arch and spandrel walls completed.
Contract Muratori Sauro	Offida	Repairs to Bridge	Rebuild 3 brick arch spans each of 15 mt.	30%	10 Aug.	3 Arches 40% completed
Contract Muratori Sauro	Offida	Repairs to Bridge	Build central pier & provide steel super- structure. (R.S.J.S.)	75%	10 Aug.	Pier completed Awaiting steelwork. .../to Sheet 2

Statement of Work as at 31 July 45

Job No.	Agency	Location	Description	Size	% Compl.	Est'd Compl.	Remarks
AC/245/1007	Contract C. Muratori Metauro	Ascoli	Repairs to Bridge at 25.11 Km.	Build 3 piers & provide steel superstructure (R.S.J/s/)	75%	10 Aug.	Pier con- struction
AC/245/1008	I.B.R.	Offida Castel di Lama to Ascoli	Track repairs.	11.5 Km. track maintenance & minor renewals.	40%	10 Aug.	

6195

EP

1476

Statement of Work as at 31 July 45

Sheet 2

Agency	Location	Description	Size	% Compl.	Est'd Compl.	Remarks.
Contract Munatori Maurice	Ascoli	Repairs to Bridge at 25.11 Km.	Build 3 piers & provide steel superstructure (R.S.J/s/)	75%	10 Aug.	Piers completed Awaiting steelwork
I.S.E.	Offida Mastel di Mara to Ascoli	Track repairs.	11.97 Km. track maintenance & minor renewals.	40%	10 Aug.	

EGD

RAILWAY CONSTRUCTION CONTRACT WORK UNDER OF
ALLIED COMMISSION

State of Work as at 31 July 1945

LINE 242

Job No.	Agency	Location	Description	Size	% Compl.	Est'd Compln.	
AC/242/1001	I.S.R.	Civitanova to Torrovalle	Track repairs.	12.7 Km. track maintenance & minor renewals.	60%	12 Aug.	
AC/242/1002	Contract C. Muratori Metauro	Torrovalle	Repairs to Bridge at 12.55 Km.	Rebuild abutment & provide steel superstructure	95%	12 Aug.	Re du ring slat
AC/242/1003	I. S.R.	Torrovalle to Macerata	Track repairs.	14.47 Km. track maintenance & minor renewals.	55%	12 Aug.	
AC/242/1004	Contract C. Muratori Metauro	Macerata	Repairs to Bridge at 26.35 Km.	Rebuild 7 piers & 8 brick arches each of 13 mt. span.	35%	12 Aug.	4 P. 1 Ar Cent all
AC/242/1005	Contract C. Muratori Metauro	Macerata	Repairs to tunnel at 27.8 Km.	Rebuild 12 mt. length of brick barral.	80%	12 Aug.	
AC/242/1006	I.S.R.	Macerata to Tolentino	Track repairs.	18.52 Km. track maintenance & minor renewals.	40%	12 Aug.	
01							
02							
03							
04							

RAILWAY CONSTRUCTION CONTRACT WORK UNDER OF
ALLIED COMMISSION

State of Work as at 31 July 1945

Sheet 1

Agency	Location	Description	Size	% Compl	Est'd Compln	Remarks.
001 I.S.R.	Civitanova to Morrovalle	Track repairs.	12.71 Km. track maintenance & minor renewals.	60%	12 Aug.	
002 Contract C. Muratori Metauro	Morrovalle	Repairs to Bridge at 12.55 Km.	Rebuild abutment & provide steel superstructure	95%	12 Aug.	Re designed with reinforced concrete deck slab.
003 I. S.R.	Morrovalle to Macerata	Track repairs.	14.47 Km. track maintenance & minor renewals.	55%	12 Aug.	
004 Contract C. Muratori Metauro	Macerata	Repairs to Bridge at 26.35 Km.	Rebuild 7 piers & 8 brick arches each of 13 mt. span.	35%	12 Aug.	4 Piers completed 1 Arch completed Centering erected for all remaining arches.
005 Contract C. Muratori Metauro	Macerata	Repairs to tunnel at 27.8 Km.	Rebuild 12 mt. length of brick barrel.	80%	12 Aug.	
006 I.S.R.	Macerata to Tolentino	Track repairs.	18.52 Km. track maintenance & minor renewals.	40%	12 Aug.	
						 /to Sheet 2

1479

State of Work as at 31 July 1945

LINE 242

Job No.	Agency	Location	Description	Size	% Compl.	Est'd Compl.	Remarks
AC/242/1007	Contract Imp. Puccini	Pollenza	Repairs to Bridge at 48.85 Km.	Rebuild to brick arches each of 10 mt. span.	10%	12 Aug.	1 Pie con 1 Arch con
AC/242/1008	Contract Imp. Puccini	S. Severino	Repairs to Bridge at 57.28 Km.	Rebuild 1 brick arch of 17 mt. span.	10%	12 Aug.	Centering
AC/242/1009	Contract Imp. Puccini	S. Severino	Repairs to Bridge at 57.28 Km.	Rebuild abutments & provide steel superstructure.	75%	12 Aug.	Abutment Awaiting
AC/242/1010	Contract Imp. Puccini	Castel- Raimondo	Repairs to Bridge at 58.11 Km.	Rebuild 1 brick arch of 8 mt. span.	5%	12 Aug.	Road on rail rebuilding Works behind this delay Demolition
AC/242/1011	I.C.R.	Tolentino to Castel- Raimondo	Track repairs.	21.54 Km. track maintenance.	65%	12 Aug.	
AC/242/1012	Contract Imp. Puccini	Castel- Raimondo	Repairs to Bridge at 58.59 Km.	Rebuild 1 brick arch of 8 mt. span.	10%	12 Aug.	Centering
AC/242/1013	Contract Imp. Puccini	Cerreto d'Esp.	Repairs to Bridge at 80.78 Km.	Rebuild 1 brick arch of 72 mt. span.	25%	12 Aug.	Centering and arch

State of Work as at 31 July 1945

Sheet 2

Agency	Location	Description	Size	Est'd Compl	Compln.	Remarks.
Contract Imp. Puccini	Polkessa	Repairs to Bridge at 43.85 Km.	Rebuild to brick arches each of 10 mt. span.	10%	12 Aug.	1 Pier completed 1 Arch centering erected
Contract Imp. Puccini	Severino	Repairs to Bridge at 54.98 Km.	Rebuild : brick work of 17 mt. span.	10%	12 Aug.	Centering erected
Contract Imp. Puccini	Severino	Repairs to Bridge at 57.28 Km.	Rebuild abutments & provide steel superstructure.	75%	12 Aug.	Abutments completed Awaiting steelwork.
Contract Imp. Puccini	Castel- Alaino	Repairs to Bridge at 68.11 Km.	Rebuild : brick arch of 8 mt. span.	5%	12 Aug.	Road on railway bank. Ing. Gile rebuilding 3 km of new road. Work behind contract time thus delaying bridge construction Demolition completed.
I. A.	Polentino to Castel- Alaino	Track repairs. 21.54 Km. track maintenance.		65%	12 Aug.	
Contract Imp. Puccini	Castel- Alaino	Repairs to Bridge at 68.99 Km.	Rebuild : brick arch of 8 mt. span.	10%	12 Aug.	Centering erected
Contract Imp. Puccini	Cerreto di Bari	Repairs to Bridge at 80.78 Km.	Rebuild : brick arch of 7 mt. span.	25%	12 Aug.	Centering erected and arch 50% completed

...../to Sheet 3

State of Work as at 31 July 1945LINE 242

Job No.	Agency	Location	Description	Size	Compl.	Est'd Compl.	
AG/242/1014	Contract Corp. Puccini	Correto d'Ala	Repairs to Bridge at 23.12 Km.	Rebuild 1 brick arch of 15 ft.	10%	12 Aug.	Center
AG/242.1015	Contract Corp. Puccini	Albacina	Repairs to Bridge at 25.04 Km.	Rebuild 1 brick arch of 15 ft. span.	20%	12 Aug.	Center Arch
AG/242/1016	L. B. B. Castel-	Albiondo to Albacina	Track repairs.	15.47 Km. track maintenance & minor renewals.	20%	12 Aug.	

5606

State of Work as at 31 July 1945

Sheet 3

Agency	Location	Description	Size	Compl.	Est'd Compln.	Remarks
014 Contract Imp. Tuncoini	Gerrato d'Assi	Repairs to Bridge	Rebuild 1 brick arch of 10 mt.	10%	12 Aug.	Centering erected
015 Contract Imp. Puccini	Alkamin	Repairs to Bridge	Rebuild 1 brick arch of 15 mt. span.	20%	12 Aug.	Centering erected Arch 25% completed
016	P. J. M. Castel- Lombardo to Labbacini	Track repairs.	13.47 Km. track maintenance & timber renewals.	20%	12 Aug.	

E917

RAILWAY CONSTRUCTION CONTRACT WORK UNDER CONTROL OF
ALLIED COMMISSION

LINE 246

State of work as at 31 July 1945

Job No.	Agency	Location	Description	Size	Est'd Compl.	Est'd Compl.	Re
AC/246/1001	I.T.R.	Giulianova to Bellante Ripattone	Track repairs.	13.6 Km. track maintenance & minor renewals.	50%	10 Aug.	
AC/246/1002	Contract Imp. Puccini	Bellante Ripattone	Repairs to Bridge at 12.55 Km.	Rebuild 1 brick arch of 15 mt. span.	85%	10 Aug.	Arch a compl
AC/246/1003	Contract Imp. Puccini	Bellante Ripattone	Repairs to Bridge at 12.55 Km.	Rebuild abutments & provide steel superstructure of 4 mt. span. (R.3.3:3.)	80%	10 Aug.	Abutments A wait of st
AC/246/1004	Contract Imp. Puccini	Bellante Ripattone	Repairs to Bridge at 13.69 Km.	Rebuild 1 pier & 2 brick arches each of 12 mt. span.	85%	10 Aug.	Arch compl
AC/246/1005	Contract Imp. Puccini	Castellalto	Repairs to Bridge at 19.12 Km.	Rebuild 4 piers & 5 brick arches each 5.45 mt. span.	65%	10 Aug.	4 Piers 3 Arches Centre 1 Sp
							

RAILWAY CONSTRUCTION CONTRACT WORK UNDER CONTROL OF
ARMED COMMISSION

Sheet 1

State of Work as at 31 July 1945

Agency	Location	Description	Size	Est'd Compl. Compl.	Remarks
I.S.R.	Giulianova to Bellante Ripattone	Track repairs.	11.5 Km. track maintenance & minor renewals.	50% 10 Aug.	
Contract Imp. Puccini	Bellante Ripattone	Repairs to Bridge	Rebuild 1 brick arch of 13 mt. span.	85% 10 Aug.	Arch and spandrel completed
Contract Imp. Puccini	Bellante Ripattone	Repairs to Bridge at 12.55 Km.	Rebuild abutments & provide steel superstructure of 4 mt. span. (R.S.J.s.)	80% 10 Aug.	Abutments completed Awaiting supply of steel.
Contract Imp. Puccini	Bellante Ripattone	Repairs to Bridge at 11.59 Km.	Rebuild 2 pier & 2 brick arches each of 12 mt. span.	85% 10 Aug.	Arches and spandrels completed
Contract Imp. Puccini	Castellalto	Repairs to Bridge at 19.12 Km.	Rebuild 4 pier & 5 brick arches each 8.45 mt. span.	65% 10 Aug.	4 Piers completed 3 Arches completed Centering erected for 1 arch 1 Spandrel completed

.../to Sheet 2

State of Work at 31 July 1945

LINE 246

Job No.	Agency	Location	Description	Size	% Compl	Est'd Compl	Remarks
AG/246/1006	Contract Imp. Puccini	Teramo	Repairs to Bridge 1st 23.67 Km.	Rebuild 1 pier & 15 brick arches each of 20 mt. span.	40%	10 Aug.	1 Pier compl 1 Arch compl Centering for Night work
AG/246/1107	I.S.H.	Bellante Ripattone to Teramo	Track repairs.	11.47 Km. of track maintenance & minor renewals.	50%		

5604

State of Work at 31 July 1945

Sheet 2

Agency	Location	Description	Size	% Compl	Est'd Compl	Remarks
Contract Imp. Muccini	Teramo	Repairs to Bridge at 23.67 Km.	Rebuild 1 pier & 15 brick arches each of 20 mt. span.	40%	10 Aug.	1 Pier completed 1 Arch completed Centering for 2 arches erected Night work now commenced.
I.S.R.	Bellante Napoli to Teramo	Track repairs.	11.47 Km. of track maintenance & minor renewals.	50%		

Egd

RAILWAY CONSTRUCTION CONTRACT WORK UNDER CONTROL OF
ALLIED COMMISSION

LINE 246

State of Work as at 30 June 1945

Job No.	Agency	Location	Description	Size	% Compl.	Est'd Compln.	
AO/246/1001	I.S.R.	Giulianova to Bellante Ripattonne	Track repairs.	13.61 Km. track maintenance & minor renewals.	Nil	10 Aug.	
AO/246/1002	Contract Imp. Puccini	Bellante Ripattonne	Repairs to Bridge at 11.61 Km.	Rebuild 1 brick arch of 15 mt. span.	5%	10 Aug.	Demolition in hand. Ce prepared a Bricks 5 ce
AO/246/1003	Contract Imp. Puccini	Bellante Ripattonne	Repairs to Bridge at 12.55 Km.	Rebuild abutments & provide steel superstructure of 4 mt. span. (R.S.J.s.)	5%	10 Aug.	Demolition and site hand. Bricks a
AO/246/1004	Contract Imp. Puccini	Bellante Ripattonne	Repairs to Bridge at 13.69 Km.	Rebuild 1 pier & 2 brick arches each of 12 mt. span.	10%	10 Aug.	Demolition and site centering at site Bricks and
AO/246/1005	Contract Imp. Puccini	Castellalto	Repairs to Bridge at 19.12 Km.	Rebuild 4 piers & 5 brick arches each 8.45 mt. span.	5%	10 Aug.	Demolition and site centering at site Bricks a
							

RAILWAY CONSTRUCTION CONTRACT WORK UNDER CONTROL OF
ALLIED COMMISSION

State of Work as at 30 June 1945

Sheet 1

Agency	Location	Description	Size	% Compl.	Est'd Compln.	Remarks.
I.S.R.	Giulianova to Bellante Ripattone	Track repairs.	13.61 Km. track maintenance & minor renewals.	Nil	16 Aug.	
Contract Imp. Puccini	Bellante Ripattone	Repairs to Bridge at 11.61 Km.	Rebuild 1 brick arch of 15 mt. span.	5%	10 Aug.	Demolition 50% complete in hand. Centering being prepared at site. Bricks & cement on site.
Contract Imp. Puccini	Bellante Ripattone	Repairs to Bridge at 12.55 Km.	Rebuild abutments & provide steel superstructure of 4 mt. span. (R.S.J.s.)	5%	10 Aug.	Demolition 50% complete and site clearance in hand. Bricks and cement on site.
Contract Imp. Puccini	Bellante Ripattone	Repairs to Bridge at 13.69 Km.	Rebuild 1 pier & 2 brick arches each of 12 mt. span.	10%	10 Aug.	Demolition 50% complete and site clearance in hand. Centering being prepared at site and 1 pier form shed. Bricks and cement on site.
Contract Imp. Puccini	Castellalto	Repairs to Bridge at 19.12 Km.	Rebuild 4 piers & 5 brick arches each 8.45 mt. span.	5%	10 Aug.	Demolition 50% complete and site clearance in hand. Centering being prepared at site. Bricks and cement on site.

...../to sheet 2

State of Work as at 30 June 1945.

৯৩৬৮

State of work as at 30 June 1945.

Sheet 2

Agency	Location	Description	Size	Compl.	Est'd Compln.	Remarks.
61 Contract Imp. Puccini	Teramo	Repairs to Bridge at 23.67 Km.	Rebuild 1 pier & 15 brick arches each of 20 mt. span.	6%	10 Aug	Demolition 60% complete and site clearance in hand. Preparing centering at site. Bricks and cement on site.
7 I.S.A.	Bellante Ripattone to Teramo	Track repairs.	11.47 Km. of track maintenance & minor renewals.	Nil	10 Aug	

LINE 245

RAILWAY CONSTRUCTION CONTRACT WORK UNDER CONTROL OF
ALLIED COMMISSION

State of work as at 30 June 1945

Job No.	Agency	Location	Description	Size	Compl.	Settled	
14/245/1001	Contract C. Muratori Metauro	Longham- solo	Repairs to Bridge at 13.80 Km.	Rebuild one pier & 4 brick arches each of 15 mt. span	3 %	10 Aug.	Demolition centering site for Cement
14/245/1002	Contract C. Muratori Metauro	Spinetoli velli	Repairs to Bridge at 17.27 Km.	Rebuild 3 brick arches 1/8 mt. span & 2/4 mt. spans.	8 %	10 Aug.	Demolition centering erected Cement
14/245/1003	I.S.A.	Spinetoli to Offida- Castel di Lama.	Track repairs.	20.60 Km. of track maintain- ce & minor repairs.	Nil	10 Aug.	
14/245/1004	Contract C. Muratori Metauro	Spinetoli velli	Repairs to Bridge at 18.53 Km.	Rebuild 1 brick arch of 10 mt.	9 %	10 Aug.	Demolition centering at site. Cement
14/245/1005	Contract C. Muratori Metauro	Offida	Repairs to Bridge at 20.15 Km.	Rebuild 3 brick arch spans each of 15 mt.	2 %	10 Aug.	Demolition Cement
14/245/1006	Contract C. Muratori Metauro	Offida	Repairs to Bridge at 22.28 Km.	Build central pier & provide steel super- structure (R.S.J.s.)	10 %	10 Aug.	Demolition

CT

S

C.

P.

...../

RAILWAY CONSTRUCTION CONTRACT WORK UNDER CONTROL OF
ALLIED COMMISSION

Sheet 1

State of work as at 30 June 1949

Agency	Location	Description	Size	Compl.	Est'd. Compl'd.	Remarks
Contract Muratori Meteuro	Consum- Solo	Repairs to Bridge at 13.30 Km.	Rebuild one pier & 4 brick arches each of 15 mt. span	3 %	10 Aug.	Demolition 20% complete. Centering being prepared at site for one arch. Cement on site.
Contract Muratori Meteuro	Spinatoli Velli	Repairs to Bridge at 17.27 Km.	Rebuild 3 brick arches 1/8 mt. span & 2/4 mt. spans.	8 %	10 Aug.	Demolition 70% complete. Centering for two arches erected and 50% complete. Cement on site.
I.S.R.	Spinatoli to Offida- vestel di Lama.	Track repairs.	20.66 Km. of track maintain- ce & minor renewals.	Nil	10 Aug.	
Contract Muratori Meteuro	Spinatoli Velli	Repairs to Bridge at 18.53 Km.	Rebuild 1 brick arch of 10 mt.	9 %	10 Aug.	Demolition 80% complete. Centering being prepared at site. Cement on site.
Contract Muratori Meteuro	Offida	Repairs to Bridge at 20.15 Km.	Rebuild 3 brick arch spans each of 15 mt.	2 %	10 Aug.	Demolition 20% complete. Cement at site.
Contract Muratori Meteuro	Offida	Repairs to Bridge at 22.28 Km.	Build central pier & provide steel super- structure (I.S.J's.)	10 %	10 Aug.	Demolition completed.

.....to sheet 2

State of Work as at 30 June 1945

Job No.	Agency	Location	Description	Size	% Compl.	Est'd Compln.	Remarks
AC/245/1007	Contract S. Muratovi Metaxuro	Ascoli	Repairs to Bridge at 25.11 Km.	Build 3 piers & provide steel superstructure (R.S.J's.)	3 %	10 Aug.	Demolition
AC/245/1008	I.B.R.	Offida- Castel di Lama to Ascoli	Track repairs.	11.98 Km. track maintenance & minor renewals.	Nil	10 Aug.	

Sheet 2

Agency	Location	Description	Size	% Compl.	Est'd Compl.	Remarks
Contract Muratori Sauro	Ascoli	Repairs to Bridge at 25.11 Km.	Build 3 piers & provide steel superstructure (R.S.J's.)	3 %	10 Aug.	Demolition of piers completed
I.S.R.	Offida- Castel di Lama to Ascoli	Track repairs.	11.98 Km. track maintenance & minor renewals.	Nil	10 Aug.	

RAILWAY CONSTRUCTION CONTRACT WORK UNDER OF
ALLIED COMMISSION

State of work as at 30 June 1945

LINE 242

Job No.	Agency	Location	Description	Size	Est'd Compl.	Compl.	Re
AC/242/1001	I.S.R.	Civitanova to Morrovalle	Track repairs.	12.71 Km. track maintenance & minor renewals.	Nil	12 Aug.	
AC/242/1002	Contract C. Muratori Metauro	Morrovalle	Repairs to Bridge at 12.55 Km.	Rebuild abutments & provide steel superstructure.	Nil	12 Aug.	
AC/242/1003	I.S.R.	Morrovalle to Macerata	Track repairs.	14.47 Km. track maintenance & minor renewals.	Nil	12 Aug.	
AC/242/1004	Contract C. Muratori Metauro	Macerata	Repairs to Bridge at 26.35 Km.	Rebuild 7 piers & 8 brick arches each of 13 mt. span.	6%	12 Aug.	Rebuild Centre Cement
AC/242/1005	Contract C. Muratori Metauro	Macerata	Repairs to tunnel at 27.81 Km.	Rebuild 12 mt. length of brick barrel.	3%	12 Aug.	Rebuild Centre Cement
AC/242/1006	I.S.R.	Macerata to Tolentino	Track repairs.	18.52 Km. track maintenance & minor renewals.	Nil	12 Aug.	

RAILWAY CONSTRUCTION CONTRACT WORK UNDER OF
ALLIED COMMISSION

State of work as at 30 June 1945

Sheet 1

Agency	Location	Description	Size	Compl.	Est'd compl.	Remarks.
I.S.R.	Civitavecchia to Murolo	Track repairs.	12.71 Km. track maintenance & minor renewals.	Nil	12 Aug.	
Contract C. Muratori Metauro	Murolo	Repairs to Bridge at 12.55 Km.	Rebuild abutments & provide steel superstructure.	Nil	12 Aug.	
I.S.R.	Murolo to Macerata	Track repairs.	14.47 Km. track maintenance & minor renewals.	Nil	12 Aug.	
Contract C. Muratori Metauro	Macerata	Repairs to Bridge at 26.35 Km.	Rebuild 7 piers & 8 brick arches each of 13 mt. span.	6%	12 Aug.	Demolition 30% completed Centering being prepared Cement on site.
Contract C. Muratori Metauro	Macerata	Repairs to tunnel at 27.81 Km.	Rebuild 12 mt. length of brick barrel.	3%	12 Aug.	Demolition 50% completed Cement on site.
I.S.R.	Macerata to Tolentino	Track repairs.	18.52 Km. track maintenance & minor renewals.	Nil	12 Aug.	

...../to sheet 2

LINE 242

State of Work as at 30 June 1945

JOB No.	Agency	Location	Description	Size	% Compl.	Est'd Compln.	Re
AO/242/1007	Contract Imp. Puccini	Pollenza	Repairs to Bridge at 40.86 Km.	Rebuild 15 brick arches each of 10 mt. span.	4%	12 Aug.	Demolition Cement
AO/242/1008	Contract Imp. Puccini	S. Severino	Repairs to Bridge at 56.08 Km.	Rebuild 1 brick arch of 17 mt. span.	2%	12 Aug.	Demolition Centering at site Cement
AO/242/1009	Contract Imp. Puccini	S. Severino	Repairs to Bridge at 57.28 Km.	Rebuild abut- ments & provide steel super- structure.	5%	12 Aug.	Demolition Cement
AO/242/1010	Contract Imp. Puccini	Castel- Raimondo	Repairs to Bridge at 68.11 Km.	Rebuild 1 brick arch of 8 mt. span.	4%	12 Aug.	Demolition
AO/242/1011	I.S.R.	Tolentino to Castel- Raimondo	Track repairs.	21.54 Km. track maintenance.	Nil	12 Aug.	
AO/242/1012	Contract Imp. Puccini	Castel- Raimondo	Repairs to Bridge at 68.59 Km.	Rebuild 1 brick arch of 8 mt. span.	4%	12 Aug.	Demolition

Sheet 2

State of Work as at 30 June 1945

Agency	Location	Description	Size	Compl.	Est'd Compln.	Remarks.
Contract Imp. Puccini	Pollenza	Repairs to Bridge at 40.85 Km.	Rebuild 12 brick arches each of 10 mt. span.	4%	12 Aug.	Demolition 90% complete. Cement on site.
Contract Imp. Puccini	S. Severino	Repairs to Bridge at 56.03 Km.	Rebuild 1 brick arch of 17 mt. span.	2%	12 Aug.	Demolition 40% completed. Centering being prepared at site. Cement on site.
Contract Imp. Puccini	S. Severino	Repairs to Bridge at 57.28 Km.	Rebuild abutments & provide steel superstructure.	5%	12 Aug.	Demolition completed. Cement on site.
Contract Imp. Puccini	Castel-Raimondo	Repairs to Bridge at 68.11 Km.	Rebuild 1 brick arch of 8 mt. span.	4%	12 Aug.	Demolition 90% completed.
I.S.R.	Tolentino to Castel-Raimondo	Track repairs.	21.54 Km. track maintenance.	Nil	12 Aug.	
Contract Imp. Puccini	Castel-Raimondo	Repairs to Bridge at 68.59 Km.	Rebuild 1 brick arch of 8 mt. span.	4%	12 Aug.	Demolition 90% completed.

...../to sheet 3

LINE 242

State of Work as at 30 June 1945

Job No.	Agency	Location	Description	Size	Est'd Compl.	Est'd Compln.	Re
AC/242/1013	Contract Imp. Puccini	Correto d'Assi	Repairs to Bridge at 80.78 Km.	Rebuild 1 brick arch of 7 mt. span.	Nil	12 Aug.	Work not yet
AC/242/1014	Contract Imp. Puccini	Correto d'Assi	Repairs to Bridge at 83.12 Km.	Rebuild 1 brick arch of 10 mt.	Nil	12 Aug.	Work only
AC/242/1015	Contract Imp. Puccini	Albacina	Repairs to Bridge at 86.04 Km.	Rebuild 1 brick arch of 15. mt. span.	2%	12 Aug.	Demolition
AC/242/1016	I.S.R.	Castell Raimondo to Albacina	Track repairs. Maintenance & minor renewals.	19.47 Km. track	Nil	12 Aug.	

5509

State of Work as at 30 June 1945

Sheet 3

Agency	Location	Description	Size	% Compl.	Est'd Compln.	Remarks.
13 Contract Imp. Puccini	Cerreto d'Assi	Repairs to Bridge	Rebuild 1 brick arch of 7 mt. span.	Nil	12 Aug.	Work not yet commenced.
14 Contract Imp. Puccini	Cerreto d'Assi	Repairs to Bridge	Rebuild 1 brick arch of 10 mt. span.	Nil	12 Aug.	Work only just started.
15 Contract Imp. Puccini	Albacina	Repairs to Bridge	Rebuild 1 brick arch of 15 mt. span.	2%	12 Aug.	Demolition 40% complete.
16 I.E.R.	Castell Rimondo to Albacina	Track repairs.	119.47 Km. track maintenance & minor renewals.	Nil	12 Aug.	

1501

1501
