Declassified E.O. 12356 Section 3.3/NND No. 785019

ACC 078/L-U/9/PWU

10000/150/260
(VOL. 1)

MISCELLA
LAZIO - U
SEPT. 194

Declassified E.O. 12356 Section 3.3/NND No. 785019

10000/150/260
(VOL. 1)

MISCELLANEOUS PROJECTS,
LAZIO - UMBRIA
SEPT. 1944 - FEB. 1945

MISCELLANEOUS PROJECTS: LAZIO-UMBRIA

9 NOV 44

10 FEB 45

Vol 7

Declassified E.O. 12356 Section 3.3/NND No. 785019

Vol 7

10000 / 150/260

THIS FOLDER
CONTAINS PAPERS
FROM SEPT 44
TO FEB - 45
CATALOGUE.

078/L-U/3/PWU

Declassified E.O. 12356 Section 3.3/NND No. 785019

MINISTERO DELLE CORPORAZIONI

DIREZIONE GENERALE DELL'INDUSTRIA

UFFICIO STUDI E RICERCHE

BOLLETTINO SETTIMANALE

DEI PREZZI E DEI CAMBI

Declassified E.O. 12356 Section 3.3/NND No. 785019

BOLLETTINO SETTIMANALE

DEI PREZZI E DEI CAMBI

Roma, _____

G. SACCONE - ROMA

Declassified E.O. 12356 Section 3.3/NND No. 785019

No	Date	Ref	From	Subject
	Reg Engr L-V	R4/Engr/120	15-11-44	Projects held at Ministry of P.W
34	" " "	R4/Engr/400	22-11-44	Mine clearance and various P.W.Bs
	" " "	" " "	16-11-44	" " " " " "
	" " "	" " "	16-11-44	List of 300 projects approved in principal
35	" " "	R4/Engr/11(c)1	11-12-44	Works Stopped for lack of funds
36	Reg Engr L-V	R4/Engr/11E	30-12-44	Urgent Works to be done at Francisna
	P.W.D. Works Secretary (RC)	1700	4-12-44	" " " " " "
37	Min. of P.W	No 738	17.1.45	Registration of discovered of bodies of Soldiers
38	" "	No 739		" " " "
39	" "	No 740	17.1.45	" " " "
40	Commr of Rems	1180	24.1.45	List of Projects approved during Dec. 1944.
41	Reg Engr L V	R4/ENG/11(4)	10.2.45	Civil Surveying Harbours

Declassified E.O. 12356 Section 3.3/NND No. 785019

N°	Date	Reference	From	Subject
1	9-11-44	1783	P.W.M.Thec.D.	War damages.Repair Istituto Re.Elena
2	9-11-44	1780	" " " " "	War damages.Repair namery and kitchen of Istituto Fisioterapico Reg.Elena
3	9-11-44	1781	" " " " "	War damage Repair of Ist.Fisioterapico Regina Elena.
4	9-11-44	883/1782	" " " " "	War damage repair of Ist.di Ortopedio of R.University.
5	10-11-44	11865/11853	Minist.Inter.	Raising of craft of Fiumicino
6	30-10-44	R4/Eng/A400	Reg.Eng.L-U	Works projects inaction on projects in Italian Government Ter.
				Rome University
7	16-11-44	078/L-U/9		Repairs and salvage.Civitavecchia Harbor
8	18-11-44	"		Prevention of accidents.
9	24-11-44	23A	HQ. RAAC	Repairs of sewers in Ostiense street
10	11-11-44	Proj.n°.114	Reg.Eng.L-U	250 m. of right quay in Fiumicino Harbor
11	13-11-44	" 121	" " "	Repair of sewers in Prenestina and Ett.Fieramosca street.
12	2-11-44	" 116	" " "	Sewer collector in Rome
13	19-11-44	" 106	" " "	Sewer collector in Rome.
14	19-11-44	" 105	" " "	Repair of South mole of Fiumicino
15	21-10-44	" 118	" " "	Cleaning of Tiber river bed between V.Emanuele & Mazzini bridges.
16	20-10-44	" 107	" " "	Repair of sewer in Via Matteucci and Via Benzoni.
17	5-10-44	" 73	" " "	Repair of sewer in Via Nomentana ,Pola G.Fea and G.B.Rossi streets
18	4-10-44	" 72	" " "	Polyclinic Umberto I°.
19	5-10-44	" 87	" " "	Repair of north mole of Fiumicino
20	5-10-44	" 90	" " "	Repair of sewers in G.da Empoli, Piaz.Biffi, Circ.Ostiense.
21	5-10-44	" 74	" " "	Repair of sewers via Massaia & Lazagna
22	4-10-44	" 70	" " "	Repair of sewer collector Marranella via Baldassare e Villa Narducci
23	4-10-44	" 67		Repair of sewer in via Casilina and

Declassified E.O. 12356 Section 3.3/NND No. 785019

8	18-11-44	"			Repairs and salvage.Civitavecchia Harbor
9	24-11-44	23A		HQ. RAAC	Prevention of accidents.
10	11-11-44	Proj.n°.	114	Reg.Eng.I-U	Repairs of sewers in Ostiense street
11	13-11-44	"	121	" " "	250 m. of right quay in Fiumicino Harbor
12	2-11-44	"	116	" " "	Repair of sewers in Prenestina and Ett.Fieramosca street.
13	19-11-44	"	106	" " "	Sewer collector in Rome
14	19-11-44	"	105	" " "	Sewer collector in Rome.
15	21-10-44	"	118	" " "	Repair of South mole of Fiumicino
16	20-10-44	"	107	" " "	Cleaning of Tiber river bed between V.Emanuele & Mazzini bridges.
17	5-10-44	"	73	" " "	Repair of sewer in Via Matteucci and Via Benzoni.
18	4-10-44	"	72	" " "	Repair of sewer in Via Nomentana ,Pola G.Fea and G.B.Rossi streets
19	5-10-44	"	87	" " "	Polyclinic Umberto I°.
20	5-10-44	"	90	" " "	Repair of north mole of Fiumicino
21	5-10-44	"	74	" " "	Repair of sewers in G.da Empoli, Piaz.Biffi, Circ.Ostiense.
22	4-10-44	"	70	" " "	Repair of sewers via Massaia & Lazagna
23	4-10-44	"	67	" " "	Repair of sewer collector Marranella via Baldassare e Villa Narducci
24	4-10-44	"	66	" " "	Repair of sewer in via Casilina and Acqua Bulicante.
25	17-10-44	"	86	" " "	Bridge over Azzone-Bocca road.MR597746
26	5-10-44	"	75	" " "	R.University Rome-Literature Bldg.
27	5-10-44	"	76	" " "	" " " " Phisiology Istitute.
28	11-10-44	"	88	" " "	Polyclinic Umberto I°.Repair of Bldgs.
29	18- 9-44	"	64	" " "	University Rome- Hygiene Institute.
30	15-9- 44	"	62	" " "	" " " .Orthopedic Chimic
31				" " "	Statictical summary Month October 44
32				" " "	" " " " " "
33	14-11-44	"		D.Solomon	Repairs Rome University.

Declassified E.O. 12356 Section 3.3/NND No. 785019

Declassified E.O. 12356 Section 3.3/NND No. 785019

COPY

HEADQUARTERS
ALLIED MILITARY GOVERNMENT
LAZIO UMBRIA REGION
(Engineering Division)
APO 394

File

10 February 1945

SUBJECT: Civitavecchia Harbour

TO : Regional Engineer Lazio Umbria Region AMG.

41

IN REPLY QUOTE: R4/ENG/11(°)1

An interim report on progress is submitted for information.

1. Additional Equipment which has arrived since my report of 31st Jan.45 is as follows:-

2 Additional dumpers making six in all now working

1 Pile driving attachment for 19 R.B. Crane

2 Compressors complete but with no pipes or tools to work with.

1 10 Ton Roller

2. The R.E. Ship Progress arrived on Friday 9th Jan.

3. The most important items of stores which has not yet been delivered are the 10 sets of Burning gear. The work is definitely being held up now for this equipment. Capt.Leishman of 861 Mech Equip has just returned from Naples and reports that they are on their way.

4. The R.E. Ship has on board two sets of burning gear which will come into use now they are going to lend us some pipes and tools for the compressors until the others arrive.

../..

1799

Declassified E.O. 12356 Section 3.3/NND No. 785019

The ta[illegible]s required of the O.C. "Progr[illegible]" are considered by him to be rather big but be is endeavouring to make a way to evercome difficulties some-how.

The first work given to this ship are

(i) Raising block at Sardinia quay

(ii) Removing mangled cranes from Bichieri wharf

(iii) Raising sunken pontoon crane.

5. The progress of work in general is good but could be speeded up with more men and more transport and plant. At a big meeting of Genio Civile Chiefs on 8th Feb. instructions were issued to Sig.Bucalossi to ensure that this was done. The provision of transport however is not within his power as the decision lies with his superiors regarding to employment of Italian truck from Rome at what is considered too high a tariff.

In my opinion in a week or so there will not be enough transport to keep the face shovel, grabs and concrete work going at the speed required without any four trucks working full time on the construction. At the moment Local trucks are carrying stone but they are withdrawn for port shipment when required. The dumpers at the moment are doing the greatest quantity of work and once a face shovel starts with compressors more trucks will be needed.

6. The roller has been working for a week and has nearly completed the road and loading area at "Tarquinia Port" sidings.

7. Timber platforms on ships are held up for the burning gear.

8. Quay removal and clearance progressing, rather alowly at present, but I think it will speed up in a day or two after the recent orders of Genio Civile for more men.

(sgd). Major R.A.
Port Construction Officer

Copy to:
Regional Engineer
P.W. & U.
Tn. A.C.
Major Goldson
2 File.

1798

Declassified E.O. 12356 Section 3.3/NND No. 785019

COMUNE
Governatorato di Roma
Ripartizione V

N. di Protocollo 1180
Risposta al N. 259 del 10-9-44
Allegati N. I elenco

Roma, lì 04 GEN 1945 19 anno

Oggetto: Elenco dei progetti approvati durante il mese di Dicembre 944

Al MINISTERO DEI LAVORI PUBBLICI
Direzione Generale dei Servizi Tecnici
ROMA

RECEIVED
P.W. & U. S/C A.C.
24 FEB 1945 078

L-U/9

40

e per conoscenza

ALL'UFFICIALE REGIONALE ALLEATO DEI SS.TT.
DELLA PROVINCIA DI
ROMA

Con riferimente alla nota sopra indicata, si trasmette l'elenco dei progetti approvati durante il mese di Dicembre 1944.

IL DIRETTORE DEI SS.TT.
(Ing.A.Maccari)

Dr Col Thompson
R.E. 26/2

1797

C O M U N E D I R O M A

RIPARTIZIONE V^ - SERVIZI AMMINISTRATIVI

ELENCO DEI PROGETTI APPROVATI DURANTE IL MESE DI DICEMBRE 1944

N.	Natura dei lavori	Località e tipo dei lavori	Impresa	Importo L.
1	Rimozione di terre e materiali.	Trasporto ai pubblici scarichi di terre e materiali ingombranti alcune vie del quartiere Nomentano	Sparaco Spartaco	336.000.=
2	Rimozione di terre e materiali	Trasporto ai pubblici scarichi di terre e materiali ingombranti alcune vie del quartiere Tiburtino	Soc.An.Coop."Serenità e Lavoro"	402.000.=
3	Lavori di riparazione	Rettifica sponde fosso di Centocelle a valle della V.Prenestina	Martella Achille	88.000.=
4	Lavori di riparazione	Rettifica sponde fosso di Centocelle a valle della V.Prenestina	Martella Achille	88.000.=
5	Lavori di riparazione	Rettifica sponde fosso di Centocelle a valle della Via Prenestina	Martella Achille	88.000.=
6	Lavori di riparazione	Riparazione Lungotevere Flaminio (lotto III)	Federici Elia	440.000.=
7	Lavori di riparazione	Riparazione Lungotevere Flaminio (lotto II)	Federici Elia	480.000.=

Declassified E.O. 12356 Section 3.3/NND No. 785019

1	Rimozione di terre e materiali.	Trasporto ai pubblici scarichi di terre e materiali ingombranti alcune vie del quartiere Nomentano		Sparaco Spartaco	336.000.=
2	Rimozione di terre e materiali	Trasporto ai pubblici scarichi di terre e materiali ingombranti alcune vie del quartiere Tiburtino		Soc.An.Coop."Serenità e Lavoro"	402.000.=
3	Laveri di riparazione	Rettifica spende fosse di Centocelle a valle della V.Prenestina		Martella Achille	33.000.=
4	Laveri di riparazione	Rettifica sponde fosso di Centocelle a valle della V.Prenestina		Martella Achille	33.000.=
5	Laveri di riparazione	Rettifica sponde fosso di Centocelle a valle della Via Prenestina		Martella Achille	33.000.=
6	Laveri di riparazione	Riparazione Lungotevere Flaminio (lotto III)		Federici Elia	440.000.=
7	Laveri di riparazione	Riparazione Lungotevere Flaminio (lotto II)		Federici Elia	480.000.=

1796

Declassified E.O. 12356 Section 3.3/NND No. 785019

Declassified E.O. 12356 Section 3.3/NND No. 785019

Translator U.Aguarone 1-19-45

Rome, 17 Jan. 1945

To the Ministry of War

Rome

MINISTRY OF PUBLIC WORK
Direction General
Technical Services.
No. 740

Subject: Cassino - First Aid Station

Frequent accidents are occuring during the work of clearing zeoris which are now being carried out in the town and Abbey of Montecassino, owing to mines difficult to locate because of the presence of other metallic materials.

It is therefore urgently necessary to provide for a first Aid Station which should operate when ever men are at work. This (F.W.) Ministry will furnish the space requi reajor this installation.

Personnel, (a doctor and assistant) could be supplied by the office of Director General of Military health (and also the necessary first aid supplies.

This matter is very urgent. We beg the Ministry to accede to this request and to ask the afore-said Director General (Mil.health) to speed the necessary measures; this F.W Ministry will instruct the Chief Eng. of Genio Civile (Frosinone) as to the necessary space requires.

1795

THE MINISTER
Ruini

COPIA

RECEIVED
P.W. & U. S/C A.C.
19 JAN 1945 078

Roma, 17 GEN. 1945 194

MINISTERO DEI LAVORI PUBBLICI

Dir.Gen.dei Serv.Tecnici

Prot. N. 740 Div.

Allegati N.

Risposta al foglio del

Div. Sez. N.

Al Ministero della Guerra
Gabinetto
ROMA

noted d.f.j. 19/1
Per note & file

OGGETTO

Cassino - Posto di pronto soccorso.

Nei lavori di sgombero di macerie che vengono eseguiti nell'abitato di Montecassino e nell'Abbazia di Montecassino si verificano spesso infortuni dovuti alla presenza di mine di difficile individuazione a causa della presenza di altri materiali metallici.

Necessita pertanto di istituire di urgenza a Cassino un posto di pronto soccorso, che dovrebbe funzionare nei giorni di lavoro degli operai. Il locale per l'impianto sarebbe fornito da questo Ministero.

Il personale (un medico-chirurgo ed un infermiere) potrebbe essere colà distaccato dalla Direzione Generale della Sanità Militare, con il materiale occorrente per il pronto soccorso e per le prime medicazioni.

Il provvedimento è della massima urgenza.

Si prega codesto Ministero di aderire alla richiesta e di in-

Declassified E.O. 12356 Section 3.3/NND No. 785019

Allegati N. .....

Risposta al foglio del .....

Div. ..... *Sez.* ..... *N.* .....

Noted Col. Thompson
Asst Col Thompson
Pls note & file

OGGETTO

Cassino - Posto di pronto soccorso.

Nei lavori di sgombero di macerie che vengono eseguiti nell'abitato di Montecassino e nell'Abbazia di Montecassino si verificano spesso infortuni dovuti alla presenza di mine di difficile individuazione a causa della presenza di altri materiali metallici.

Necessita pertanto di istituire di urgenza a Cassino un posto di pronto soccorso, che dovrebbe funzionare nei giorni di lavoro degli operai. Il locale per l'impianto sarebbe fornito da questo Ministero.

Il personale (un medico-chirurgo ed un infermiere) potrebbe essere colà distaccato dalla Direzione Generale della Sanità Militare, con il materiale occorrente per il pronto soccorso e per le prime medicazioni.

Il provvedimento è della massima urgenza.

Si prega codesto Ministero di aderire alla richiesta e di interessare la predetta Direzione Generale ad adottare con tutta sollecitudine i provvedimenti necessari prendendo accordi con questo Ministero che avrà cura di dare le opportune istruzioni all'Ingegnere Capo del Genio Civile di Frosinone.

1794

I L M I N I S T R O

fto RUINI

Declassified E.O. 12356 Section 3.3/NND No. 785019

Declassified E.O. 12356 Section 3.3/NND No. 785019

Translater U.Aquarone 19-1-45

MINISTRY OF PUBLIC WORK
Direction General
Technical Services
Pr.N.759

Rome, - - - 1945
to the Ministry of Interior
Gabinetto - ROMA
and for information of
His Grace the Abbot of Montecas=sino
MONTECASSINO
To the Chief Eng. of Genio Civile
of FROSINONE

Subject: Installation of guard posts at Cassino and Montecassino.

The Allied Commission informs us that a great number of robberies are occurring, especially during night time in the ruins of Cassino and those of the Abbey of Montecassino! The Allied Commission urges us to provide guard posts in these two locations.

We are informing the proper Ministry of this request so that measures may be taken.

For the space necessary for the guards, arrange=ments should be made between the Frosinone Genio Civile and His Grace the Abbot of Montecassino

THE MINISTER
Ruini

1793

COPIA

RECEIVED
P.W. & U. S/C A.C.
19 JAN 1945
078

MINISTERO
DEI
LAVORI PUBBLICI

Direzione Generale Servizi Tecnici

Roma, 194

Al Ministero dell'Interno
Gabinetto ROMA
e per conoscenza:
All'Ecc.il Rev.mo ABBATE di MONTECASSINO
All'Ingegnere Capo del Genio Civile di FROSINONE

Prot. N. 439 *Div.*
Allegati N.
Risposta al foglio del
Div. *Sez.* *N.*

Lt Col Thompson

Pervenuto a fine Dic 1944

OGGETTO
Impianto di posti di guardia a Cassino ed a Montecassino.

Viene segnalato dalla Commissione Alleata che si verifica gran numero di furti, specie nelle ore notturne, tra le macerie di Cassino e dell'Abbazia di Montecassino. La stessa Commissione sollecita l'impianto di speciali posti di guardia nelle due località.

Si segnala tale richiesta a codesto Ministero per i provvedimenti di competenza, e si avverte che per il locale occorrente a Cassino potranno essere presi accordi rispettivamente con il Genio Civile di Frosinone e con l'Ecc. il Rev.mo Abbate di Montecassino.

IL MINISTRO
fto RUINI

Declassified E.O. 12356 Section 3.3/NND No. 785019

All'Ingegnere Capo del Genio Civile
di MONTECASSINO
TROSINONE

Prot. N. 439 Div.
Allegati N.
Risposta al foglio del
Div. Sez. N.

OGGETTO
Impianto di posti di guardia a Cassino ed a Montecassino.

Lt Col Thompson
Presente e file
Maggio 1944

Viene segnalato dalla Commissione Alleata che si verifica gran numero di furti, specie nelle ore notturne, tra le macerie di Cassino e dell'Abbazia di Montecassino. La stessa Commissione sollecita l'impianto di speciali posti di guardia nelle due località.

Si segnala tale richiesta a codesto Ministero per i provvedimenti di competenza, e si avverte che per il locale occorrente a Cassino potranno essere presi accordi rispettivamente con il Genio Civile di Frosinone e con l'Ecc. il Rev.mo Abbate di Montecassino.

IL MINISTRO
fto RUINI

1792

Declassified E.O. 12356 Section 3.3/NND No. 785019

Declassified E.O. 12356 Section 3.3/NND No. 785019

Translater C.Aquarone 1-19-45

MINISTRY OF PUBLIC WORK
Direction General
Technical Services.
N.158

Rome, 17 Jan. 1945

To the Chief Eng. of Genio Civile
FROSINONE

and for information of:
The Compartment's Inspector Gen.
of Genio Civile
ROME

37

Subject: Cassino and Montecassino - Danger of mines during clearing work.

The Allied Commission informs us that in removing the debris at Cassino and Montecassino, no precautions are being taken to find out and make harmless the mines which are amiast the debris. Your Office is requested to send at once the proper number of expert workmen there. Your Office are to be very careful in such places where metal beams or oth other iron material could impede your research.

If you will refer to the Circular N. 144 of 5 January you will find that your Office can arrange with the Military Engineers Center at S. Martino del Cimino for expert assistance in all matters of mine removal, to improve the methods of research and avoid accidents.

The Minister
Ruini

1791

COPIA

RECEIVED
P.W. & U. S/C A.C
19 JAN 1945

Roma, 17 [illegible] 194

MINISTERO DEI LAVORI PUBBLICI

Dir.Gen.dei Servizi Tecnici

Prot. N. 738 Div. .....
Allegati N. .....
Risposta al foglio del .....
Div. ..... Sez. ..... N. .....

OGGETTO
Cassino e Montecassino - Pericolo delle mine nei lavori di sgombro.

Al l'Ingegnere Capo del Genio Civile FROSINONE
e per conoscenza:
All'Ispettore Generale Compartimentale del Genio Civile ROMA

Lt Col Thompson
Passato a fatto
Roma 19/1

La Commissione Alleata segnala che nei lavori di sgombro a Cassino ed a Montecassino non si adotterebbe alcuna cautela per ricercare e rendere innocue le mine che si trovano fra le macerie. S'invita codesto Ufficio a inviare subito sopraluogo un numero adeguato di operai specializzati e si avverte che dovrà porsi la più grande attenzione in quei posti nei quali la presenza di travi o altro materiale di ferro potesse ostacolare le ricerche.

Con riferimento alla circolare in data 5 gennaio corr. n.144, codesto Ufficio, ove ne avesse bisogno, potrebbe prendere accordi col segnalato centro di addestramento istituito dal Genio Militare a S.Martino del Cimino, sia per gli specialisti e sia per i sistemi più adatti per rendere più sicure le ricerche e per evitare comunque infortuni.

Declassified E.O. 12356 Section 3.3/NND No. 785019

Div. _____

Allegati N. _____

Risposta al foglio del _____

Div. _____ Sez. _____ N. _____

Lt Col Thompson
Permit to fly
Rag 191

OGGETTO

Cassino e Montecassino - Pericolo delle mine nei lavori di sgombro.

La Commissione Alleata segnala che nei lavori di sgombro a Cassino ed a Montecassino non si adotterebbe alcuna cautela per ricercare e rendere innocue le mine che si trovano fra le macerie. S'invita codesto Ufficio a inviare subito sopraluogo un numero adeguato di operai specializzati e si avverte che dovrà porsi la più grande attenzione in quei posti nei quali la presenza di travi o altro materiale di ferro potesse ostacolare le ricerche.

Con riferimento alla circolare in data 5 gennaio corr. n.144, codesto Ufficio, ove ne avesse bisogno, potrebbe prendere accordi col segnalato centro di addestramento istituito dal Genio Militare a S.Martino del Cimino, sia per gli specialisti e sia per i sistemi più adatti per rendere più sicure le ricerche e per evitare comunque infortuni.

IL MINISTRO
fto RUINI

1799

Declassified E.O. 12356 Section 3.3/NND No. 785019

Declassified E.O. 12356 Section 3.3/NND No. 785019

G.de CEF/gb
47659

HEADQUARTERS
ALLIED MILITARY GOVERNMENT
LAZIO UMBRIA REGION
(Engineering Division)
AFO ~~394~~

30 December 1944

RECEIVED
P.W. & U. S/C A.C.
3 JAN 1945
078

TO : H.Q. A.C. (P.W.)
H.Q. Region Lazio & Umbria

SUBJECT : Urgent work to be done at Fiumicino.

IN REPLY QUOTE : R4/ENG/11E

Reference PWRC/1500/700 dated 4th Dec. attached.

1. For information - A very clear and able statement of the problem. I have inspected the site and agree.

2. This covers all points raised in my R4/ENG/11(a) dated 18 Nov. except:

(a) Possibility of relief spill-way further up river.
(b) Debris of bridge on Tiber Proper below junction.
(c) Extra Equipment from Navy Sub-Commission - This was promised by them about 10th Dec. and we were asked to stop demolition and did.
Result NOTHING arrived.

Lt.Col.R.E.
Regional Engineer
Lazio Umbria Region AMG.

Enclosure: 1
Copy to:
P.W.(R C)
Lt.Col. Bolick

Lt Col Thompson
I believe this comes under the heading of Port work or River Control. Sapl review.
3/1

1789

HEADQUARTERS
ALLIED MILITARY GOVERNMENT
LAZIO- UMBRIA REGION
(Engineering Division)
APO 394

ASS/dpe

710.AG(Fm)

P.W. (E.C.)/1500/700

Rome, 4 December, 1944

Subject: Urgent work to be done at Fiumicino.

To : Genio Civile of Tevere and Agro Romano.

1. The recent flood of the Tiber on 28 to 30 November reached a peak of 11.80 m. on the Rome guage (at Ripetta) about 1800 hr. on 29 (wed.) November. This would exceed by 0.40 m. the flood stage reached on 3 November. Both of these floods seriously flooded Fiumicino. The records in the Hydrographic office show 12 floods during the last 21 years in which the peak guage reading exceeded 13 meters. Ten of these floods occured previous to straightening the Tiber below Rome which was done in August 1940 and two of them occured in 1941. The straightening of the Tiber below Rome hasn't been completed for sufficient years to establish a relationship between known guage heights and effect on height of water in the navigation canal. There can be no doubt that same increases the flood situation at Fiumicino.

2. The writer viewed the course of the flood on the 29th. and 30th. of November. Several hours before a peak level was reached in the navigation canal, water was observed passing thru sand boils under the levee or thru direct breaks in the quay at 12 different points, (some of which were poorly sand bagged and some without protection) and at additional points such as street storm water drains (which were sand bagged) and the public urinals. Due to the blowing of the canal face of the quay at 15 to 20 foot intervals, the brick wall of the quay on the town side is fractured both horizontally and vertically and small streams of water were pouring into the Town at hundreds of places. This is due to the fact that the quay is formed by rock fill and depended on the mortar laid brick wall facing the town for the water tight element between the river and the Town. At no place did water reach the top of the original level of the unbroken part of the quay.

3. It is my opinion that the flood depth in Fiumicino was increased due to the part of the highway swing bridge and the two tankers that are still in the navigation canal. Also that the Town would have been flooded even with all obstructions completely removed from the

Declassified E.O. 12356 Section 3.3/NND No. 785019

1. The recent flood of the Tiber on 28 to 30 November reached a peak of 11.80 m. on the Rome gauge (at Ripetta) about 1800 hr. on 29 (wed.) November. This would exceed by 0.40 m. the flood stage reached on 3 November. Both of these floods seriously flooded Fiumicino. The records in the Hydrographic office show 12 floods during the last 21 years in which the peak guage reading exceeded 13 meters. Ten of these floods occured previous to straightening the Tiber below Rome which was done in August 1940 and two of them occured in 1941. The straightening of the Tiber below Rome hasn't been completed for sufficient years to establish a relationship between known guage heights and effect on height of water in the navigation canal. There can be no doubt that same increases the flood situation at Fiumicino.

2. The writer viewed the course of the flood on the 29th. and 30th. of November. Several hours before a peak level was reached in the navigation canal, water was observed passing thru sand boils under the levee or thru direct breaks in the quay at 12 different points, (some of which were poorly sand bagged and some without protection) and at additional points such as street storm water drains (which were sand bagged) and the public urinals. Due to the blowing of the canal face of the quay at 15 to 20 foot intervals, the brick wall of the quay on the Town side is fractured both horizontally and vertically and small streams of water were pouring into the Town at hundreds of places. This is due to the fact that the quay is formed by rock fill and depended on the mortar laid brick wall facing the town for the water tight element between the river and the Town. At no place did water reach the top of the original level of the unbroken part of the quay.

3. It is my opinion that the flood depth in Fiumicino was increased due to the part of the highway swing bridge and the two tankers that are still in the navigation canal. Also that the Town would have been flooded even with all obstructions completely removed from the navigation canal due to the open breaks in the quay and the lesser leaks at hundreds of other places. However temporary repair or closing

1783

Declassified E.O. 12356 Section 3.3/NND No. 785019

of the breaks in the quay would considerably lessen the damage.

4. Boat barrage between the moles. Considerable of the upper portions of the boat barrage between the moles near the outlet of the canal have been removed by use of over a half ton of explosive since the flood of 3rd. of November. What is left of the boat barrage had little effect on the height of water farther up the canal. Great restriction to the outlet of the canal (between the moles) is caused by the piling of both moles being displaced by mines into the stream area of the canal and all the concrete deck and supporting superstructure of a short stretch of the moles is lying in the water way. The water way has been so restricted at this point that at the time viewed (noon of 30th. Nov.) it was estimated there was a 30 cm. drop in the water surface in passing this restriction. A high velocity existed from the restriction and thru the resulting rapids down stream for a distance of about 100 feet. The remainder of the boat barrage is at the foot of these rapids.

5. a) Agreement with Compagnia Marittima for Restoration of Fiumicino Harbor for Navigation was entered into under date of 30 June. Previous to this both Allied and Italian naval authorities had been consulted and these authorities advised they were not interested in the clearance of this port as it was not of an immediate military character. Further that no equipment would be available for this purpose because of the immediate need for such equipment at Civitavecchia and shortly at Livorno and the lesser ports in that area which were of military importance.

b) The present working agreement was entered into because it permitted early action, did not require controlled materials and does not exceed 1,000,000 lire in cost to A.M.G. The latter condition was essential in order to avoid the long delay entailed in getting a project thru the different approving agencies whether, the Minister of Public Works or A.M.G. were to finance the work. All the available equipment of several firms was combined for operating administration under Compagnia Marittima. At the time the clearing of the port was deemed urgent for the transporting of supplies for Rome Region.

Declassified E.O. 12356 Section 3.3/NND No. 785019

4. Boat barrage between the moles. Considerable of the upper por-
tions of the boat barrage between the moles near the outlet of the ca-
nal have been removed by use of over a half ton of explosive since the
flood of 3rd. of November. What is left of the boat barrage had little
effect on the height of water farther up the canal. Great restriction
to the outlet of the canal (between the moles) is caused by the piling
of both moles being displaced by mines into the stream area of the
canal and all the concrete deck and supporting superstructure of a
short stretch of the moles is lying in the water way. The water way has
been so restricted at this point that at the time viewed (noon of 30th.
Nov.) it was estimated there was a 30 cm. drop in the water surface in
passing this restriction. A high velocity existed from the restriction
and thru the resulting rapids down stream for a distance of about 100
feet. The remainder of the boat barrage is at the foot of these rapids.

5. a) Agreement with Compagnia Marittima for Restoration of Piu-
micino Harbor for Navigation was entered into under date of 30 June.
Previous to this both Allied and Italian naval authorities had been con-
tacted and these authorities advised they were not interested in the
clearance of this port as it was not of an immediate military character.
Further that no equipment would be available for this purpose because
of the immediate need for such equipment at Civitavecchia and shor
at Livorno and the lesser ports in that area which were of military
importance.

b) The present working agreement was entered into because it
permitted early action, did not require controlled materials and does
not exceed 1,000,000 lire in cost to A.M.G. The latter condition was
essential in order to avoid the long delay entailed in getting a pro-
ject thru the different approving agencies whether, the Minister of
Public Works or A.M.G. were to finance the work. All the available
equipment of several firms was combined for operating administration
under Compagnia Marittima. At the time the clearing of the port was
deemed urgent for the transporting of supplies for Rome Region.

c) Unfortunately in early August, emphasis was changed from
clearing the boat barrage obstructing the channel near the outlet to
raising the fishing craft for economic and fishing reasons. This policy
emanated from H.Q.-A.C. thru the Regional Commissioner. At or about
the same time a conference was held of the heads of coal, economic,
food supply, transportation, electricity (movement of coal supply for

1787

Declassified E.O. 12356 Section 3.3/NND No. 785019

Rome plant involved) and other interested Sections, on the different levels of authority as A.A.I., A.F.H.Q., A.C., Rome Region and it was decided that the port at Fiumicino was of no interest to the above groups. The change of emphasis was unfortunate in that the only favorable weather for removing the barrage at the outlet is during the months of July, August and some times the first half of September.

d) You have asked for interpretation of the working agreement with Compagnia Marittima. The principal idea was the removal of the existing wreckage to restore the port for navigation for the use of Rome Region in transporting supplies. The company doing the work was acting as a private enterprise for salvage and as such was free to deal directly with the interested parties. It was not the thought to preclude the Company from negotiating with the proper authorities for the removal of such items as the ship barrage and the swing bridge. The actual condition of the barrage, what would be salvageable and what not salvageable was not known at the time the agreement was entered into. By the same token it was not the idea to only destroy craft that were unfit for future use but also to remove same. It is admitted it is not the type of agreement that either the then Regional Engineer or myself considered fully sufficient to cover a lot of unknown factors but seemed the most expedient considering the urgency, the private character of the ships involved, questions of jurisdiction of Allied and Italian Naval authorities and the equipment available.

6. Urgent work needed to be done by your office at once:

a) Complete negotiations for removal of swing bridge, boat barrage and two unsalvageable tankers.

b) Take emergency steps to have all piling, concrete deck and supporting superstructure of both moles, removed wherever same projects into the orginal water way. This material can be placed on the sea side of the moles for the purpose of reinforcement. This should be done to remove the present outlet restriction and to eliminate hazard to navigation and should be done whether the moles are rebuilt or not.

Some thought will have to be given as to the future alignment of piling for the reconstruction of the destroyed part of the quay. If on present alignment and the existing piling are cut off [illegible] level instead of

Declassified E.O. 12356 Section 3.3/NND No. 785019

levels of authority as A.A.I., A.F.H.Q., A.C., Rome Region and it was decided that the port at Fiumicino was of no interest to the above groups. The change of emphasis was unfortunate in that the only favorable weather for removing the barrage at the outlet is during the months of July, August and some times the first half of September.

d) You have asked for interpretation of the working agreement with Compagnie Maritima. The principal idea was the removal of the existing wreckage to restore the port for navigation for the use of Rome Region in transporting supplies. The company doing the work was acting as a private enterprise for salvage and as such was free to deal directly with the interested parties. It was not the thought to preclude the Company from negotiating with the proper authorities for the removal of such items as the ship barrage and the swing bridge. The actual condition of the barrage, what would be salvageable and what not salvageable was not known at the time the agreement was entered into. By the same token it was not the idea to only destroy craft that were unfit for future use but also to remove same. It is admitted it is not the type of agreement that either the then Regional Engineer or myself considered fully sufficient to cover a lot of unknown factors but seemed the most expedient considering the urgency, the private character of the ships involved, questions of jurisdiction of Allied and Italian Naval authorities and the equipment available.

5. Urgent work needed to be done by your office at once:

a) Complete negotiations for removal of swing bridge, boat barrage and two unsalvageable tankers.

b) Take emergency steps to have all piling, concrete deck and supporting superstructure of both moles, removed wherever same projects into the orginal water way. This material can be placed on the sea side of the moles for the purpose of reinforcement. This should be done to remove the present outlet restriction and to eliminate hazard to navigation and should be done whether the moles are rebuilt or not.

Some thought will have to be given as to the future alignment of piling for the reconstruction of the destroyed part of the quay. If on present alignment and the existing piling are cut off below water level instead of removed, considerable difficulty will be experienced in placing a new line of piling in the future.

Note: Although fishing schooners have been coming in and out of the harbor for some time the first coal boat (50 m. x 8 m. draft 2.40 m.) loaded with 233 tons of charcoal docked at Fiumicino today (Dec. 4).

1786

Declassified E.O. 12356 Section 3.3/NND No. 785019

e) Take emergency steps to build a temporary dike or protection at some six major breaks in the right quay. Some leakage thru the dike near the overhead conveyor, in the east end of the low area of the coal yard and three points around the coal company buildings should be permanently repaired as they are not tied in with the quay or salvage work in any way.

d) Take temporary steps to more effectively close the openings for the ferry, storm water drains and public urinals against flood water. Although most of these places were sand bagged, none of them were very effective in preventing water from entering the Town.

e) Project situation. Projects 60,61,90,116,121,133 and 134 were approved by this office, the first as early as 9th. of September, for a total of 33,770,000 L. An immediate check should be made of their status in order to determine the ultimate funds available and plan immediate prosecution of the work accordingly. I am convinced from a survey of this last flood that permanent relief from flooding of the Town will not be attained until the Town face of the right quay wall has been rebuilt wherever same has been damaged by mines.

f) Complete soundings requested some time ago, along right and left quays and moles and thru center line of canal, bar in front of mole, closer soundings below, over and upstream at ship barrage, the two largest tankers and the draw bridge to determine present status of bed and any changed conditions from soundings taken last July.

7. The following suggestions are made in considering final plans for repair to quays and moles:

a) Due to some increase in intensity of flood due to straightening the fiber below Rome, study should be given to whether there is sufficient water way between the moles. If same is not considered sufficient would it be advisable to place the reconstructed part only of the right mole outside the present damaged mole, removing all of the latter? Later if the outlet portion is reconstructed the alignment could be made to coincide with the work to be done at this time.

b) Consideration should also be given to the possible need of a flood spillway being left at the upstream end of

Declassified E.O. 12356 Section 3.3/NND No. 785019

[illegible] protection
[illegible] surveyor, in the east end of the low area of the coal [illegible] tube leakage thru the dike
and three points around the coal company buildings should be per-
manently repaired as they are not tied in with the quay or salvage work
in any way.

d) Take temporary steps to more effectively close the opening for the ferry, storm water drains and public urinals against flood water. Although most of these places were sand bagged, none of them were very effective in preventing water from entering the Town.

e) Project situation. Projects 60,61,80,116,121,133 and 134 were approved by this office, the first as early as 9th. of September, for a total of 33,770,000 L. An immediate check should be made of their status in order to determine the ultimate funds available and plan immediate prosecution of the work accordingly. I am convinced from a survey of this last flood that permanent relief from flooding of the Town will not be attained until the Town face of the right quay wall has been rebuilt wherever same has been damaged by mines.

f) Complete soundings requested some time ago; along right and left quays and moles and thru center line of canal, bar in front of mole, closer soundings below, over and upstream at ship barrage, the two largest tankers and the draw bridge to determine present status of bed and any changed conditions from soundings taken last July.

7. The following suggestions are made in considering final plans for repair to quays and moles:

a) Due to some increase in intensity of flood due to straightening the Tiber below Rome, study should be given to whether there is sufficient water way between the moles. If same is not considered sufficient would it be advisable to place the reconstructed part only of the right mole outside the present damaged mole, removing all of the latter? Later if the outlet portion is reconstructed the alignment could be made to coincide with the work to be done at this time.

b) Consideration should also be given to the possible need of a flood spillway being left at the point of the present break in the quay where same joins the mole. This might be sufficient for flood purposes if lengthened over present opening. Same might be constructed by spacing the large concrete blocks with sufficient water way between and placing

1785

Declassified E.O. 12356 Section 3.3/NND No. 785019

a concrete deck over the whole. In either case the water way between the moles should be kept sufficiently narrowed so that this tract of the channel is kept free from silting.

e) Consideration should be given to raising the right quay 12" to 16" in height on reconstruction.

d) Consideration should be given to a back water flood gate on all outlets such as street storm water inlets, public urinals and sewers. If same are used it will be necessary to set them into the face of the quay to prevent being damaged by boats passing or anchored along quay. It might be more effective to reconstruct the catch basins so that they can be effectively blocked during high water periods and valve off the sewer outlets.

8x Inaction of all parties concerned may have been partially the cause of flooding in the past. It will take several months to reconstruct the right quay. Items 6 a to 6 f are emergency items that need to be done and quick action on the part of your office will lessen or possibly eliminate a future flooding of Fiumicino.

A.M. Michel

A.M. MICHEL, Major, C.E.
Fn. Works & Water Sec.-Rome Comune

HQ AC(PW) ✓
NB Regt L.O.

Declassified E.O. 12356 Section 3.3/NND No. 785019

c) Consideration should be given to raising the right quay 12" to 16" in height on reconstruction.

d) Consideration should be given to a back water flood gate on all outlets such as street storm water inlets, public urinals and sewers. If some are used it will be necessary to set them into the face of the quay to prevent being damaged by boats passing or anchored along quay. It might be more effective to reconstruct the catch basins so that they can be effectively blocked during high water periods and valve off the sewer outlets.

8. Inaction of all parties concerned may have been partially the cause of flooding in the past. It will take several months to reconstruct the right quay. Items 6 a to 6 f are emergency items that need to be done and quick action on the part of your office will lessen or possibly eliminate a future flooding of Piumicino.

A.E. MICHEL, Major, C.E.
In. Works & Water Sec.-Rome Commune

HQ AC(PW) ✓
MTO Region No 2

1) For information - a very clear and able statement of the problem as I have suggested it to C and agree.

2) Also covers all points raised in my Rep[ort] [illegible] except:
(a) Possibility of [illegible] further up river
(b) Debris of bridge on Tiber Project. Colonel [illegible] of Exec Engineer from Navy Sub-commission has the [illegible] and did — Result NOTHING

Gen Hardy Lewis

1787

Declassified E.O. 12356 Section 3.3/NND No. 785019

Declassified E.O. 12356 Section 3.3/NND No. 785019

G.de CEF/gb

HEADQUARTERS
ALLIED MILITARY GOVERNMENT
LAZIO UMBRIA REGION
(Engineering Division)
APO 394

11 December 1944

RECEIVED
P.W. & U S/C A.C.
12 DEC 1944

TO : HQ. AC. P.W. (for personal attention of Director)

SUBJECT : Works stopped.

IN REPLY QUOTE : R4/ENG/17(c)1

Lt Col Thompson
Pls study and bring up at meeting with Minister today Eaf 13/12

I attended the monthly meeting of Capi di Genio Civile at which Director General TIZZANO was present. -

(1) Funds and Projects hold up.

All Capi said NO Funds received and work stopped.

The Director General appeared ignorant of the fact that projects financed from AMG funds never went near him and one of the reasons he gave for projects being held up was that he did not know which projects required AMG funds and which Ministerial funds. - He also stated that the administration side of the Ministry was NOT functioning. -

Each approving letter from this office always states Funds to be obtained from Regional Finance officer or"Funds to be obtained from your Minister"

A complete list of projects held up by Ministero was sent to you at your request in order to follow up some three weeks ago. - This clears the whole position up to date of rendition so far as provinces are concerned. -

To make quite sure that there is no excuse for such ignorance can that list be taken by an officer personally to Ing. TIZZANO and an investigation made into this gross failure by the Ministry - at Ministerial level.

The position has been so bad that Capi have been forced to EMBEZZLE Funds provided for AMG projects.

1783

./.

Declassified E.O. 12356 Section 3.3/NND No. 785019

Full provision has been made for all projects approved from AMG Funds and reimbursement is URGENT or they will be stopped also.-

(2) Materials. All Capi (with part exception of TERNI who are getting some ~~been~~ but insufficient tiles from MARSCIANO) are now held up by lack of Material - particularly roofing.

ACTION.
(a) Representations to Head of Economic Division to immediately release to this Region the whole of the Roofing felt stock and output at Colleferro.
(b) Release the whole of the Corrogated Iron sheets at TERNI for use in this region now not after winter is over.

Both these were reported to Industry AC. H.Q. by Regional Industry some weeks ago and still no apparent action. Both are blocked by A.C.
(c) Expedite transport of Lignite which is available at pit head to Brick and Tile factories.

Capo Frosinone reports that MOROLE and FROSINONE CECCANO Brickworks could produce ½ million tiles if they had 600 tons of Coal.
Regional Industry are fully ~~akin~~ alive to the need and trying to help.
(d) Get agriculture to fell timber and saw mills or pit saws going. - There are pine trees at Ostia LIDO, FRIGENE and UMBERTO Park Rome all beauty or bathing spots and SACRED to the Bathing beauties of ROME City.
There is lots of Hard wood near SABAUDIA in LITTORIA less suitable but in England it has had to be used even green. - Boarding for under roofing felt etc. is unobtainable.
(e) There is very strong information that tiles are being concealed and withheld for sale for private gain by Brickworks and Prefects do NOT appear to be requisitioning tiles from damaged private houses not being repaired. -

---

The likely ~~Load~~ food of such shortage was emphasised in the demand for Materials submitted in May by this Region and again in my Report of 25th August and individual cases as they arose. -

Lt.Col.R.E.
Regional Engineer
Lazio Umbria Region AMG.

pto/

Declassified E.O. 12356 Section 3.3/NND No. 785019

Copy to:

Regional Commissioner Lazio & Umbria (4 copies)
(Attention Ex.Officer provinces)
Office copy only
P.W.(P) to see office copy and initial and follow up with Agriculture & Industry.

G.de CEF/gb

HEADQUARTERS
ALLIED MILITARY GOVERNMENT
LAZIO UMBRIA REGION
(Engineering Division)
APO 394

34

15 November 1944

TO : HQ. Allied Commission Civil Affairs Section (through HQ. L & U Region)

SUBJECT : URGENT PUBLIC WORKS

IN REPLY QUOTE : R4/ENG/120

Your 4/31. A/CA dated 8th November 1944.

1. The information requested is likely to take a month or more to obtain as communication with Communes are slow - Data about Roofless Persons and repairable houses asked for on 13th September has so far only been received from 3 Provinces and two of those incomplete as regards some communes.

It seems desirable to give the overall picture immediately so far as Proforma paras II, IX, X, XII, XIII, XV, XVIII and in part XVI and XVII and VI. -

As I am not aware of any responsibility resting on this Division for item 3 Pregnant ~~matters~~ or the other items.

2. A return of Bridges has already been made under my R4/ENG/A490 dated 11/XI/44 in telephonic request.

3. A complete list of about 300 projects amounting to 700 million lira approved in principal in Italian Government Territory is available in this office and can be seen in this office either in summary or detail all are essential ; all are BLOCKED somewhere at MINISTERIAL LEVEL. -

I suggest as a start that an officer of Devastated Areas should visit this office so, then, generally and accompanied by one of my officers visit the Ministry offices concerned and ascertain where they are reposing and release them and provide the necessary funds to enable them to be put in hand. -

These include some Housing Repair Projects. -

Declassified E.O. 12356 Section 3.3/NND No. 785019

SUBJECT : URGENT PUBLIC WORKS

IN REPLY QUOTE : R4/ENG/120

Your 4/31. A/CA dated 8th November 1944.

1. The information requested is likely to take a month or more to obtain as communication with Communes are slow - Data about Roofless Persons and repairable houses asked for on 13th September has so far only been received from 3 Provinces and two of those incomplete as regards some communes.

It seems desirable to give the overall picture immediately so far as Proforma paras II, IX, X, XII, XIII, XV, XVIII and in part XVI and XVII and VI. -

As I am not aware of any responsibility resting on this Division for item 3 Pregnant ~~matters~~ or the other items.

2. A return of Bridges has already been made under my R4/ENG/A490 dated 11/XI/44 in telephonic request.

3. A complete list of about 300 projects amounting to 700 million lira approved in principal in Italian Government Territory is available in this office and can be seen in this office either in summary or detail all are essential ; all are BLOCKED somewhere at MINISTERIAL LEVEL. -

I suggest as a start that an officer of Devastated Areas should visit this office so, then, generally and accompanied by one of my officers visit the Ministry offices Concerned and ascertain where they are reposing and release them and provide the necessary funds to enable them to be put in hand. -

These include some Housing Repair Projects. -

4. Housing Repairs.

Prior to 11th October projects for repair of Private Houses was definitely blocked by FINANCE. - On 11th October Il Ministro dei Lavori Pubblici issued a letter to Ispettore Generale Compartimentale dell'Ufficio Civile giving limited authority on certain conditions with a limited financial

1783

./.

Declassified E.O. 12356 Section 3.3/NND No. 785019

provision of about £. 80 million.

This is totally inadequate ; a recent return from FROSINONE and LITTORIA provinces estimates that it is technically possible to repair houses sufficient for 38.000 people out of a total of 136.000 roofless people in these provinces.

To do this five main things are necessary.

(a) Government authority to repair every house fit to repair by private or public initiation and definite statement of policy for reimbursement of repairs done by owners so as to free private initiative.

(b) In AMG Territory £. 10.000 per house has been allowed by letter drafted 21 September (released 2nd October), this is something.
Financial Provision.
The average of one large project of £. 14,000.000 is £. 9.000 per head for repairs against £. 60.000 per head for New Houses. 30.000 persons at 9.000 equals 270 million in Frosinone and Littoria. On 15th November financial provision has been made for 405 million in these two provinces.

(c) Staff. This office can deal with our side although extras would help. The Genio Civile Staff is entirely inadequate to deal with preparation or supervision of this and in my opinion require large scale reinforcement.

I have been advising Genio Civile to engage extra staff commencing july 18th, they have tried to obtain but the salaries they are permitted to offer are inadequate to attract or hold suitable men.

This has been fully reported in letters and verbally.

The enclosed copy of letter to Ispettore Generale Comp. del Genio Civile gives my views on this subject. - Time will be required to digest staff but first must be obtained the authority for adequate salaries. -

(d) TRANSPORT
(a) Per Genio Civile Staff MUST be increased.
(b) Transport of Materials will soon reach limit. Extra will be required.

(e) Materials. Much can be done with salvaged material (copy of

Sent Exporting & Agents Pkt X

RH/ENG/17-(c) 1.
21-11-44

Declassified E.O. 12356 Section 3.3/NND No. 785019

To do this five main things are necessary.

(a) Government authority to repair every house fit to repair by private or public initiation and definite statement of policy for reimbursement of repairs done by owners so as to free private initiative.

In AMG Territory £. 10.000 per house has been allowed by letter drafted 21 September (released 2nd October), this is something.

(b) Financial Provision.
The average of one large project of £. 14,000.000 is £. 9.000 per head for repairs against £. 60.000 per head for New Houses. 30.000 persons at 9.000 equals 270 million in Frosinone and Littoria. On 15th November financial provision has been made for 46 million in these two provinces.

(c) Staff. This office can deal with our side although extras would help. The Genio Civile Staff is entirely inadequate to deal with preparation or supervision of this and in my opinion require large scale reinforcement.

I have been advising Genio Civile to engage extra staff commencing july 18th, they have tried to obtain but the salaries they are permitted to offer are inadequate to attract or hold suitable men.

This has been fully reported in letters and verbally.

The enclosed copy of letter to Ispettore Generale Comp. del Genio Civile gives my views on this subject. - Time will be required to digest staff but first must be obtained the authority for adequate salaries. -

Sent separately to AFHQ PW X

RH/ENG/17(c) 1.

21-11-44

(d) TRANSPORT

(a) Per Genio Civile Staff MUST be increased.
(b) Transport of Materials will soon reach limit. Extra will be required.

(e) Materials. Much can be done with salvaged material (many of salvage projects are among those blocked).

Release of coal for Housing Lime and Bricks and Tiles necessary.

Quicking in of the process of releasing Cement and other controlled materials so that they are dealt with daily NOT monthly. -

./.

1787

Declassified E.O. 12356 Section 3.3/NND No. 785019

5. Attached are separate notes on each of the Headings ~~of~~ with which this office deals.

Lt.Col.R.E.
Regional Engineer
Lazio Umbria Region AMG

Enclosures.

Declassified E.O. 12356 Section 3.3/NND No. 785019

Declassified E.O. 12356 Section 3.3/NND No. 785019

RECEIVED
U.S. [illegible] A...
24 NOV 1944

HEADQUARTERS
ALLIED MILITARY GOVERNMENT
LAZIO UMBRIA REGION
(Engineering Division)
APO 394

22nd November 1944

TO : M.G. Region L. & U.
(attention Ex. officer Provinces) (2 copies)

SUBJECT: D E V A S T A T E D A R E A S

IN REPLY QUOTE/ R4/LMG/A4CC

Reference your R 5647 dated 11th November and my R4/LMG/120 dated 15th November.

Herewith the enclosures marked thereon to follow.

Lt.Col.R.E.
Regional Engineer
Lazio Umbria Region AMG

Enclosures:

Copy to:
→ H.Q. A.C. (P.W.)
P.W. (P)
Office 3

By C.C. Thompson

This should be carefully studied as there is no doubt much valuable data within which can be used as a basis for some action.

26/11

Declassified E.O. 12356 Section 3.3/NND No. 785019

DEVASTATED AREA

Summary of Enclosures

Reference R5647 dated 11 November and my R4/ENG/120 dated 15 November.

Item II.IX.X.

Reports so far received in response to letter of 13th September and copy of letter attached have been scheduled and copy of schedule attached : (3)

		Remarks
FROSINONE	Province	(The headings used are slightly different in 2nd column)
LITTORIA	Province	Six Communes missing including FONDI which is extensively destroyed. (arrived 21 and added) The remaining Communes are I think unimportan
VITERBO	Province	VITERBO town which is most damaged in Provinc is omitted.

It should be noted that only damaged towns that could NOT house its population in existing houses making full use of billeting were required by my letter.

These figures can only be regarded as very approximate.

Item XII. BRIDGES already sent in about a week ago attached is a supplementary list of 10 Bridges on STATE Roads (now Military)

Item XIII.

MINES. A general summary of positions given.

Item XV. Separate Notes on (a) Water
(b) Electricity
(c) Sewers
(d) Gas (Nil outside ROME).

Item XVIII.

(a)Work in hand
(b)Local Resources.

Distribution of this and all appendixes

HQ. Region	(2)
HQ.AC. P.W.	(1)
P.W.(P)	1
Office	3.

1777

Item XV (a)

The following towns are still without an adequate supply of water

1. PROVINCE OF LITTORIA

(a) San Mario, SCAURI, CASTELFORTE – MINTURNO) Minefields being cleared and prior to repairs) heavily mined NOT yet repairable.

(b) FORMIA – Ample supply at Street fountains. Preparatory action in hand for reconstruction of headworks destroyed and antiquated

(b) GAETA. – Repairs to damaged Main as far as FORMIA and temporary connection to FORMIA Spring – Work reported well advanced this will provide water at Fountains only.
All this had to be swept for Mines. –
The reservoirs and distribution system have still to be cleared of Mines –
Final scheme being prepared.

(c) ITRI. – Only carted drinking water from FORMIA –
Tanks for reception of this water have been installed.
Main aqueduct badly damaged and inefficient prewar. –
A scheme for Temporary pipe was approved 3rd August but unable to get release of 7 km of piping required.
Alternative scheme using portion of old aqueduct being prepared.

(d) FONDI – Water arriving by gravity to Fountains, Reservoir to be repaired and pumps replaced – Military Pumps were in action until recently ~~they~~ removed –

(e) TERRACINA – Pumps and Reservoir destroyed and also distribution –
Temporary pump has been installed and is supplying water to several Fountains at low level as distribution system is repaired more fountains will be added.
Water to high part of town involves clearing Mines from Reservoir and repair of reservoir, and a new pump –
Later the temporary DIESEL pump on main will require replacement by Electric Pumps when motors and Energy is available.

Declassified E.O. 12356 Section 3.3/NND No. 785019

	CASTELFORTE	heavily mined NOT yet repairable.
(a)	FORMIA	Ample supply at Street fountains. Preparatory action in hand for reconstruction of headworks destroyed and antiquated
(b)	GAETA. -	Repairs to damaged Main as far as FORMIA and temporary connection to FORMIA Spring - Work reported well advanced this will provide water at Fountains only. All this had to be swept for Mines. - The reservoirs and distribution system have still to be cleared of Mines - Final scheme being prepared.
(c)	ITRI.	Only carted drinking water from FORMIA - Tanks for reception of this water have been installed. Main aqueduct badly damaged and inefficient prewar. - A scheme for Temporary pipe was approved 3rd August but unable to get release of 7 km of piping required. Alternative scheme using portion of old aqueduct being prepared.
(d)	FONDI	Water arriving by gravity to fountains, Reservoir to be repaired and pumps replaced - Military Pumps were in action until recently ~~the~~ removed -
(e)	TERRACINA	Pumps and Reservoir destroyed and also distribution - Temporary pump has been installed and is supplying water to several Fountains at low level as distribution system is repaired more fountains will be added. Water to high part of town involves clearing Mines from Reservoir and repair of reservoir, and a new pump - Later the temporary DIESEL pump on main will require replacement by Electric Pumps when motors and Energy is available.

Note.

Electricity for the above is NOT yet available and unlikely to be so far many months - The line from south being mined and completely destroyed. -

./.

1776

Declassified E.O. 12356 Section 3.3/NND No. 785019

Full technical reports were made on all of these with definite recommendations for final solution by Prof. COLOSIMO Prof. of Hydraulics Rome University last July/August passed to Genio Civile definite projects have NOT yet been received.

(f) LITTORIA — Gravity supply to ground floor of houses - Project for Reservoir and pump repair and Water Towers approved in Principal awaiting approval of Italian Ministry and Funds.

(g) APRILIA — Presently local wells -
Pumps destroyed and area reported heavily mined - Civil Contractor recently given task of clearing mines.

2. ROME PROVINCE

(a) ANZIO & NETTUNO — new pumps and Chlorination apparatus installed and and Mains repaired and water at fountains work on distribution system in hand.

(b) CIVITAVECCHIA — One out of 3 mains repaired Genio Civile requested to submit projects for repairs of other two.

(c) OSTIA — Limited supply off ROME Supply -
Pressure Bad, with completion of headworks and improvement of Electricity Supply should improve.

(d) SIMBRIVIO Aquedotto. Supplying 300,000 inhabitants which was completely breached was temporarily repaired and last month the new bridge was finally completed.
All towns served get full supply from Mains.
Work in hand on repairs to distribution system in towns including Velletri.

(e) Towns round LAZIALI HILLS. All have some water but ALBANO and GENZANO the present supply is bad quality -
Work on all these is in hand completion depends on repairs to Motors and arrival of Electric Energy - Progress has been disappointedly slow except for MARINO where main is complete. Other in hand are FRASCATI, GENZANO, ALBANO, GROTTAFERRATA and NEMI, one complete and ROCCA PAPA

Declassified E.O. 12356 Section 3.3/NND No. 785019

(f) LITTORIA — Gravity supply to ground floor of houses - Project for Reservoir and pump repair and Water Towers approved in Principal awaiting approval of Italian Ministry and Funds.

(g) APRILIA — Presently local wells - Pumps destroyed and area reported heavily mined - Civil Contractor recently given task of clearing mines.

2. ROME PROVINCE

(a) ANZIO & NETTUNO — new pumps and Chlorination apparatus installed and and Mains repaired and water at fountains work on distribution system in hand.

(b) CIVITAVECCHIA — One out of 3 mains repaired Genio Civile requested to submit projects for repairs of other two.

(c) OSTIA — Limited supply off ROME Supply - Pressure Bad, with completion of headworks and improvement of Electricity Supply should improve.

(d) SIMBRIVIO Aquaduct. Supplying 300,000 inhabitants which was completely breached was temporarily repaired and last month the new bridge was finally completed. All towns served get full supply from Mains. Work in hand on repairs to distribution systems in towns including Velletri.

(e) Towns round LAZIALI HILLS. All have some water but ALBANO and GENZANO the present supply is bad quality - Work on all these is in hand completion depends on repairs to Motors and arrival of Electric Energy - Progress has been disappointedly slow except for MARINO where main is complete. Other in hand are FRASCATI, GENZANO, ALBANO, GROTTAFERRATA and REMI, one complete and ROCCA PAPA sufficient water for Winter ; requires very high pressure pump before summer.

(f) VALMONTONE — had no water except wells. Work in hand on MAINS.

(g) MONTELL MADONNA. Repairs to main and new pump installed, a second pump is desirable.

(h) LANUVIO — repair project approved .

(i) COLLEFERRO — Pump awaits Electricity.

1775

./.

Declassified E.O. 12356 Section 3.3/NND No. 785019

(j) ARTENA — Pump and repairs meanwhile water in fountain.

(k) TIVOLI — repairs to distribution in hand.

(l) Remaining Towns — all satisfactory - although ROME CITY is still about 95% and until Electric Supply improves will continue to have some troubles, but minor compared with GUSTAV line Area.

3. FROSINONE PROVINCE:

(a) FROSINONE — New pump installed and sufficient supply ; new low level reservoir completed - High level reservoir a long term policy but project prepared but must await improvement in Cement situation - A second pump is desirable - Repairs to distribution in hand -

(b) CEPRANO — main cut over demolished bridge temporarily reconstructed and about end of month when semi-permanent high level bridge is complete should be safe.

(c) S.APPOLINARE-S.GIORGIO main cut on long span bridge - projects for a temporary foot bridge and another bridge awaiting Ministerial approval and Funds.

(d) Following also have been approved by Regional Engineer and await Ministero approval and Financing:
CASSINO, ALVITO, VICALVI, SUPINO, ROCCASECCA.

(e) Other towns satisfactory.

G E N E R A L.

In all these provinces preparation of schemes, supervision of work and consequently progress has been seriously delayed by insufficient staff and insufficient cars to cope with the work - In my opinion if adequate salaries on Allied scale were offered Engineers could be found. -

Genio Civile salaries are grossly low this influences scale of salaries for temporary staff.

This has been fully represented but no result yet.

Declassified E.O. 12356 Section 3.3/NND No. 785019

95% and until Electric Supply improves will continue to have some troubles, but minor compared with GUSTAV line Area.

3. FROSINONE PROVINCE:

(a) FROSINONE — New pump installed and sufficient supply ; new low level reservoir completed - High level reservoir a long term policy but project prepared but must await improvement in Cement situation - A second pump is desirable - Repairs to distribution in hand -

(b) CEPRANO — main cut over demolished bridge temporarily reconstructed and about end of month when semi-permanent high level bridge is complete should be safe.

(c) S.APPOLINARE-S.GIORGIO main cut on long span bridge - projects for a temporary foot bridge and another bridge awaiting Ministerial approval and Funds.

(d) Following also have been approved by Regional Engineer and await Ministero approval and Financing:
CASSINO, ALVITO, VICALVI, SUPINO, ROCCASECCA.

(e) Other towns satisfactory.

G E N E R A L.

In all these provinces preparation of schemes, supervision of work and consequently progress has been seriously delayed by insufficient staff and insufficient cars to cope with the work - In my opinion if adequate salaries on Allied scale were offered Engineers could be found. -

Genio Civile salaries are grossly low this influences scale of salaries for temporary staff.

This has been fully represented but no result yet.

It requires pressing again and again until achieved or money will be thrown away on hastily prepared projects and bad workmanship - It is false economy.

More Cars and tyres are ESSENTIAL.

These things have in my opinion particularly effected ROME and LITTORIA Province who with more staff could have got much of the work completed 2 or 3 months ago. -

FROSINONE Province with the initiative of Maj. Evans and a Capo del Genio Civile heavily overworking got much going earlier but it also suffers seriously from inadequate staff and transport. -

1774

Declassified E.O. 12356 Section 3.3/NND No. 785019

Item XV (b) Electricity.

Available 10.2% of Prewar installed load.

Distribution Lines now in good condition	1912 km
still damaged	1898 km

Of the damaged ones 45 km are now in process of being cleared of mines to enable work to be started and a further list of about 15 long lines awaiting clearance before work can be done these are all listed in priority for action when means permit.

Distribution is now being extended to some pumps nearing repair in LITTORIA Marshes and further repairs of lines will enable Electrically driven Water Pumps to be brought back into use.

There is no Electricity from TERRACINA to GARIGLIANO this used to come from South and the repair of this line which was considered in June is being taken up again apart from Lighting, Mills etc. it effects the Water Supply pumps of 6 towns. -

---

Generally, except in Terracina Garigliano Stretch, repair of distribution is keeping pace with available energy but with increases in Generation expected in December the position may be reversed.

(c) SEWERS, and Demolition and Debris and SALVAGE.

In all devastated towns these are badly damaged - I consider we are most fortunate in getting through the summer without serious epidemics from this cause. -

Some repairs have been done, work is in hand in many cases damage cannot be got at until debris has been removed. -

The standard in most demolished towns at present is, "if the limited amount of water available to put in disappears without visible flooding, then alright" - as more water for flushing is available and debris removed more points for repair will be found over along period of time.

Declassified E.O. 12356 Section 3.3/NND No. 785019

means permit.

Distribution is now being extended to some pumps nearing repair in LITTORIA Marshes and further repairs of lines will enable Electrically driven Water Pumps to be brought back into use.

There is no Electricity from TERRACINA to GARIGLIANO this used to come from South and the repair of this line which was considered in June is being taken up again apart from Lighting, Mills etc. it effects the Water Supply pumps of 6 towns. -

---

Generally, except in Terracina Garigliano Stretch, repair of distribution is keeping pace with available energy but with increases in Generation expected in December the position may be reverged.

(c) SEWERS, and Demolition and Debris and SALVAGE.

In all devastated towns these are badly damaged - I consider we are most fortunate in getting through the summer without serious epidemics from this cause. -

Some repairs have been done, work is in hand in many cases damage cannot be got at until debris has been removed. -

The standard in most demolished towns at present is, if the limited amount of water available to put in disappears without visible flooding, then alright as more water for flushing is available and debris removed more points for repair will be found over a long period of time.

The extant of Debris removal can be grouped approximately by number of projects passed in October

	Debris	Sewer Repairs
FROSINONE Province	46	2
LITTORIA "	9	-
ROMA "	34	6
	89	8
Previously passed projects	46	6

177

Declassified E.O. 12356 Section 3.3/NND No. 785019

Item XVIII

(a) Work in hand in Region.

All projects have been passed through Regional Engineer for about 2.000 million lira (5 million pounds) of which more than half is held up awaiting approval and funds by Minister of Works. -

Complete lists of all these projects are available in office of Regional Engineer and a list of those held up is enclosed with dates of passing this office and dates of onward passage from Genio Civile to Minister. -

Many of these projects are below 500.000 lire and provided a block grant of funds was made available would be freed, to go ahead as final approval has been delegated by Minister this without FUNDS is useless. -

A block grant of 350 million lira for general works other than housing was talked of early in October but has NOT yet matured.

Also totally inadequate.

Housing Repairs.

The present position of housing repair projects is :

	Funds allocated (these funds are NOT yet released)	Projects submitted
FROSINONE	35 million lira	26 million lira
LITTORIA	10 " "	27 " "
ROMA	30 " "	4 " "
RIETI	1 " "	5 " "
VITERBO	10 " "	3 " "
	86 million lira	65 million lira

My approximate estimate of requirements for Repairs in the 3 Southern provinces alone is 360 million and early steps are required to release more funds so that Finance can keep ahead of Projects. -

Increase of staff will increase speed of preparation of projects.

In TERNI AMG territory up to 25 October following reissue on 2 October projects of 10 million lira were approved and financed.

(b) Materials.

3/52 tons . IRON and Bricks

Declassified E.O. 12356 Section 3.3/NND No. 785019

passing this office and dates of onward passage from Genio Civile to Minister. -

Many of these projects are below 500,000 lire and provided a block grant of funds was made available would be freed, to go ahead as final approval has been delegated by Minister this without FUNDS is useless. -

A block grant of 350 million lira for general works other than housing was talked of early in October but has NOT yet matured.

Also totally inadequate.

Housing Repairs.

The present position of housing repair projects is :

	Funds allocated (these funds are NOT yet released)	Projects submitted
FROSINONE	35 million lira	26 million lira
LITTORIA	10 " "	27 " "
ROMA	30 " "	4 " "
RIETI	1 " "	5 " "
VITERBO	10 " "	3 " "
	86 million lira	65 million lira

My approximate estimate of requirements for Repairs in the 3 Southern provinces alone is 360 million and early steps are required to release more funds so that Finance can keep ahead of Projects. -

Increase of staff will increase speed of preparation of projects.

In TERNI AMG territory up to 25 October following release on 2 October projects of 10 million lira were approved and financed.

(b) Materials.

Cement very short supply. Outstanding demands 3152 tons . LIME and Bricks and Tiles require Coal to burn. Demands submitted 2 months ago .

Timber at present mainly salvage - 1772

./.

Declassified E.O. 12356 Section 3.3/NND No. 785019

Trees exist in LITTORIA and ROMA now that sap is receding felling and ~~s~~mills should be pressed - ~~Fairly~~ machinery the old pit saw as still used in INDIA. Failing

Stone available from debris.

Roofing material very short.

Glass very short - the only factory lacks coal. (SCIARRA - ROME in heard with Industry Division)

All debris contracts include a salvage clause of all usable material to be stacked in Genio Civile Deposits for reuse.

Enclosures

Declassified E.O. 12356 Section 3.3/NND No. 785019

G.2e CEF/gb

HEADQUARTERS
ALLIED MILITARY GOVERNMENT
LAZIO UMBRIA REGION
(Engineering Division)
APO 394

16 November 1944

~~TO~~ :

~~DISTRICT~~ :

~~EX RAPID SCOTT~~ :

Item XIII. Mines

1. Generally Mines are numerous in the area round the Anzio Beach Head and in the CUSTAV Line Area - and all along the Coast Line. -

2. In RIETI Province the Provincial Commissioner reported officially 750 mines collected by a squad and considered sufficiently cleared to agree to the Squad moving to FROSINONE.

3. For the southern part of FROSINONE Province a copy of the VIII Army mine location map has been obtained and copies made and issued to Genio Civile of Province.

Some work has been done in areas where work was required there remains a vast area untouched. -

The squad from RIETI worked for some weeks and was reported to be doing good work prior to stopping through heavy casualties.

4. In PERUGIA Province the Provincial Commissioner has reported a civil mine lifting squad at work trained by Army and doing good work. - No data as to numbers lifted.

5. In LITTORIA Province it has been ascertained from CES Army AMG that mine location reports are made. Application has been made to obtained copies of these locations to branch of HQ. AC. dealing with Mines, FBS, but with no result.

Declassified E.O. 12356 Section 3.3/NND No. 785019

~~SUBJECT~~ :

~~IN REPLY QUOTE~~:

Item XIII. Mines

1. Generally Mines are numerous in the area round the Anzio Beach Head and in the GUSTAV Line Area - and all along the Coast Line. -

2. In RIETI Province the Provincial Commissioner reported officially 750 mines collected by a squad and considered sufficiently cleared to agree to the Squad moving to FROSINONE.

3. For the southern part of FROSINONE Province a copy of the VIII Army mine location map has been obtained and copies made and issued to Genio Civile of Province.

Some work has been done in areas where work was required there remains a vast area untouched. -

The squad from RIETI worked for some weeks and was reported to be doing good work prior to stopping through heavy casualties.

4. In PERUGIA Province the Provincial Commissioner has reported a civil mine lifting squad at work trained by Army and doing good work. - No data as to numbers lifted.

5. In LITTORIA Province it has been ascertained from CMS Army AMG that mine location reports are made. Application has been made to obtained copies of these locations to branch of HQ. AC. dealing with Mines, PWB, but with no result. -

(a) The existing of mine fields is generally known locally but without delimination. -

The best indication is agricultural land is uncut grain crops as the inhabitants being hungry went on cutting till someone got killed. 177

./.

Declassified E.O. 12356 Section 3.3/NND No. 785019

(b) The Italian Mine Company stationed at GAETA has been given the task of Clearing 8 Water Supply systems of mines. - It has cleared two of these sufficiently for work on repairs to be done for temporary supply.

These are GAETA and FORMIA. - Work is in progress on remainder of GAETA supply and supplies for MINTURNO, SCAURI, BULGARINI; and preliminary reconnaissances of FONDI, ITRI, TERRACINA.

Progress is slow and casualties have been heavy. - At present rate these water supplies will take another 2 months.

(c) Housing Sites have had to be swept at TERRACINA and GAETA.

(d) All blown bridges before Reconstruction should be swept-a dozen have been ordered on Civil Mine Contractor but floods have prevented action.

(e) In LITTORIA alone their was known to be 100 km of POWER Line inaccessible for repairs due to mines. Sweeping of 50 kilometers is now in hand by civil Contract - and some work was done by the Mine Company on the line GAETA - GARIGLIANO - and will continue when water supplies are completed. - A detailed list of lines requiring sweeping is available sufficient work for some months ahead.

A vast area remains to sweep in LITTORIA Province including the whole of the Coastal Belt. -

6. ROME PROVINCE

Considerable work was done in ROME COMUNE by Allied Troops and an Italian Mine Company. Neither available since before 1st August.

A portion of ROME CITY has been without water because pipe damage could not be approached for MINES. - This is now being cleared by Civil Contractor. -

Minefields exist along the coast and AREZIO region and VALMONTONE area.

---

7. GENERALLY. Such sweeping as has so far been done is confined to the small areas required to enable essential works to be done, and the means

Declassified E.O. 12356 Section 3.3/NND No. 785019

These are GAETA and FORMIA. - Work is in progress on remainder of GAETA supply and supplies for MINTURNO, SCAURI, SPIGARELLI; and preliminary reconnaissances of FONDI, ITRI, TERRACINA.

Progress is slow and casualties have been heavy. - At present rate these water supplies will take another 2 months.

(c) Housing Sites have had to be swept at TERRACINA and GAETA.

(d) All blown bridges before Reconstruction should be swept-a dozen have been ordered on Civil Mine Contractor but floods have prevented action.

(e) In LITTORIA alone there was known to be 100 km of POWER Line inaccessible for repairs due to mines. Sweeping of 30 kilometers is now in hand by civil Contract - and some work was done by the Mine Company on the line GAETA - GARIGLIANO - and will continue when water supplies are completed. - A detailed list of lines requiring sweeping is available sufficient work for some months ahead.

A vast area remains to sweep in LITTORIA Province including the whole of the Coastal Belt. -

6. ROME PROVINCE.

Considerable work was done in ROME COMUNE by Allied Troops and an Italian Mine Company. Neither available since before 1st August.

A portion of ROME CITY has been without water because pipe damage could not be approached for MINES. - This is now being cleared by Civil Contractor. -

Minefields exist along the coast and ANZIO region and VALMONTONE area.

---

7. GENERALLY. Such sweeping as has so far been done is confined to the small areas required to enable essential works to be done, and the means ever for that is insufficient. -

The vast problem of clearing the country side essential for agriculture has NOT been even started.

A rough guess of cost of doing it is placed at over 200 million lire.

1769

Lt.Col.R.E.
Regional Engineer
LAZIO UMBRIA Region AMG.

Copy to:
Mines File

Declassified E.O. 12356 Section 3.3/NND No. 785019

Declassified E.O. 12356 Section 3.3/NND No. 785019

DETAILS OF PROJECTS (Non Military) APPROVED IN PRINCIPAL BY REGIONAL ENGINEER

(Highways Dept

Proj. No.	Route	Km.	Description	Contractor	Cat. Required	ACC/Lire	ACC/£	Date of approval	Remarks
75	82	69+409	Culvert	Garboli	Nil	650.000	=	14/10	(ACC/28
76	"	69+913	"	"	"	530.000	=	14/10	(Submitt (approv (Genio
49a	"	78+350	Ret. Wall	Mancini	"	540.000	495.000	30/10	=
50a	"	105+900	"	"	"	105.000	96.000	"	=
172	"	93+459	Bridge	"	"	190.000	174.000	"	=
173	"	93+605	"	"	"	630.000	578.000	"	=
174	"	102+980	"	"	"	180.000	164.000	"	=
175	"	103+164	"	"	"	250.000	228.000	"	=
176	"	107+650	"	"	"	230.000	205.000	"	=
177	"	118+900	"	"	"	2.360.000	1.298.000	"	=
					T O T A L	4.715.000	3.170.000		

Declassified E.O. 12356 Section 3.3/NND No. 785019

OJECTS (Fm Military) APPROVED IN PRINCIPAL BY REGIONAL ENGINEER


(Highways Department)


	Description	Contractor	Mat. Required	ACC/1s L.	ACC/2s L.	Date of approval	Remarks
9	Culvert	Carboli	Nil	650.000	=	14/10	(ACC/2s not yet (submitted for (approval by (Genio Civile
8	"	"	"	520.000	=	14/10	
0	Ret. Wall	Mancini	"	540.000	495.000	30/10	=
0	"	"	"	105.000	96.000	"	=
0	Bridge	"	"	190.000	174.000	"	=
0	"	"	"	630.000	570.000	"	=
0	"	"	"	180.000	164.000	"	=
4	"	"	"	250.000	228.000	"	=
0	"	"	"	230.000	205.000	"	=
0	"	"	"	1.350.000	1.236.000	"	=
	T O T A L			4.715.000	3.170.000		

Declassified E.O. 12356 Section 3.3/NND No. 785019

MAPS AND CHARTS TOO LARGE TO FILM
ON ONE EXPOSURE ARE FILMED CLOCKWISE
BEGINNING IN THE UPPER LEFT CORNER,
LEFT TO RIGHT, AND TOP TO BOTTOM.

SEE DIAGRAMS BELOW.

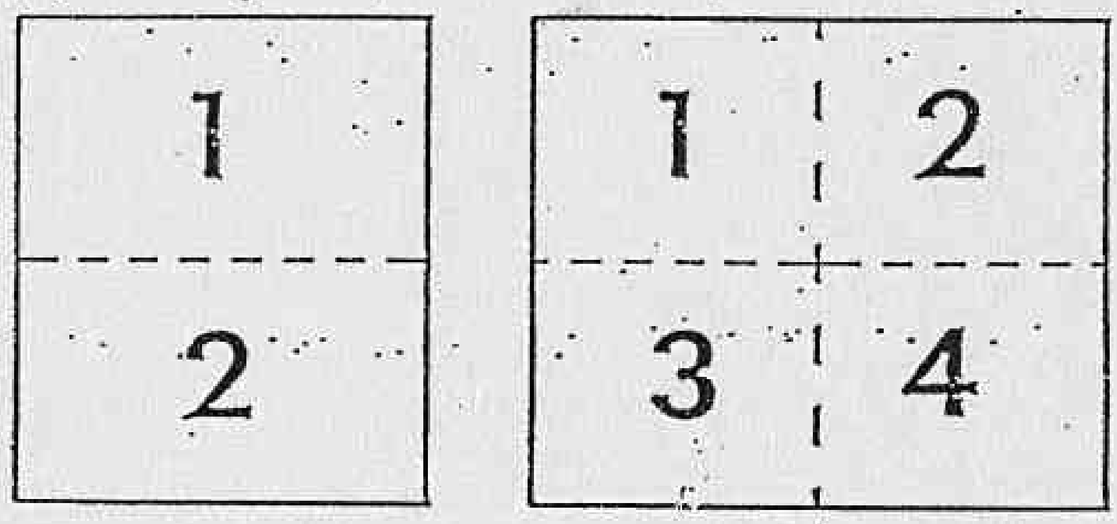

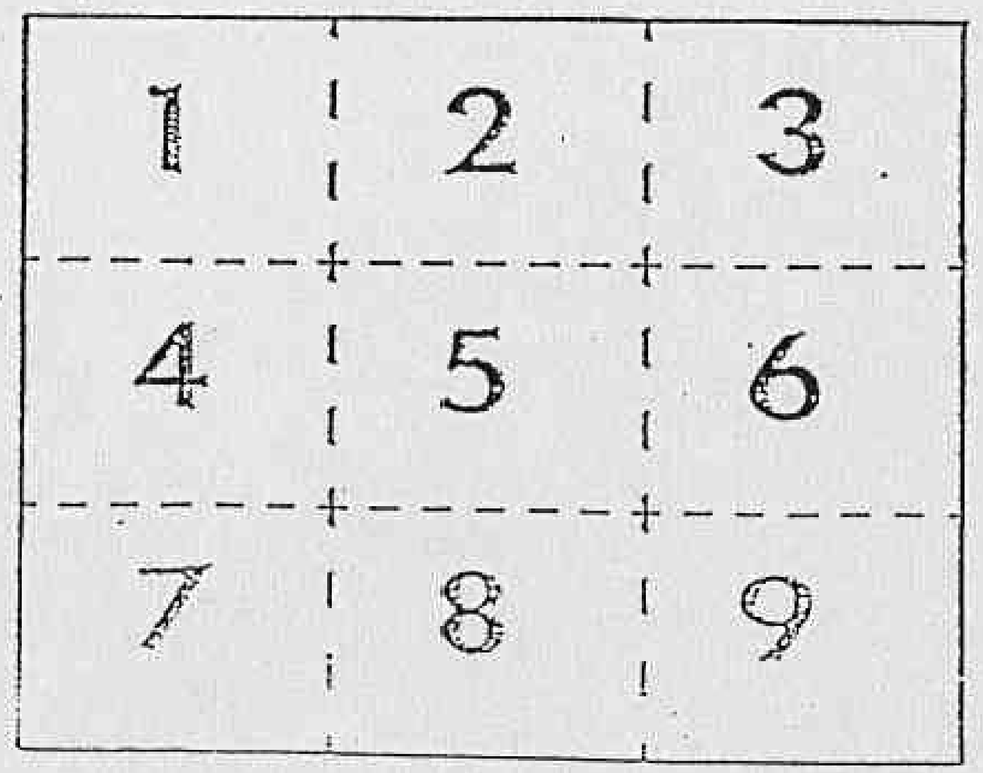

Declassified E.O. 12356 Section 3.3/NND No. 785019

ELENCO DELLE PERIZIE APPROVATE "IN PRINCIPLE" E POI INVIAT
AL MINISTERO DEI LL.PP. DAL 15.8.1944

PROVINCIA DI ROMA

n° di ord.	PROGETTO E DESCRIZIONE	IMPORTO	Rifer.e data approv. del REG.ENG.		Inv Min n°
1	ALBANO e GENZANO : Water supply	800.000	101.58	16.8.44	Chies mento
2	TIVOLI: Removal of debois	1.000.000	101.73	18.8.44	Appro
3	" " " "	1.000.000	101.74	" " "	"
4	" " " "	1.000.000	101.75	" " "	"
5	CIVITAVECCHIA: repairs buildings	1.000.000	101.86	21.8.44	2070
6	MONTEPORZIO: Repairs to church	72.000	101.82	21.8.44	2138
7	CIVITAVECCHIA: " " pear	4.000.000	101.89	21.8.44	2170
8	GROTTAFERRATA: " " sewerages	330.000	101.90	21.8.44	2068
9	ROCCA DI PAPA: Removal of debris	986.000	101.91	21.8.44	2072
10	MARINO: " " "	910.000	101.92	21.8.44	2171
11	" " " "	980.000	101.93	21.8.44	2071
12	ROCCA DI PAPA: " " "	996.000	101.94	21.8.44	2072
13	MARINO: " " "	987.000	101.95	21.8.44	2071
14	VALMONTONE: Repairs to houses	504.000	101.96	21.8.44	2071
15	ROCCA DI PAPA: " " acqueduct	440.000	101.97	21.8.44	2106
16	GENZANO,ARICCIA,ALBANO:Repairs to acqueduct	1.000.000	101.98	21.8.44	2106
17	CIVITAVECCHIA: Reconstruction pear "Trajano"	990.000	101.101	26.8.44	3539
18	TIVOLI:Repairs to Riformatorio "Sez.Cappuccini"	800.000	101.104	26.8.44	2182
19	" " " " "Sez.Centrale"	650.000	101.105	28.8.44	2182
20	SUBIACO: Removal of Debris	990.000	101.106	31.8.44	2300
21	VELLETRI: " " "	757.000	101.110	6.9.44	2441
22	VELLETRI: " " "	196.000	101.111	6.9.44	2441
23	VELLETRI: " " "	195.000	101.112	6.9.44	2441
24	ANZIO: Clearing schip yard	800.000	101.114	6.9.44	2439
25	VELLETRI: Removal of debris	936.000	101.116	6.9.44	2440
26	SUBIACO: " " "	980.000	101.126	9.9.44	2479
27	ANZIO: Clearing at port	75.000	101.127	9.9.44	2477
28	ALBANO: Repairs to sewerage	995.000	101.127	9.9.44	2476
29	PRATICA DI MARE: Bonifica	1.000.000	101.130	6.8.44	2429
30	FRASCATI: Repairs to Villa Biondi	600.000	101.131	7.9.44	2449
31	MONTEPORZIO:	870.000	101.150		
32	MONTECOMPATRI: Removal of debris	180.000	101.151	14.9.44	2562
33	ROCCA PRIORA:	400.000	101.152		
34	PALESTRINA: Removal of debris	880.000	101.164	21.9.44	2760
35	CARPINETO:	880.000	101.165	21.9.44	4239
36	ANZIO:	995.000	101.166	21.9.44	Appr
37	ALBANO: Repairs to streets	910.000	101.172	22.9.44	2786

Declassified E.O. 12356 Section 3.3/NND No. 785019

ELENCO DELLE PERIZIE APPROVATE "IN PRINCIPLE" E POI INVIATE AL MINISTERO DEI LL.PP. DAL 15.8.1944

PROVINCIA DI ROMA

GETTO E DESCRIZIONE	IMPORTO	Rifer.e data approv. del REG.ENG.	Invio al Ministero		Approvazione del Ministero	
			n°	Data	n°	Data
NZANO : Water supply	800.000	101.58 16.8.44	Chiesto al Genio Civ.completamento pratica.			
oval of debois	1.000.000	101.73 18.8.44	Approv.def.Mod/ACC/1		inv.al G.C.	
" " "	1.000.000	101.74 " " "	"	" " "	"	
" " "	1.000.000	101.75 " " "	"	" " "	"	
IA: repairs buildings	1.000.000	101.86 21.8.44	2070	17.10.44		
: Repairs to church	72.000	101.82 21.8.44	2138	17.10.44		
IA: " " pear	4.000.000	101.89 21.8.44	2170	17.10.44		
IA: " " sewerages	330.000	101.90 21.8.44	2068	11.11.44		
PA: Removal of debris	986.000	101.91 21.8.44	2072	17.10.44		
" " "	910.000	101.92 21.8.44	2171	17.10.44		
" " "	980.000	101.93 21.8.44	2071	17.10.44		
PA: " " "	996.000	101.94 21.8.44	2072	17.10.44		
" " "	987.000	101.95 21.8.44	2071	17.10.44		
Repairs to houses	504.000	101.96 21.8.44	2071	10.11.44		
PA: " " acqueduct	440.000	101.97 21.8.44	2106	23.9.44	398	27.10.44
CIA,ALBANO:Repairs to acqueduct	1.000.000	101.98 21.8.44	2106	22.9.44		
IA: Reconstruction pear "Trajano"	990.000	101.101 26.8.44	3539	9.11.44		
irs to Riformatorio "Sez.Cappuccini"	800.000	101.104 26.8.44	2182	24.10.44		
" " "Sez.Centrale"	650.000	101.105 28.8.44	2182	24.10.44		
oval of Debris	990.000	101.106 31.8.44	2300	16.9.44		
" "	757.000	101.110 6.9.44	2441	20.9.44		
" "	196.000	101.111 6.9.44	2441	20.9.44		
" "	195.000	101.112 6.9.44	2441	20.9.44		
ing schip yard	800.000	101.114 6.9.44	2439	23.9.44		
moval of debris	936.000	101.116 6.9.44	2440	23.9.44		
" "	980.000	101.126 9.9.44	2479	23.9.44		
ing at port	75.000	101.127 9.9.44	2477	20.9.44	353	11.11.44
irs to sewerage	995.000	101.127 9.9.44	2476	20.9.44		
ARE: Bonifica	1.000.000	101.130 6.8.44	2429	26.9.44	Inviata Min.Agricoltura	
pairs to Villa Biondi	600.000	101.131 7.9.44	2449	10.10.44		
I: Removal of debris	870.000	101.150				
	180.000	101.151 14.9.44	2562	7.10.44		
	400.000	101.152				
emoval of debris	880.000	101.164 21.9.44	2760	11.11.44		
	880.000	101.165 21.9.44	4239	11.11.44		
	995.000	101.166 21.9.44	Approv.def.al G.C.			
irs to streets	910.000	101.172 22.9.44	2780	17.10.44		

Declassified E.O. 12356 Section 3.3/NND No. 785019

27	ANZIO: Clearing at port	75.000	101.127	9.9.44	2477
28	ALBANO: Repairs to sewerage	995.000	101.127	9.9.44	2476
29	PRATICA DI MARE: Bonifica	1.000.000	101.130	6.8.44	2429
30	FRASCATI: Repairs to Villa Biondi	600.000	101.131	7.9.44	2449
31	MONTEPORZIO:	870.000	101.150		
32	MONTECOMPATRI: Removal of debris	180.000	101.151	14.9.44	2562
33	ROCCA PRIORA:	400.000	101.152		
34	PALESTRINA: Removal of debris	830.000	101.164	21.9.44	2760
35	CARPINETO:	880.000	101.165	21.9.44	4239
36	ANZIO:	995.000	101.166	21.9.44	Approv.
37	ALBANO: Repairs to streets	910.000	101.172	22.9.44	2780
38	GROTTAFERRATA:	746.000	101.179	25.9.44	2873
39	GROTAFFERRATA: Removal of debris	548.000	101.179		2873
40	FRASCATI: part.D) " " "	868.000	101.180	25.9.44	4302
41	FRASCATI: part.F) " " "	885.000	101.182		4300
42	FRASCATI: part.E) " " "	909.000	101.183		4303
43	ALBANO: Repair to sewerages	992.000	101.219	27.9.44	In corso
44	ROCCA DI PAPA: Repair to sewerages	192.000	101.220	27.9.44	3030
45	CIVITAVECCHIA: Repair to schools	825.000	101.221	27.9.44	In corso
46	CIVITAVECCHIA: " " dwellings	650.000	101.222	29.9.44	Approv. ta all'U
47	FRASCATI: 1^ part)	993.000	101.223	29.9.44	3057
48	FRASCATI: 2 part) Removal of debris	930.000	101.224	29.9.44	richiest
49	FRASCATI: 3 part)	940.000	101.225	29.9.44	"
50	GROTTAFERRATA: Demolitions & removal of debris	735.000	101.229	29.9.44	3058

Declassified E.O. 12356 Section 3.3/NND No. 785019

port	75.000	101.127 9.9.44	2477	20.9.44	353	11.11.44
sewerage	995.000	101.127 9.9.44	2476	20.9.44		
onifica	1.000.000	101.130.6.8.44	2429	25.9.44	Inviata Min.Agricoltura	
to Villa Biondi	600.000	101.131 7.9.44	2449	10.10.44		
	870.000	101.150				
emoval of debris	180.000	101.151 14.9.44	2562	7.10.44		
	400.000	101.152				
l of debris	880.000	101.164 21.9.44	2760	11.11.44		
	880.000	101.165 21.9.44	4239	11.11.44		
	995.000	101.166 21.9.44	Approv.def.al G.C.			
streets	910.000	101.172 22.9.44	2780	17.10.44		
	746.000	101.179 25.9.44	2873	11.11.44		
noval of debris	548.000	101.179	2873	11.11.44		
" " "	868.000	101.180 25.9.44	4302	13.11.44		
" " "	835.000	101.182	4300	13.11.44		
" " "	909.000	101.183	4303	13.11.44		
sewerages	992.000	101.219 27.9.44	In corso			
air to sewerages	192.000	101.220 27.9.44	3030	13.11.44		
air to schools	825.000	101.221 27.9.44	In corso			
" " dwellings	650.000	101.222 29.9.44	Approv.defin.dell'ACC/1 e inviata all'Ufficio Genio Civile			
	993.000	101.223 29.9.44	3057	13.11.44		
Removal of debris	930.000	101.224 29.9.44	richiesta al G.C. la perizia			
	940.000	101.225 29.9.44	"	"	"	"
olitions & removal of debris	735.000	101.229 29.9.44	3058	10.10.1944		

Declassified E.O. 12356 Section 3.3/NND No. 785019

nº di ord.	PROGETTO E DESCRIZIONE	IMPORTO	Riferim. data approvaz. del Min. Lav.		Invio al Ministero nº	Invio al Ministero data
51	MONTELANICO: Demolitions & Removal of debris	610.000	101.230	29.9.44	3058	10.10.4
52	NETTUNO:	990.000	101.231	29.9.44	3058	10.10.4
53	SUBIACO-/ARZIA:	970.000	101.243			
54	ARDEA-ANZIO-NETTUNO: Re-housing	992.000	101.244	2.10.44	3133	27.10.4
55	ETANO ROMANO:	760.000	101.245			
56	ARTENA: Removal of debris & Repair to sewerage	3.600.000	101.246	2.10.44	3136	6.11.44
57	FRASCATI: Repairs to Convento PP.Minori	1.260.000	101.249	2.10.44	3134	14.10.4
58	MACCARESE: Bonifica	11.500.000	101.226	5.10.44	3199	13.10.4
59	PALIANO:	4.200.000	101.227	5.10.44	3140	13.10.4
60	PALESTRINA: Removal of debris	940.000	101.228	5.10.44	3058	10.10.4
61	ARICCIA: Removal of Istituto Ortopedico	2.475.000	101.273	7.10.44	Richiesto pa	
62	CIVITAVECCHIA: Removal of Istituto Case Popol.	820.000	101.274	7.10.44	3172	13.11.4
63	CIVITAVECCHIA: " " " " "	845.000	101.275	7.10.44	Approv.def.	
64	ALBANO: Repairs to Civil Hospital	810.000	101.278	7.10.44	3173	24.11.4
65	CAVE: Landslip to Prenestina road	1.050.000	102.36	9.10.44	400/2 inv.al	
66	CIVITAVECCHIA: bridges salvages	220.000	101.296	10.10.44	3349	23.11.4
67	S.MAURO: Repair Bridges nº10	4.300.000	103.95	11.10.44	Approv.def.	
68	ROCCA DI PAPA: Repairs to Chiesa Parrocchiale	69.480	101.298	11.10.44	"	"
69	PALESTRINA: Repairs to sewerages	1.700.000	101.299	11.10.44	3341	17.10.4
70	TIVOLI: Removal of debris - IV part)	1.000.000	101.300	11.10.44	Non risulta	
71	VELLETRI: Water supply	4.300.000	101.302	12.10.44	"	"
72	LANUVIO: Erection Wood's huts	507.000	101.327	16.10.44	3463	13.11.4
73	GENZANO: Removal debris	910.000	101.328	16.10.44	3463	13.11.4
74	" " "	800.000	101.329	16.10.44	3463	13.11.4
75	CIVITAVECCHIA: Repairs to sewerage	800.000	101.330	16.10.44	3463	13.11.4
76	VALMONTONE: Erection wood's huts	950.000	101.332	16.10.44	3463	13.11.4
77	CIVITAVECCHIA: Repairs to sewerage	610.000	101.331	16.10.44	3463	13.11.4
78	TEVERE RIVER: Removal of debris and sewerage	4.200.000	101.337	17.10.44	3541	11.11.4
79	ANTICOLI-CORRADO- PALO: Repairs to Provincial road	5.800.000	101.43	18.10.44	3540	17.11.4
80	BRACCIANESE ROAD: Km. 56,6 -- repairs to bridge nº 1	360.000	103.109	18.10.44	3531	9.11.4
81	BRACCIANESE ROAD: Km. 72,3 -- " " nº 5	1.150.000	103.110	18.10.44	3532	11.11.4
82	GENZANO: Removal debris and Salvages	675.000	101.338	19.10.44	3534	19.11.4
83	VELLETRI: Repairs to Irigoma	1.000.000	101.339	23.10.44	Si attende vio al Mini	
84	CIAMPINO: Repairs to acqueduct	820.000	101.241	27.10.44	3867	16.11.4
85	CIAMPINO: " " church	520.000	101.389	27.10.44	3852	17.11.4
86	NETTUNO: Removal of debris	151.000	101.4bis	28.10.44	In corso	
87	ALBANO: Vanvitelli works	860.000				

Declassified E.O. 12356 Section 3.3/NND No. 785019

e DESCRIZIONE	IMPORTO	Riferim. data approvaz. del RED.PRO.	Invio al Ministero		Approvazione del Ministero	
			n°	data	n°	data
pilitions & Removal of debris	610.000	101.230 29.9.44	3058	10.10.44		
	990.000	101.231 29.9.44	3058	10.10.44		
A: { Re-Mounting	970.000	101.243 {				
	992.000	101.244 { 2.10.44	3133	27.10.44		
	760.000	101.245 {				
of debris & Repair to sewerage	3.800.000	101.246 2.10.44	3136	6.11.44		
s to Convento PP.Minori	1.260.000	101.249 2.10.44	3134	14.10.44		
ges	11.500.000	101.226 5.10.44	3199	13.10.44	Inviata al Min. Agricoltura	
	4.200.000	101.227 5.10.44	3140	13.10.44	" " "	
val of debris	940.000	101.228 5.10.44	3058	10.10.44		
of Istituto Ortopedico	2.475.000	101.273 7.10.44	Richiesta perizia al G.C.			
moval of Istituto Onse Fopol.	820.000	101.274 7.10.44	3172	13.11.44		
" " " " "	845.000	101.275 7.10.44	Approv.def.ACC/1 al G.C.			
Civil Hospital	819.000	101.278 7.10.44	3173	24.11.44		
Prenestina road	1.050.000	102.36 9.10.44	ACC/2 inv.all'Uff.Tec.Prov.Roma			
dges salvages	226.000	101.296 10.10.44	3349	23.11.44		
ridges n° 10	4.300.000	103.35 11.10.44	Approv.def.ACC/1 inviata al G.C.			
pairs to Chiesa Parrocchiale	69.480	101.298 11.10.44	"	" "	"	" "
rs to sewerages	1.700.000	101.299 11.10.44	3341	17.10.44		
f debris - IV part)	1.000.000	101.300 11.10.44	Non risulta l'approv.dell'ACC/1			
upply	4.300.000	101.302 12.10.44	"	"	"	"
Wood's huts	507.000	101.327 16.10.44	3463	13.11.44		
debris	910.000	101.328 16.10.44	3463	13.11.44		
"	800.000	101.329 16.10.44	3463	13.11.44		
pairs to sewerage	800.000	101.330 16.10.44	3463	13.11.44		
om wood's huts	950.000	101.332 16.10.44	3463	13.11.44		
pairs to sewerage	610.000	101.331 16.10.44	3463	13.11.44		
val of debris and sewerage	4.200.000	101.337 17.10.44	3541	11.11.44		
epairs to Provincial road	5.880.000	101.43 18.10.44	3540	17.11.44		
Km. 56,6 - repairs to bridge n° 1	360.000	103.109 18.10.44	3531	9.11.44		
Km. 72,3 - " " n° 5	1.150.000	103.110 18.10.44	3532	11.11.44		
ebris and Salvages	675.000	101.336 19.10.44	3534	19.11.44		
to Prisons	1.000.000	101.339 23.10.44	Si attende copia perizia per invio al Ministero			
to aqueduct	820.000	101.241 27.10.44	3867	16.11.44		
church	520.000	101.389 27.10.44	3852	17.11.44		
f debris	151.000	101.4bis 28.10.44	In corso			

Declassified E.O. 12356 Section 3.3/NND No. 785019

79	GETTEVENO- PALO: Repairs to Provincial road			5.880.000	101.43	18.10.44	3540
80	FRACCIANESE ROAD: Km. 56,6 -- repairs to bridge		n° 1	360.000	103.109	18.10.44	3331
81	FRACCIANESE ROAD: Km. 72,3 -- "	"	n° 5	1.150.000	103.110	18.10.44	3532
82	GENZANO: Removal debris and Salvages			675.000	101.338	19.10.44	3534
83	VELLETRI: Repairs to Prisons			1.000.000	101.339	23.10.44	Si attende vio del Mi
84	CIAMPINO: Repairs to acqueduct			820.000	101.241	27.10.44	3867
85	CIAMPINO: " " church			520.000	101.389	27.10.44	3852
86	NETTUNO: Removal of debris			151.000	101.4bis	28.10.44	In corso
87	ALBANO: Various works			898.000	101.400	28.10.44	Approv.de
88	MARINO: Works executed by the Comune			666.432	101.419	31.10.44	" "
89	CARPINETANA ROAD: Repair to bridge n°		15	515.000	103.148	3/11/44	
90	" " " " "	"	16	472.000	103.149	3.11.44	
91	" " " " "	"	17	851.000	103.150	3.11.44	4069
92	" " " " "	"	18	399.000	103.151	3.11.44	
93	" " " " "	"	19	388.000	103.152	3.11.44	
94	FRASCATI: Repairs to schools of Villa Sora			800.000	101.473	7.11.44	4207
95	LANUVIO: Repairs to Istituto Salesiani			760.000	101.474	11.11.44	Si attend Comio Civ

Declassified E.O. 12356 Section 3.3/NND No. 785019

epairs to Provincial road	5.880.000	101.43	18.10.44	3540	17.11.44
km. 56,6 - repairs to bridge					
n° 1	360.000	103.109	18.10.44	3531	9.11.44
km. 72,3 - " " n° 5	1.150.000	103.110	18.10.44	3532	11.11.44
bris and Salvages	575.000	101.338	19.10.44	3534	19.11.44
to Irisonn	1.000.000	101.339	23.10.44	Si attende copia perizia per invio al Ministero	
to sequestrt	820.000	101.241	27.10.44	3867	16.11.44
" church	520.000	101.380	27.10.44	3852	17.11.44
f debris	151.000	101.4[illegible]	28.10.44	In corso	
ks	898.000	101.400	28.10.44	Approv.def.AUC/1 inv. al C.C.	
ted by the Commo	566.432	101.419	31.10.44	" " " " "	
Repair to bridge n°15	515.000	103.148	3/11/44		
" " " " 16	472.000	103.149	3.11.44		
" " " " 17	851.000	103.150	3.11.44	4009	17.11.44
" " " " 18	399.000	103.151	3.11.44		
" " " " 19	383.000	103.152	3.11.44		
to schools of Villa Sora	800.000	101.473	7.11.44	4207	17.11.44
o Istituto Salesiani	760.000	101.474	11.11.44	Si attende copia perizia dal Genio Civile	

Declassified E.O. 12356 Section 3.3/NND No. 785019

ELENCO DELLE PRATICHE APPROVATE "IN PRINCIPIO" O TRASMESSE AL MINISTERO DEI LL.PP. DAL 15.8.1944
PROV. DI LITTORIA

N° d'ordine	PROJECT AND DESCRIPTION	AMOUNT	Ref. Date of approval by MIN. LAV.	Invio a
				N°
1	SEZZE: Removal of Debris 84	610.000	18/11/44 77	Approved
2	SPERLONGA: " " " 85	160.000	21/11/44 70	dell'A.C.
3	TERRACINA: " " " 133	715.000	21/11/44 80	Spediti
4	CASTELFORTE " " 134	970.000	21/11/44 81	mod. A.C.
5	ELENA: (GAETA) " " 137 (II part)	960.000	21/11/44 83	
6	" " " " 136 (III part)	925.000	21/11/44 84	
7	FORMIA: " " 138	900.000	21/11/44 85	
8	CISTERNA: " " 139	927.000	20/12/44 100	2137
9	" Re-housing	67.000.000	29/11/44 118	approved
10	Repairs to bridges N° 20, 9, 1, 2 4 little bridges	9.932.100	29/11/44 79	2366
11	ROCCAGORGA 176	280.000	6/12/44 113	2437
12	LITTORIA: Repairs to Aqueduct 235	5.445.000	13/11/44 125	3768
13	" " " Cisterna RR.CC. 228	1.240.000	13/11/44 146	2526
14	ITRI: Removal of debris 227	996.000	13/11/44 147	3103
15	CORI: " " " 226	790.000	13/11/44 148	3106
16	LITTORIA: Repairs to Ufficio Finance 225	434.000	15/11/44 162	APPROVED MOD.L.L.
17	TERRACINA: Re-housing 236	20.000.000	20/11/44 193	2761
18	MONTEBUONO DI GAETA: Re-housing 237	27.000.000	20/11/44 194	2766
19	TERRACINA: Removal of debris 342	999.000	27/11/44 209	4073
20	CISTERNA: " " " 348	556.000	27/11/44 10	"
21	PONTINIA: Repairs to bridge N°8 on Sisto Road 512	3.400.000	9/12/44 7	3765
22	TERRACINA { 564	965.000	10/12/44	
23	CORI BASSO { Removal of debris 566	710.000	10/12/44	3352
24	CORI ALTO { 565	865.000	10/12/44	
25	LITTORIA: Repairs to bridge N°5 on Selvicciola 563	7.700.000	12/12/44	3348
26	" " " buildings of Istit.Case Popol. 567	14.937.000	13/12/44	3359
27	" " " P.O. 560	830.000	15/12/44	3457
28	" SEZZE: Repairs to bridge N°12 559	995.000	17/12/44	3509

Declassified E.O. 12356 Section 3.3/NND No. 785019

ELENCO DELLE PERIZIE APPROVATE "IN PRINCIPIO" e POI INVIATE
AL MINISTERO DEI LL.PP. DAL 15.1.1944
PROV. DI LITTORIA

...D AND DESCRIPTION	AMOUNT	Def. Date of approval by MIN. ENG.	Invio al Min.		Approv. del Ministero	
			N°	Date	N°	Date
of Debris 84	610.000	11/11/44	Approvate definitivamente			
" " 85	160.000	21/11/44	dall'ACC.			
" " 133	715.000	21/11/44	Spedite all'ufficio i			
" " 134	970.000	21/11/44	mod. ACC/1 e ACC/2			
" " 137 (II part)	960.000	21/11/44				
" " 136 (III part)	925.000	21/11/44				
" " 138	500.000	21/11/44				
" " 139	927.000	20/11/44	2187	23/9/44		
housing	6?.000.000	2/11/44	accordo			
ges N° 20, 9, 1, 2 & 11 ttle bridges	9.934.100	9/11/44	2366	20/9/44		
6	280.000	6/11/44	2437	23/9/44		
ge to Aqueduct 235	5.445.000	14/11/44	3798	10/11/44		
" Caserma RR.CC. 228	1.=42.000	13/11/44	2526	7/10/44		
f debris 227	996.000	13/11/44	3168	7/10/44		
" 226	798.000	13/11/44	3168	7/10/44		
ing to Ufficio Finanze 225	434.000	15/11/44	Approv. Min. all'aff. 1 mod. ACC.			
housing 236	20.000.000	20/11/44	2701	7/10/44		
...: Re-housing 237	27.000.000	20/11/44	2766	30/9/44		
val of debris 342	999.000	27/11/44	4073	7/10/44		
" " 340	955.000	27/11/44	"	"		
ing to bridge N°8 on Litto Road 512	3.400.000	9/11/44	3168	24/10/44		
564	565.000	10/11/44				
Removal of debris 556	710.000	10/11/44	3352	30/10/44		
555	855.000	10/11/44				
ge to bridge N°5 on Valvisciola 563	7.750.000	12/11/44	3343	23/10/44		
" building of Istit.Case Popol. 567	14.917.000	13/11/44	3356	17/10/44		
" P.C. 560	830.000	15/11/44	3457	3/11/44		
...: Remains to bridge N°12 559	995.000	17/11/44	3509	5/11/44		

Declassified E.O. 12356 Section 3.3/NND No. 785019

20	CISTERNA: " " "	318		250.000	27/5/44	10	"
21	TERRACINA: Repairs to bridge N°8 on Latto Road	312		3.400.000	9/10/44	191-47	3168
22	TERRACINA	564		965.000	10/10/44	191-56	
23	CORI BASSO Removal of debris	566		710.000	10/10/44	191-284	3352
24	CORI ALTO	565		865.000	10/10/44	191-285	
25	LITTORIA: Repairs to bridge N°5 on Valvisciola	563		7.750.000	12/10/44	191-288	3348
26	" " " buildings of Istit.Case Popol.	557		14.937.000	13/10/44	191-293	3358
27	" " " P.O.	560		830.000	16/10/44	191-313	3457
28	" SERMONETA: Repairs to bridge N°12	559		995.000	17/10/44	191-195	3509
29	SEZZINA ROAD: Repairs to bridge N° 3	660		2.900.000	17/10/44	191-197	3508
30	FONDI: Removal of Debris	658		998.000	17/10/44	191-336	3542
31	Repairs to bridge N°4	887		3.640.000	18/10/44	191-342	3533
32	FONDI:)	873		997.000	23/10/44	191-345	3727
33	")	880		995.000	23/10/44	191-346	"
34	MINTURNO)	881		506.000	23/10/44	191-347	"
35	TERRACINA:) Repairs to private houses for	883		988.000	23/10/44	191-348	"
36	MINTURNO:) 876 roofless people			995.000	23/10/44	191-349	"
37	APRILIA:)	882		815.000	23/10/44	191-350	"
38	TERRACINA:)	877		992.000	23/10/44	191-351	"
39	TERRACINA: Removal of debris	879		973.000	23/10/44	191-356	3692
40	" Repairs to private houses	868		990.000	24/10/44	191-361	3720
41	GAETA : " " pour of port	885		28.870.000	24/10/44	191-362	3735
42	Repairs to bridges N°19-1+31 little bridges	884		11.910.490	27/10/44	191-188	3869
43	CISTERNA: Repairs requisitioned dwellings	875		991.900	28/10/44	191-389	3836
44	" 176 Erection of 5 huts	1132		690.000	31/10/44	191-413	3942
45	PORTATORE RIVER: Repairs to bridge N° 7	880		11.300.000	4/11/44	193-153	4068

Declassified E.O. 12356 Section 3.3/NND No. 785019

" " 318	955.000	17/9/44	"	"	
...ire to bridge N°8 on Forte Road 512	3.400.000	19/9/44	3165	24/10/44	
564	265.000	19/9/44			
...moval of debris 566	710.000	19/9/44	3356	30/10/44	
565	865.000	19/9/44			
...s to bridge N°5 on Valviaciola 963	7.750.000	19/9/44	3348	23/10/44	
" buildings of Istit.Case Popol. 957	14.937.000	19/9/44	3356	17/10/44	
" P.O. 560	830.000	19/9/44	3157	3/11/44	
...Repairs to bridge N° 12 559	995.000	19/9/44	3509	5/11/44	
...pairs to bridge N° 3 660	2.900.000	19/9/44	3508	5/11/44	
...of Debris 658	518.000	19/9/44	3542	5/11/44	
...dge N°4 887	3.640.000	19/9/44	3533	5/11/44	
	997.000	19/9/44	3727	12/11/44	
	995.000	19/9/44	"	"	
	506.000	19/9/44	"	"	
...pairs to private houses for 883	988.000	19/9/44	"	"	
...offices people	995.000	19/9/44	"	"	
	815.000	19/9/44	"	"	
	992.000	19/9/44	"	"	
...l of debris 879	973.000	19/9/44	3692	9/11/44	
...s to private houses 866	990.000	19/9/44	3720	11/11/44	
" pear of port 885	20.870.000	19/9/44	3735	"	
...ges N°19-31 little bridges 884	11.910.490	19/9/44	3869	13/11/44	
...s requisitioned dwelling 875	991.900	19/9/44	3836	11/11/44	
...ion of 5 huts 1132	690.000	19/9/44	3942	15/11/44	
...Repairs to bridge N° 7 888	11.300.000	19/9/44	4068	15/11/44	

(over)

Declassified E.O. 12356 Section 3.3/NND No. 785019

46	APRILIA: Repairs to various offices			1.700.000	6/101/469	4203
47	TERRACINA) 1112			989.000	7/11/44	4210
48	CISTERNA)			994.000	7/11/469	4404
49	ITRI) : Repairs to dwellings			931.000	7/101/471	4405
50	FONDI)			958.000	7/101/472	4406
51	S.DONATO RIVER : Repairs to bridges	14+15+16	1106	2.227.000	8/101/458	4353
52	VIA APPIA: Roads repair	(Iprt)	1107	9.725.000	8/101/456	4352
53	Repairs road of bonifica		1108	2.138.000	8/101/457	4351
54	FONDI: Definitive repairs of acquedact			2.970.000	11/101/429	4395

Declassified E.O. 12356 Section 3.3/NND No. 785019

rs to various offices			1.700.000	6/11/44	4203	15/11/44
1112			989.000	7/11/44	4210	"
pairs to dwellings			994.000	7/11/44	4484	"
			931.000	7/11/44	4405	"
			958.000	7/11/44	4406	"
: Repairs to bridges 14+15+16		1106	2.225.000	8/11/44	4353	in copia
s repair	(Iprt)	1107	9.725.000	8/11/44	4352	"
bonifica		1108	2.138.000	8/11/44	4351	"
ve repairs of aqueduct			2.970.000	11/11/44	4395	"

Declassified E.O. 12356 Section 3.3/NND No. 785019

ELENCO DELLE PERIZIE APPROVATE "IN PRINCIPIO" E POI INVIATE AL MINISTERO DEI LL.PP. DAL 15.9.1944

PROV. DI FROSINONE

nº di ord.	PROGETTO E DESCRIZIONE	IMPORTO	Riferim.to e data approvazione del Provv.	Invio a Ministero nº	Invio a Ministero data
1	Frosinone: Repairs to private buildings I scheme	4.530.000	101.132	4234	11/10/44
2	" " " " II scheme	5.184.000	101.133		
3	" " " "III "	4.230.000	101.134		
4	Amaseno: Removal of debris	974.000	101.136 13-9-44		
5	Ferentino: " " "	992.000	101.137 13-9-44		
6	" " " "	996.000	101.138 13-9-44		
7	Anagni: " " "	992.000	101.139		
8	Vallecorsa: " " "	996.000	101.140		
9	Pofi: " " "	746.000	101.141		
10	Veroli: " " "	991.000	101.142		
11	Frosinone: " " " (East Section)	991.000	101.143	4234	11/10/44
12	" " " " (Central ")	996.000	101.144	4234	11/10/44
13	" " " " (West ")	997.000	101.145	4235	11/10/44
14	Repairs to bridge nº1 on the Rogo ditch	930.000	103.41	2542	11/10/44
15	" " " " 3 Casamari on the Torrent Amaseno	2.700.000	103.42	2543	7/10/44
16	Repairs to bridge nº31 near Sgurgola	1.000.000	103.44	3159	17/10/44
17	" " " " 41 on Rapido River	1.120.000	103.46	2542	7/10/44
18	" " " " 38 near Borolo	3.800.000	103.47	2541	7/10/44
19	Fontecorvo: Removal of debris	995.000	101.167	4236	11/10/44
20	Cassino: " " " (1st.part)	997.000	101.168		
21	Aquino: " " " (2 and part)	995.000	101.169		
22	" " " " (3 and part)	980.000	101.170	Fon pervenuto	
23	Fontecorvo: Repairs to Case Popolari	430.000	101.171	2779	30/10/44
24	" " " " "	700.000	101.207	2964	6/11/44
25	" " " " "	635.000	101.208	2964	6/11/44

Declassified E.O. 12356 Section 3.3/NND No. 785019

ELENCO DELLE PERIZIE APPROVATE "IN PRINCIPIO" E POI INVIATE
AL MINISTERO DEI LL.PP. DAL 15.8.1944
PROV. DI MODENA

OGGETTO E DESCRIZIONE	IMPORTO	Riferim.to e data approvazione del RES.PRO.	Divis.ne al Ministero		Approvazione del Ministero	
			n°	Data	n°	Data
Repairs to private buildings I scheme	4.530.000	101.132	Approv.definit.		103/1 invio al Genio Civile	
" " " II scheme	5.184.000	101.133	13/9/1944			
" " "III "	4.230.000	101.134				
Removal of debris	974.000	101.136 13-9-44				
" " "	992.000	101.137 13-9-44				
" " "	996.000	101.138 13-9-44				
" " "	992.000	101.139	13/9/44			
" " "	996.000	101.140	13/9/44			
" " "	746.000	101.141	13/9/44			
" " "	991.000	101.142	13/9/44			
" " " (East Section)	991.000	101.143		4234	11.11.44	
" " " (Central ")	996.000	101.144	13/9/44	4234	11.11.44	
" " " (West ")	997.000	101.145		4235	11.11.44	
Bridge n°1 on the Rugno ditch	930.000	103.41	15/9/44	2542	11.10.44	
" " 3 Casamari on the Torrent	2.700.000	103.42	15/9/44	2541	7.10.44	
Bridge n°31 near Sgurgola	1.000.000	103.44	15/9/44	3159	17.10.44	All°Uff.G.C.per completamento
" " 41 on Rapido River	1.120.000	103.46	15/9/44	2542	7.10.44	
" " 35 near Torrole	3.800.000	103.47	15/9/44	2541	7.10.44	
Removal of debris	995.000	101.167	21/9/44	4236	11.11.44	Approv.def.ACC/1 al Genio Civile
" " " (1st.part)	997.000	101.168	21/9/44			
" " " (2 and part)	995.000	101.169				
" " " (3 and part)	880.000	101.170	21/9/44	Non pervenuta a questo Ufficio		
Repairs to Case Popolari	430.000	101.171	22/9/44	2779	30.10.44	
" " " "	700.000	101.207	27/9/44	2964	6.10.44	
" " " "	635.000	101.208	27/9/44	2964	6.10.44	

Declassified E.O. 12356 Section 3.3/NND No. 785019

18	"	"	"	" 36 near Isoroio		3.000.000	103.47	15/9/44	2541	7.10
19	Pontecorvo: Removal of debris					995.000	101.167	21/9/44	4236	11.11
20	Cassino:	"	"	"	(1st.part)	997.000	101.168	21/9/44		
21	Aquino:	"	"	"	(2 and part)	995.000	101.169	21/9/44	Non pervenute	
22	"	"	"	"	(3 and part)	880.000	101.170			
23	Pontecorvo: Repairs to Case Popolari					430.000	101.171	22/9/44	2779	30.10
24	"	"	"	"	"	700.000	101.207	27/9/44	2964	6.10
25	"	"	"	"	"	635.000	101.208	27/9/44	2964	6.10
26	Aquino: (1st scheme)					960.000	101.211			
27	Arce:					510.000	101.212			
28	Pastena:					990.000	101.213			
29	Fontana Liri:					540.000	101.214			
30	S.Giovanni Incarico:				Removal debris	830.000	101.215	27/9/44		
31	Ceprano:					960.000	101.216			
32	Isola Liri:					670.000	101.217			
33	Pico:					972.000	101.218		4236	11.11
34	Repairs to bridges N°4 and 5 Isola Liri					750.000	103.60		4236	11.11
35	"	"	"	"19	near Anagni	300.000	103.61		4236	11.11
36	"	"	"	"18	" "	1.100.000	103.62	28/9/44	4236	11.11
37	"	"	"	"73	" Clevio	2.300.000	103.63		4236	11.11
38	"	"	"	"16	" Paliano	2.000.000	103.64			
39	"	"	"	"43	" Sora	800.000	103.67	4/10/44	3131	30.10

Declassified E.O. 12356 Section 3.3/NND No. 785019

38 near Torolo	3.800.000	103.47 15/9/44	2341	7.10.44		
of debris	995.000	101.167 21/9/44	4236	11.11.44	Approv.def.ACC/1 al Genio Civile	
" " (1st.part)	997.000	101.168 21/9/44				
" " (2 and part)	995.000	101.169				
" " (3 and part)	885.000	101.170 21/9/44	Non pervenuta a questo Ufficio			
to Case Popolari	430.000	101.171 22/9/44	2779	30.10.44		
" " "	700.000	101.207 27/9/44	2964	6.10.44		
" " "	635.000	101.208 27/9/44	2964	6.10.44		
	960.000	101.211				
	510.000	101.212				
	990.000	101.213				
	540.000	101.214				
Removal debris	830.000	101.215 27/9/44				
	960.000	101.216				
	670.000	101.217				
	972.000	101.218	4230	11.11.44	Approv.def.ACC/1 al G.C.	
3/4 and 5 Isola Sacra	750.000	103.60	4236	11.11.44	id.	—
"19 near Ardeatina	300.000	103.61	4236	11.11.44	id.	
"18 " "	1.100.000	103.62 20/9/44	4236	11.11.44	id.	
"73 " Cisterna	2.300.000	103.63	4236	11.11.44	id.	
"16 " Velletri	2.000.000	103.64				
"43 " Roma	800.000	103.67 4/10/44	3131	30.10.44		

Declassified E.O. 12356 Section 3.3/NND No. 785019

n° di ord.	PROGETTO E DESCRIZIONE	IMPORTO	Riferim. data approvazione del Min. LL.PP.	Invio al Ministero	
				n°	Data
40	Removal of Debris to Tiburtina road	113.000	101.251 5.10.44	Approv. def. A.C.	
41	Alatri: Removal debris from streets	24.000	101.252 " " "	"	"
42	Supino: Repairs to sewerages	17.000	101.253 " " "	"	"
43	Supino: Removal debris from streets	65.000	101.254 " " "	"	"
44	Anagni: " " " "	100.000	101.255 " " "	"	"
45	Frosinone: Repairs to Prenestina road	20.417	101.256 " " "	"	"
46	Alvito: " " Aqueducts	5.085	101.257 " " "	"	"
47	Alvito: Removal Debris	77.667	101.258 " " "	"	"
48	Vicalvi: Repairs to Aqueduct	18.000	101.259 " " "	"	"
49	Alatri: Removal of Debris	12.495	101.260 " " "	"	"
50	S.Giorgio al Liri: Removal of Debris	52.841	101.262 " " "	"	"
51	Vicalvi: Removal of Debris	30.420	101.263 " " "	"	"
52	S.Giorgio: Repairs to sewerages	67.890	101.264 " " "	"	"
53	Alatri: Removal of Debris	321.500	101.265 " " "	"	"
54	Supino: Repairs to Aequeduct	10.000	101.261 " " "	"	"
55	Anagni: Repairs to Sanatorio	530.000	101.277 7.10.44	"	"
56	Pastena, Mte. Rondi Repairs to Bridge n°71	950.000	103.96 9.10.44	"	"
57	Esperia:	996.000	101.280 9.10.44	"	"
58	Pontecorvo: II part.)	960.000	101.281 " " "	"	"
59	Pontecorvo: III part.)	995.000	101.282 " " "	"	"
60	Pontecorvo: IV part.) - Removal of debris	942.000	101.283 " " "	"	"
61	Pontecorvo: V part.)	990.000	101.284 " " "	"	"
62	Patrica: Repairs to bridge n° 20	806.000	103.99 12.10.44	3354	23.10
63	Cassino: Repairs to Hospital	1.000.000	101.276 13.10.44	Approv. def.	
64	Pontecorvo: " " "	962.000	101.287 10.10.44	3350	9.10
65	Isola Liri: Repair to buildings of Cons Popol.	4.473.000	101.301 12.10.44	3346	30.10
66	Casalvieri: Repairs to Bridge n° 74	642.000	103.102 16.10.44	Approv. def.	
67	S.Apollinare: " " " " 86	1.990.000	103.104 16.10.44	3310	10.1
68	S.Apollinare: " " " " 87	530.000	103.105 10.10.44	Approvato def.	
69	Cassino: Repairs to Aequeduct	1.930.000	101.340 19.10.44	3335	9.10
70	S.Vittore: Removal of Debris	675.000	101.341 15.10.44	3336	10.1
71	Piedimonte " " "	900.000	101.342 19.10.44	"	"
72	Frosinone: Repairs to buildings of Antigne Pr.	3.200.000		2511	15.
73	" " " " "Cons.Prov.Ec.	1.125.000		2511	15.
74	" " " " "Patern.Inf.	805.000		2511	15.
75	" " " " "ex GIL(Hosp.)	1.900.000	Approv. by	2511	15.
76	" " " " "Uff.Registro	184.000	ACC M/176	2511	15.
77	" " " " " P.O.	395.000	19 October	2511	15.
78	" " " " "Genio Civile	457.000	1944	2511	15.
	" " " " "Schools	820.000		2511	15.

Declassified E.O. 12356 Section 3.3/NND No. 785019

DESCRIZIONE	IMPORTO	Riferim. data approvazione del REG.ENG.	Invio al Ministero		Approvazione del Ministero	
			n°	Data	n°	Data
to Tiburtina road	113.000	101.251	9.10.44	Approv.def.ACC/1 C.C.	Inviata al	
debris from streets	24.000	101.251	" " "	"	"	"
to sewerages	17.000	101.253	" " "	"	"	"
debris from streets	65.000	101.254	" " "	"	"	"
" " "	198.000	101.255	" " "	"	"	"
ra to Prenestina road	20.417	101.256	" " "	"	"	"
" Aqueducts	5.085	101.257	" " "	"	"	"
Debris	77.567	101.258	" " "	"	"	"
to Aqueduct	18.000	101.259	" " "	"	"	"
of Debris	12.495	101.260	" " "	"	"	"
ri Removal of Debris	52.841	101.262	" " "	"	"	"
of Debris	30.420	101.263	" " "	"	"	"
ra to sewerages	67.890	101.264	" " "	"	"	"
of Debris	521.500	101.265	" " "	"	"	"
to Aqueduct	10.000	101.261	" " "	"	"	"
to Seminario	530.000	101.277	7.10.44	"	"	"
Bonds Repairs to Bridge n°71	950.000	103.96	9.10.44	"	"	"
	996.000	101.280	9.10.44	"	"	"
part.)	960.000	101.281	" " "	"	"	"
part.)	995.000	101.282	" " "	"	"	"
part.) -- Removal of debris	942.000	101.283	" " "	"	"	"
part.)	990.000	101.284	" " "	"	"	"
	806.000	103.99	12.10.44	3354	23.10.44	
to bridge n° 20	1.000.000	101.276	13.10.44	Approv.def.ACC/1	Inv.al C.C.	
to Hospital	902.000	101.287	10.10.44	3350	9.10.44	
" "		101.301	12.10.44	3346	30.10.44	
air to buildings of Cons Popol.	4.473.000	103.102	16.10.44	Approv.def.ACC/1	Inv.al C.C.	
airs to bridge n° 74	642.000	103.104	18.10.44	3510	10.11.44	
" " " " 86	1.990.000	103.105	10.10.44	Approvaz.def.ACC/1	Inv.al C.C.	
" " " " 87	530.000	101.340	19.10.44	3939	9.10.44	
	1.939.000	101.341	19.10.44	3536	10.11.44	
to Aqueduct	675.000	101.342	19.10.44	"	" " "	
val of Debris	900.000			2511	15.9.44	
" " "				2511	15.9.44	
ires to buildings of Abbazia Pr.	3.200.000			2511	15.9.44	
" " " "Cons.Prov.Ec.	1.125.000			2511	15.9.44	
" " " "Intern.Inf.	805.000			2511	15.9.44	
" " " "ex GIL(Hosp)	1.900.000			2511	15.9.44	
" " " "UPI.Registry	184.000			2511	15.9.44	
" " " " P.O.	355.000			2511	15.9.44	
" " " "Genio Civile	457.000			2511	15.9.44	
" " " "Schools	820.000			2511	15.9.44	

Oggo. by
ACC M/176
19 October
1944

Declassified E.O. 12356 Section 3.3/NND No. 785019

68	S.Apollinares " " " "	87		530.000	103.139	10.10.44	Appro
69	Casalinos Repairs to Aqueduct			3.930.000	101.340	19.10.44	3535
70	S.Vittoros Removal of Debris			675.000	101.341	19.10.44	3536
71	Piedimonte " " "			900.000	101.342	19.10.44	"
72	Provincial Repairs to buildings of Artigne Pr.			3.200.000			2511
73	" " " "		"Cons.Prov.Bo.	1.125.000			2511
74	" " " "		"Matern.Inf.	805.000			2511
75	" " " "		"ex GIL(Hosp.	1.900.000	Appr. by		2511
76	" " " "		"Dif.Registro	184.000	Acc M/176		2511
77	" " " "		" P.O.	355.000	19 October		2511
78	" " " "		"Genio Civile	457.000	1944		2511
79	" " " "		"Schools	820.000			2511
80	" " " "		"Lab.Igiene	2.300.000			2511
81	" " " "		"Archivio Not.	30.000			2511
82	" " " "		"Electrical Station	5.650.000			2511
83	Sora " houses			6.790.000	101.353	23.10.44	
84	Roccasecca " to aqueduct			560.000	101.353	23.10.44	3720
85	Roccasecca " to Communal building			805.000	101.355	23.10.44	3724
86	Roccasecca " to Schools			600.000	101.357	23.10.44	non pert
87	Fontechiarle " to Bridge n° 83			300.000	103.119	23.10.44	3748
88	Roccasecca " to Bridge n° 85			540.000	103.120	24.10.44	non pert
89	Guarcino " to Bridge n° 9			650.000	103.121	24.10.44	3748
90	Anagni- Paliano - Repairs to Bridge n°17			1.300.000	103.122	24.10.44	3749
91	Morrocavalli - " " " "	30		1.230.000	103.123	24.10.44	3749
92	Pontecorvo " " " "	34		5.000.000	103.129	28.10.44	3860
93	Road deviation with two bridges on place of Melfa bridge n°40			586.000	103.130	31.10.44	3947

Declassified E.O. 12356 Section 3.3/NND No. 785019

" " "	87	530.000	103.105	10.10.44	Adjudicación def.	1/1	Inv. al G.C.
Aqueduct of Dehrin		3.930.000	101.340	19.10.44	3535	9.10.44	
" "		675.000	101.341	19.10.44	3536	10.11.44	
" "		900.000	101.342	19.10.44	"	" " "	
the buildings of Aldeas Inf.		3.200.000			2511	15.9.44	
" "	"Cons.Prov.Es.	1.125.000			2511	15.9.44	
" "	"Intern.Inf.	805.000			2511	15.9.44	
" "	"ex CTI(Hosp)	1.900.000			2511	15.9.44	
" "	"Uff.Registro	184.000			2511	15.9.44	
" "	" P.O.	355.000			2511	15.9.44	
" "	"Genio Civile	457.000			2511	15.9.44	
" "	"Schools	820.000			2511	15.9.44	
" "	"Lab.Igiene	2.300.000			2511	15.9.44	
" "	"Archivio Not.	30.000			2511	15.9.44	
" "	"Electrical Station	5.690.000			2511	15.9.44	
[illegible]		6.790.000	101.353	23.10.44			
the aqueduct		560.000	101.353	23.10.44	3728	16.11.44	
the Communal building		805.000	101.355	23.10.44	3724	16.11.44	
the Schools		600.000	101.357	23.10.44	non pervenuta		
the Bridge n° 83		500.000	103.119	23.10.44	3748	16.11.44	
the Bridge n° 85		540.000	103.120	24.10.44	non pervenuta		
the Bridge n° 9		650.000	103.121	24.10.44	3748	16.11.44	
Repairs to Bridge n°17		1.300.000	103.122	24.10.44	3749	10.11.44	
" " " " 38		1.230.000	103.123	24.10.44	3749	10.11.44	
" " " " 34		5.000.000	103.129	28.10.44	3860	12.11.44	
the two bridges on place of		586.000	103.130	31.10.44	3947	16.11.44	

Oppo. by
ACC 111/176
19 October
1944

Declassified E.O. 12356 Section 3.3/NND No. 785019

MEMO (thru channels)

Lt Col Thompson

To Director P.W.& U. S/C

From : D.Solomon -P.W.Div.

Nov. 14, 1944

Subject - Repairs to Rome University
(and similar Public Bldgs).

Not","Does the building require repair"
But," Is the building required", should determine the action taken!

War damage repairs to buildings comprising Rome University - completed, in work, and proposed or to be in future proposed, will aggregate expenditures of approximately 60,000,000 Lire.

We may assume that such portions of the University as are now or later to be used for actual hospital purposes will have"repair projects"approved after proper screening.

This leaves educational and research fecilities as the balance.

Question One - Shall higher education temporarily take second place to essential housing. The answer is Yes

Question two - If answer to No. 1 is no, then how much of this University is actually presently required for its' minimum needs: it should be borne in mind that the ultimate maximum use of each square foot of usable space should be had, after shifting and rearranging of University activities has been accomplished.

The writers' impression, gained from a number of inspection trips to and through portions of the University, is that less than one-half of the pre war

Declassified E.O. 12356 Section 3.3/NND No. 785019

total of space would be ample for present needs, if and after proper rearrangingof activities were accomplished: further it appears that most of such reduced required space can be found in undamaged or slightly damaged buildings;

This would reduce presently necessary repair works to items of work needed to preserve remainder from additional damage from the elements, plus emergency repair to the spaces to be used actively for University purposes.

Under the presently followed system of instituting repair projects, many buildings enjoying slight use require expensive work. Were compression of activities accomplished, many such apparently necessary jobs could be safely delayed 1-2 or 3 years without hindering University activities appreciably.

I recommend a complete reversal of the present approach to this subject, to wit:

1) Determine the minimum number of buildings that could house the present University activities.

2) Use undamaged or slightly damaged buildings for these activities.

3) Fix these and let the balance wait!

Such a course will release labor, materials, and funds for other more essential uses, preferably Housing Repairs.

I further suggest strong representations to the Ital. Govt to implement this ideas not only as to Rome University, but as to all similar non or partyessential Public Works.

David Solomon
David Solomon

Correct

The above approach is correct. But don't forget that we were only "advice" what to do as that is completely within the control of the Italians.

Ed 6/12

1144B
LV/9

LAZIO UMBRIA REGIONE A.M.G.

Public Works (P) Section

Statistical Summary of month of October 1944

32

WORKS APPROVED	Approval in principle	Definite approval	TOTAL
1. Value of Work definitely approved up to 30 Sept/44	==	==	195.780.540
2. Value of works approved during month of October/44			
a) by Regional Engineer	198.825.796	63.856.925	
b) by Ispettore Comp.	17.436.430		
c) by HQ.ACC.		162.359.231	
		226.216.156	226.216.156
	216.262.226	total up to 31 Oct/44	421.996.696

UNDER APPROVAL IN PRINCIPLE ITEM 2(a) includes:

1) Approvals in principle given for works (in Italian Government

Declassified E.O. 12356 Section 3.3/NND No. 785019

Statistical Summary of month of October 1944

WORKS APPROVED	Approval in principle	Definite approval	TOTAL
1. Value of Work definitely approved up to 30 Sept/44	==	==	195.780.540
2. Value of works approved during month of October/44			
a) by Regional Engineer	198.825.796	63.856.925	
b) by Ispettore Comp.	17.436.430		
c) by HQ.ACC.		162.359.231	
		226.216.156	226.216.156
	216.262.226	total up to 31 Oct/44	421.996.696

UNDER APPROVAL IN PRINCIPLE ITEM 2(a) includes:

1) Approvals in principle given for works (in Italian Government Territory) direct to Ispettore del Genio Civile

2) Recommendations on ACC/1 made to HQ/ACC for works(in AMG Territory)

1762

Declassified E.O. 12356 Section 3.3/NND No. 785019

Declassified E.O. 12356 Section 3.3/NND No. 785019

L A Z I O & U M B R I A REGION A.M.G.
Public Works (P) Section

REPORT ON PROJECTS "approved in principle"

PROVINCE	MONTH	Nº of projects approved in principle		Confirmed by ACC (more than £.1.000.000) and ACC/1 received.
		For ACC confirmation	For Ministero confirmation	
ROMA 84	August	1	15	-
	September	- 18	32 66	-
	October	17	19	-
LITTORIA 41	August	-	4	-
	September	8	7	-
	October	7	15	-
FROSINONE 88	August	4	1	4
	September	8	33	
	October	6	36	
185		51	162	4
213		213		

Declassified E.O. 12356 Section 3.3/NND No. 785019

L A Z I O & U M B R I A REGION A.M.G.
Public Works (P) Section


REPORT ON PROJECTS "approved in principle"


MONTH	Nº of projects approved in principle		Confirmed by ACC (more than £.1.000.000) and ACC/1 received.	Confirmed by Ministry (less than £.1.000.000) and ACC/2 received.
	For ACC confirmation	For Ministero confirmation		
...ber	1	15	-	-
...r	- 18	32 66	-	-
	17	19	-	-
...ber	-	4	-	-
...r	8	7	-	-
	7	15	-	-
...ber	4	1	4	-
...r	8	33		-
	6	36		-
	51	162	4	0
	213			


Declassified E.O. 12356 Section 3.3/NND No. 785019

MAPS AND CHARTS TOO LARGE TO FILM
ON ONE EXPOSURE ARE FILMED CLOCKWISE
BEGINNING IN THE UPPER LEFT CORNER,
LEFT TO RIGHT, AND TOP TO BOTTOM.

SEE DIAGRAMS BELOW.

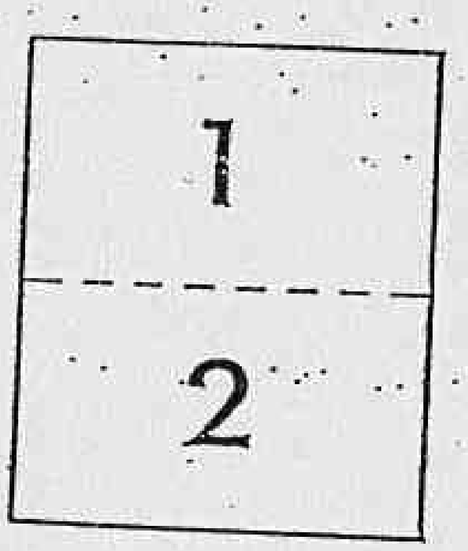

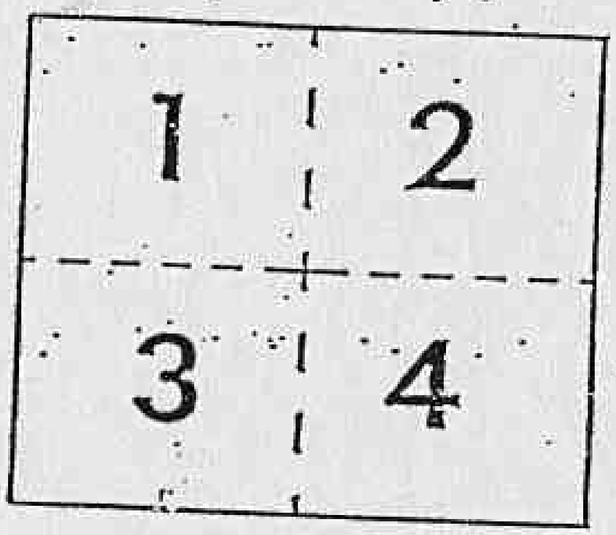

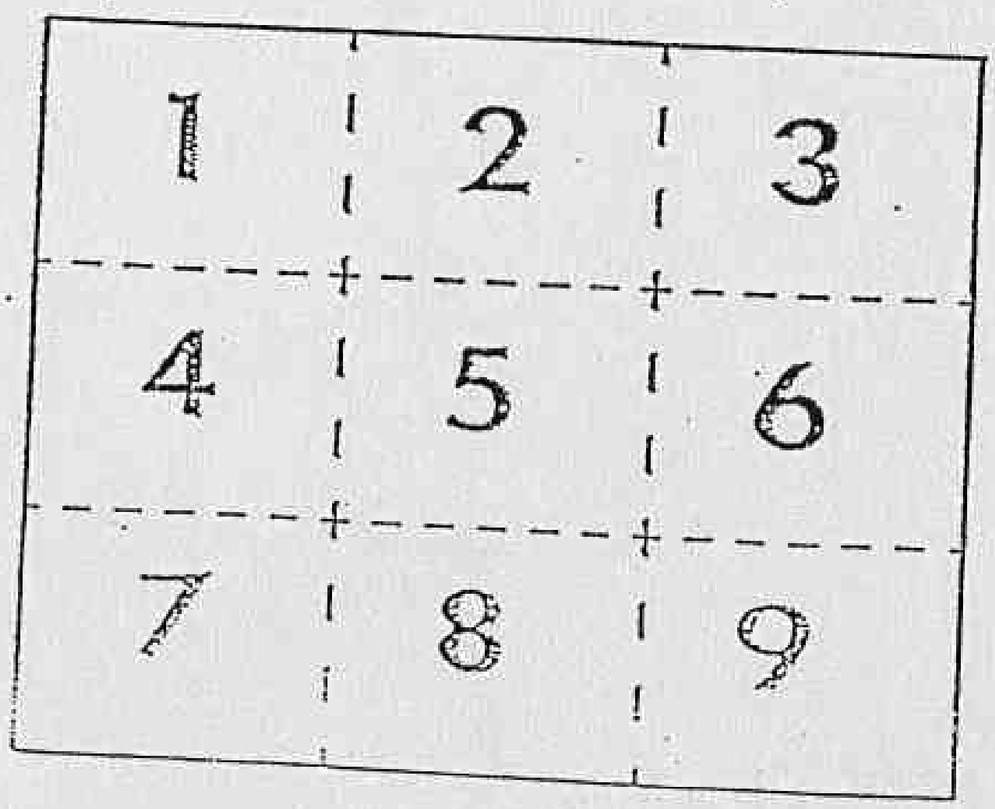

Declassified E.O. 12356 Section 3.3/NND No. 785019

LAZIO-UMBRIA REGION A.M.G. REPORT FOR MONTH OF OCTOBER 44 (P.W. (P))

Works approved during month by H. Q. - A. C. C

Territory All Provinces

REF.	LOCATION	PROJECT AND DESCRIPTION
	FROSINONE PROV.	
101.13	FROSINONE	Repairs Public Buildings
292	CASSINO E PONTECORVO	Specimen block houses
	CASSINO	Re-housing
	LITTORIA PROV.	
101.242	TERRACINA	Specimen block houses
.290	CISTERNA	" " "
.339	FORMIA	" " "
	PERUGIA PROV.	
103.113	CORCIANO	Reconstruction bridge N° 114 - Sht. 13/625.982
114	NURSINA	" " " 185 - " 16/985.600
115	LEONESSA	" " " 52 - " 16/ 19.57
	RIETI PROV.	
102.29	TURANESE ROAD	Reconstruction supporting walls
103.66	TANCIA "	" Bridge n° 15
	ROMA PROV.	
101.321	VALMONTONE	Re-housing
.322	GENZANO	"
.323	FRASCATI	"
.324	LANUVIO	"
.325	TIVOLI	"
.326	VELLETRI	"
.386	ANZIO	"
103.95	SUBALPENSE ROAD	Convertion of barracks in dwellings Reconstruction Bridge N° 10 -(Sht. 17/26.64)
	TERNI PROV.	
101.50	TERNI	Repairs to churches
.65a	"	Civil Hospital
.65b	"	" "
.87	"	Repairs to building labour office
.291	"	" " Aqueduct
103.48	Bdg. N°6 on NERA R.	Road deviation and repair bdg. - 16/78.37
.50	AMERINA ROAD	Reconstr. Bdg. N°10 - 15/53.55
.9	TERNI/CANTALUPO	" S. Valentino Bdg. N°11 - 15/89.39
.52	CIVAGLIA	" Bdg. N° 13 - 16/98.44
.53	MARMORE	" " " 14 - 16/96.36
.54	[illegible]	

Declassified E.O. 12356 Section 3.3/NND No. 785019

UMBRIA REGION A.M.G.

REPORT FOR MONTH OF OCTOBER 44 (P.W. (P))

Works approved during month by H. Q. - A. C. C.

P2(a)

Territory All Provinces

LOCATION	PROJECT AND DESCRIPTION		ESTIMATED COST
FROSINONE PROV.			
FROSINONE	Repairs Public Buildings		14.910.000
CASSINO E PONTECORVO	Specimen block houses		3.237.395
CASSINO	Re-housing	3	33.000.000
LITTORIA PROV.			
TERRACINA	Specimen block houses		2.320.000
CISTERNA	" " "		1.670.000
FORMIA	" " "	3	1.111.341
PERUGIA PROV.			
CORCIANO	Reconstruction bridge Nº 114 - Sht. 13/625.982		2.550.000
NURSINA	" " " 185 - " 16/985.600		1.480.000
LEONESSA	" " " 52 - " 16/ 19.57		2.390.000
RIETI PROV.			
TURANESE ROAD	Reconstruction supporting walls		2.140.000
TANCIA "	" Bridge nº 15	2	1.920.000
ROMA PROV.			
VALMONTONE	Re-housing		13.895.000
GENZANO	"		4.861.500
FRASCATI	"		10.883.000
LANUVIO	"		4.951.000
TIVOLI	"		8.175.000
VELLETRI	"	8	16.245.000
ANZIO	Convertion of barracks in dwellings		4.500.000
SUBALPINE ROAD	Reconstruction Bridge Nº 10 -(Sht. 17/26.64)		4.300.000
TERNI PROV.			
TERNI	Repairs to churches		1.000.000
"	Civil Hospital		500.000
"	" "		5.500.000
"	Repairs to building Labour Office		450.000
"	" Aqueduct		5.500.000
Bdg. Nº6 on NERA R.	Road deviation and repair bdg. - 16/70.37		2.000.000
AMERINA ROAD	Reconstr. Bdg. Nº10 - 15/53.55		7.200.000
TERNI/CANTALUPO	" S. Valentino Bdg. Nº11 - 15/89.39		450.000
CITTAGLIA	" Bdg. Nº 13 - 16/98.44		430.000
NARMORE	" " " 14 - 16/96.36		950.000
[illegible]	"		

Declassified E.O. 12356 Section 3.3/NND No. 785019

101.50	TERNI	Repairs to churches	
.65a	"	Civil Hospital	
.65b	"	" "	
.67	"	Repairs to building Labour Office	
.291	"	" " Aqueduct	
103.48	Bdg.N°6 on NERA R.	Road deviation and repair bdg.	- 16/70.37
.50	AMERINA ROAD	Reconstr. Bdg. N°10	- 15/53.55
.9	TERNI/CANTALUPO	" S. Valentino Bdg. N°11	- 15/89.39
.52	OTRICOLI	" Bdg. N° 13	- 16/98.44
.53	NARNI	" " " 14	- 16/96.36
.54	S. GIROLAMO DITCH	" " " 15	- 16/83.23
.55	CASTELVECCHIO/ALERONA ST.	" S. GIOVANNI Bdg. N°16	- 15/38.65
.57	FOSSO DELL'ABADIA	" Bdg. N° 18	- 15/41.55
.58	PORTANO/TICULLE-FABRO	" " " 19	- 15/42.82
.92	ORVIETO/TORRE S.SEVERO	" "DEL MARCHESE" Bdg.	- 15/43.57

GRAND TOTAL £.

16

1739

Declassified E.O. 12356 Section 3.3/NND No. 785019

	Repairs to churches		1.000.000
	Civil Hospital		500.000
	" "		5.500.000
	Repairs to building Labour Office		450.000
	" " Aqueduct		6.500.000
...A VERA P.	Road deviation and repair bdg.	- 16/78.37	2.000.000
...O	Reconstr. Bdg. N°10	- 15/59.59	7.200.000
...E.EURO	" S. Valentino Bdg. N°11	- 15/89.39	450.000
	" Bdg. N° 13	- 16/98.44	430.000
	" " " 14	- 16/96.36	950.000
...A DITCH	" " " 15	- 16/83.23	1.000.000
...CARDO/MERONA	" S. GIOVANNI Bdg. N°16	- 15/58.65	270.000
...L'ABADIA	" Bdg. N° 18	- 15/44.55	430.000
...ICOLLE-FABRO	" " " 19	- 15/42.82	450.000
...ORRE S.SEVERO	" "DEL MARCHESE" Bdg.	- 15/43.57	700.000
	GRAND TOTAL	£.	162.359.231

Declassified E.O. 12356 Section 3.3/NND No. 785019

Lazio-Umbria Region AMG.

REPORT for MONTH of OCTOBER /44 (P.W. (P)

Works approved during month at Regional level

A.M.G. Territory VITERBO Province

Approved by REGIONAL ENGINEER Limit L. 1.000.000

(No controlled materials)

REF.	LOCATION	PROJECT and DESCRIPTION	ESTIMAT
		a) Water supply	
101.343	VITERBO	Repairs to Aqueduct	760.0
		Total a)	L. 760.0
		b) Repairs buildings & Rehousing	
		N I L	
		Total b)	
		c) other works (excluding roads & bridges)	
101.248	VITERBO Prov.	Debris removal to Marta River	500.
101.363	ARLENA, CANINO, TESSENANO	Removal of debris " " "	280.
101.364	BAGNOREGGIO, CELLENO CASTIGLIONE	" " "	220.
101.365	BIEDA, VEIANO	" " "	480.
101.366	CANEPINA, VALLERANO	" " "	440.
101.367	CAPRANICA, SUTRI	" " "	480.
101.368	CAPRAROLA, VIGNA-NELLO	" " "	300.
101.369	CARBOGNANO, CORCANO FABBRICA	" " "	260.
101.370	A CIVITACASTELLANA	" " "	1.000.
101.371	FARNESE, ISCHIA VALENTANO	" " "	340
101.372	MONTALTO di CASTRO	" " "	250
101.373	MONTEFIASCONE	" " "	600
[illegible]	ORTE	" " "	[illegible]

Declassified E.O. 12356 Section 3.3/NND No. 785019

ria Region AMG.

REPORT for MONTH of OCTOBER /44 (P.W. (P)

Works approved during month at Regional level

G. Territory VITERBO Province

by REGIONAL ENGINEER Limit L. 1.000.000

(No controlled materials)

LOCATION	PROJECT and DESCRIPTION	ESTIMATED COST
VITERBO	a) Water supply Repairs to Aqueduct	760.000
	Total a)	L. 760.000
	b) Repairs buildings & Rehousing	
	N I L	
	Total b)	
	c) other works (excluding roads & bridges)	
VITERBO Prov.	Debris removal to Marta River	500.000
ARLENA, CANINO,	Removal of debris	
TESSENANO	" " "	280.000
BAGNOREGGIO, CELLENO		
CASTIGLIONE	" " "	220.000
BIEDA, VEIANO	" " "	480.000
CANEPINA, VALLERANO	" " "	440.000
CAPRANICA, SUTRI	" " "	480.000
CAPRAROLA, VIGNA-NELLO	" " "	300.000
CARBOGNANO, CORCANO		
FABBRICA	" " "	260.000
A CIVITACASTELLANA	" " "	1.000.000
FARNESE, ISCHIA		
VALENTANO	" " "	340.000
MONTALTO di CASTRO	" " "	250.000
MONTEFIASCONE	" " "	600.000
CRTE	" " "	1.000.000

Declassified E.O. 12356 Section 3.3/NND No. 785019

101.367		CAPRANICA, SUTRI	"	"	"			480.0
101.368		CAPRAROLA, VIGNANELLO	"	"	"			300.0
101.369		CARBOGNANO, CORCANO FABBRICA	"	"	"			260.0
101.370	A	CIVITACASTELLANA	"	"	"			1.000.0
101.371		FARNESE, ISCHIA VALENTANO	"	"	"			340.0
101.372		MONTALTO di CASTRO	"	"	"			250.0
101.373		MONTEFIASCONE	"	"	"			600.0
101.374		ORTE	"	"	"			1.000.0
101.375		RONCIGLIONE	"	"	"			450.0
101.376		SORIANO nel CIMINO	"	"	"			780.0
101.377		TARQUINIA, TUSCANIA	"	"	"			380.0
101.378		VETRALLA	"	"	"			840.0
101.379		VITERBO	Removal of debris			(I scheme)		1.000.0
101.380		"	"	"	"	(II scheme)		860.0
101.381		"	"	"	"	(III scheme)		975.0
101.382		"	"	"	"	(IV scheme)		430.0
101.383		"	"	"	"	(V scheme)		660.0
101.384		"	"	"	"	(VI scheme)		940.0
						Total c)		13.465.0
			d) non military road & bridges					
103.77		VITERBO/CASTIGLIONE	Repair Bridge N°38			(MR. 15/445.516)		250.0
103.78		"	"	"	" 39	(" 15/470.536)		390.0
103.79		SORANESE Road	"	"	" 48	(" 15/204.566)		388.0
103.80		CIMINA Road	"	"	" 28	(" 15/596.040)		350.0
103.81		VITERBO/TUSCANIA	"	"	" 33	(" 15/309.270)		1.000.0
103.82		ORIOLESE Road	"	"	" 20	(" 15/016.44°)		850.0
103.83		RONCIGLIONESE Road	"	"	" 29	(" 15/590.140)		400.0
103.84		DEVIATION of CASSIA	"	"	" 22	(" 15/516.060)		1.000.0
103.85		BASSANESE Road	"	"	" 21	(" 15/48.04)		220.0
103.86		ORIOLESE Road	"	"	" 47	(" 15/45.01)		500.0
						Total d)		5.348.0
						GRAND TOTAL(a+b+c+d)		19.573.0

Declassified E.O. 12356 Section 3.3/NND No. 785019

	CAPRANICA, SUTRI	"	"	"	480.000
	CAPRAROLA, VIGNANELLO	"	"	"	300.000
	CARBOGNANO, CORCANO	"	"	"	260.000
	FABBRICA	"	"	"	1.000.000
A	CIVITACASTELLANA	"	"	"	340.000
	FARNESE, ISCHIA	"	"	"	250.000
	VALENTANO	"	"	"	600.000
	MONTALTO di CASTRO	"	"	"	1.000.000
	MONTEFIASCONE	"	"	"	450.000
	ORTE	"	"	"	780.000
	RONCIGLIONE	"	"	"	380.000
	SORIANO nel CIMINO	"	"	"	840.000
	TARQUINIA, TUSCANIA	"	"	"	1.000.000
	VETRALLA	"	"	"	860.000
	VITERBO	Removal of debris		(I scheme)	975.000
	"	"	"	(II scheme)	430.000
	"	"	"	(III scheme)	660.000
	"	"	"	(IV scheme)	940.000
	"	"	"	(V scheme)	
		"	"	(VI scheme)	
			Total c)		13.465.000
	d) non military road & bridges				
	VITERBO/CASTIGLIONE	Repair Bridge N°38 (MR. 15/445.516)			250.000
	"	"	" 39 (" 15/470.536)		390.000
	SORANESE Road	"	" 48 (" 15/204.566)		388.000
	CIMINA Road	"	" 28 (" 15/596.040)		350.000
	VITERBO/TUSCANIA	"	" 33 (" 15/309.270)		1.000.000
	ORIOLESE Road	"	" 20 (" 15/016.440)		850.000
	RONCIGLIONESE Road	"	" 29 (" 15/590.140)		400.000
	DEVIATION of CASSIA	"	" 22 (" 15/516.060)		1.000.000
	BASSANESE Road	"	" 21 (" 15/48.04)		220.000
	ORIOLESE Road	"	" 47 (" 15/45.01)		500.000
			Total d)		5.348.000
		GRAND TOTAL (a+b+c+d)			19.573.000

34

Declassified E.O. 12356 Section 3.3/NND No. 785019

TERNI (cont'd)

D) Non military road and bridges

102.26	AMERINA ROAD (1st PART)	Road surface repair	
27	" " (2nd ")	" " "	
28	BASCHI COMUNE	Reactivation communal road	
31	SALA ROAD 1st PART	Road repair	
32	" " 2nd "	" "	
33	" " 3rd "	" "	
34	" " 4th "	" "	
35	ORVIETO/ALERONA SCALO	" "	
37	LEONE ROAD	" "	
38	TAMBURINO ROAD	" "	
39	CORTA DELLA STAZIONE, ORVIETO	" "	
40	MARCHIGIANO ROAD	" "	
41	COMUNE CASTELVISCARDO	" "	
42	COMUNAL ROADS OF BADIA, PUGNVIAGGIO COLONNETTA	" "	
103.49	CICLIANO	Repair Bdg n.7	Sht 15/494.392
56	TERNI BAGNOREGGIO	" " n.17	Sht 15/45.53
69	TORRE S.SEVERO	" " FATATA" ON MONTAC-CHIONE R	Sht 15/47.57
70	MONTERUBIAGLIO/ORVIETO	" " "PONTE ROSSO"	Sht 15/42.62
71	COMUNE ORVIETO	" " Bdg.On.ABBADIA Ditch	Sht 15/46.58
72	AMELIA/PENNA	" " Bdg.	Sht 15/68.37
73	" "	" "Barnaba" Bdg.	Sht 15/68.37
74	" "	" "Cenciolello" Bdg.	Sht 15/68.37
75	ORVIETO COMUNE	" Bdg On Chiani Tor.	Sht 15/464.630
76	" "	" Bdg On Fosso Grande	Sht 15/77.37
91	FABBRO/FICULLE	" Bdg n.20	Sht 15/395.760
93	NARNI SCALO/AMELIA	" Bdg n.8	Sht 16/75.38
100	FABBRO/CITTA' DI PIEVE	" "Poggiovalle" Bdg	Sht 15/36.80
103	COMUNE PORANO	" "Molinella" Bdg	Sht 15/44.55

TOTALE

GRAND TOTAL (a+b+c+d) L.

Declassified E.O. 12356 Section 3.3/NND No. 785019

TERNI (Cont'd)

D) Non military roads and bridges

	Road surface repair		70.000
	" " "		140.000
	Reactivation communal road		50.000
	Road repair		960.000
	" "		935.000
	" "		1.000.000
	" "		1.000.000
	" "		990.000
	" "		100.000
	" "		100.000
	" "		100.000
	" "		70.000
	" "		950.000
	" "		1.000.000
Repair Bdg n.7		Sht 15/494.392	300.000
" " n.17		Sht 15/45.53	105.000
" " "PATATA" ON MONTAC= ORIONE R		Sht 15/47.57	192.000
" " "PONTE ROSSO"		Sht 15/42.62	82.000
" " Bdg.On.ABBADIA Ditch		Sht 15/46.58	77.000
" " Bdg.		Sht 15/68.37	151.000
" "Barnaba" Bdg.		Sht 15/68.37	180.000
" "Cenciolello" Bdg.		Sht 15/68.37	110.000
" Bdg On Chiani Tor.		Sht 15/464.630	700.000
" Bdg On Fosso Grande		Sht 15/77.37	550.000
" Bdg n.20		Sht 15/395.760	380.000
" Bdg n.9		Sht 16/75.38	445.000
" "Poggiovelle" Bdg		Sht 15/36.80	560.000
" "Molinella" Bdg		Sht 15/44.55	300.000
	TOTALE		11.597.000
	GRAND TOTAL (a+b+c+d)	L.	34.898.925

A ROAD (1st PART)
" (2nd ")
COMUNE
OAD 1st PART
" 2nd "
" 3rd "
" 4th "
D/ALERONA SCALO
ROAD
INO ROAD
DELLA STAZIONE,
O
HIANO ROAD
CASTELVISCARDO
L ROADS OF BADIA,
GGIO COLONNETTA
O
AGNOREGGIO
.SEVERO
BIAGLIO/ORVIETO
ORVIETO
PENNA
"
"
COMUNE
"
TICULIE
CALO/AMELIA
CITTA' DI PIEVE
ORANO

Declassified E.O. 12356 Section 3.3/NND No. 785019

ezio-Umbria Region A.M.G.

A.M.G. Territory

REPORT for MONTH of October 1944 (Public Works) P.W.

Works approved during month at Regional Level

Territory T E R N I Province

Approved by Regional Engineer

Limit L
(no contr

REF.	L O C A T I O N	P R O J E C T A N D D E S C R I P T I O N
		a) Water supply
		Nil
		TOTAL a)
		b) Repairs to buildings - Re-housing
101.50/1,2,3	T E R N I	Repairs to Church S.Francesco
	"	" " " S.Antonio
	"	" " Cattedrale del Duomo
55/1,2	"	" " Civil Hospital (1 and 2 Part)
185	"	" " Covitto Umberto I
187	"	" " Palazzo del Governo
189	ORVIETO	" " School
190	T E R N I	" " Asilo Infantile
191	"	" " Caserma Vigili del fuoco
192	STRADA MARCIANESE	" " Casa Cantoniera
193	ORVIETO	Rural schools resettlement
197	TERNI	Repairs to " Laboratorio d'Igiene "
198	ORVIETO	" " School at Penano
202	TERNI	" " Casa del mutilato
204	"	" " "Ospizio Colle dell'Oro"
205	"	" " Caserma Carabinieri
206	"	" " Church at S.Maria degli Spiazzi
232	"	" " dwellings Giardino n.1
233	"	" " " " n.2
234	"	" " " " n.3
235	"	" " " " n.4
236	"	" " " " n.5
237	"	" " " " n.6
238	"	" " " " n.7
239	"	" " " " n.8
240	"	" " Hospital "Le Grazie"
266	BASCHI	" " Casa Cantoniere
267	TERNI	" " Appartement at "Istituto Tecnico"
270	"	" " " " "Banca d'Italia"
271	"	" " Dispensario Antitubercolare
87	"	" " Buildings Labour Office
279	MONTECASTRILLI	" " Schools
285	TERNI	" " Buildings 1° Scheme
286	"	" " 2
287	"	" " 3
288	"	

Declassified E.O. 12356 Section 3.3/NND No. 785019

gion A.M.G.

y

REPORT for MONTH of . . . . . October 1944 . . . . . (Public Works) P.W.(P)

Works approved during month at Regional Level

Territory T E R N I Province

ional Engineer

Limit L.1.000.000
(no controlled materials)

LOCATION	PROJECT AND DESCRIPTION	ESTIMATED COST
	a) Water supply	
	Nil	
	TOTAL a)	L. —
	b) Repairs to buildings - Re-housing	
TERNI	Repairs to Church S.Francesco	460.000
"	" " " S.Antonio	250.000
"	" Cattedrale del Duomo	290.000
"	" Civil Hospital (1 and 2 Part)	500.000
"	" Covitto Umberto I	100.000
"	" Palazzo del Governo	138.000
RIETO	" " School	32.000
TERNI	" " Asilo Infantile	200.000
"	" Caserma Vigili del fuoco	106.000
A MARCIANESE	" " Casa Cantoniera	55.000
PO	Rural schools resettlement	45.000
	Repairs to " Laboratorio d'Igiene "	150.000
PO	" " School at Penano	10.000
	" " Casa del mutilato	100.000
	" " "Capizio Colle dell'Oro"	43.000
	" " Caserma Carabinieri	85.000
	" " Church at S.Maria degli Spiazzi	41.600
	" " dwellings Giardino n.1	185.000
	" " " " n.2	180.000
	" " " " n.3	170.000
	" " " " n.4	165.000
	" " " " n.5	185.000
	" " " " n.6	195.000
	" " " " n.7	180.000
	" " " " n.8	190.000
	" " Hospital "Le Grazie"	100.000
	" " Casa Cantoniera	1.325
	" " Appartament at "Istituto Tecnico"	22.000
	" " " " Banca d'Italia"	200.000
	" " Dispensario Antitubercolare	105.000
	" " Buildings Labour Office	450.000
ASTRILLI	" " Schools	550.000
	" " Buildings 1° Scheme	1.000.000
	" " 2	1.000.000
	" " 3	1.000.000

Declassified E.O. 12356 Section 3.3/NND No. 785019

236	"	"	"	"	"	n.4	
237	"	"	"	"	"	n.5	
238	"	"	"	"	"	n.6	
239	"	"	"	"	"	n.7	
240	"	"	"	"	"	n.8	
266	PASCHI	"	"	Hospital "Le Grazie"			
267	TERNI	"	"	Case Cantoniere			
270	"	"	"	Appartement at "Istituto Tecnico"			
271	"	"	"	" " " Banca d'Italia"			
87	"	"	"	Dispensario Antitubercolare			
279	MONTECASTRILLI	"	"	Buildings Labour Office			
285	TERNI	"	"	Schools			
286	"	"	"	Buildings 1° Scheme			
287	"	"	"	2			
288	"	"	"	3			
289	"	"	"	4			
304	"	"	"	5			
305	"	"	"	in Viale del Cassero 1° Scheme			
306	"	"	"	" " " " II "			
307	"	"	"	" " " " III "			
308	"	"	"	" " " " IV "			
309	"	"	"	" " " " V "			
310	"	"	"	" " " " VI "			
							TOTAL B)
101.173÷178	TERNI PROVINCE	C) Other Works (excluding roads a bridges)					
184	TERNI	Removal of debris in various communes (6 schemes)					
186	"	Repair to sewer system					
188	ORVIETO	Debris removal from Palazzo del Governo					
199	TERNI	Repair to fontana					
200	"	Removal debris at Quartiere Battisti					
201	"	" " " " Fonderia					
203	"	" " " " Giardino					
268	FOSSO CAVALLOCCI	" " " " Flaminio					
269	TORRENTE LAIA	" "					
311÷315	TERNI	" "					
316,317	"	" " (5 schemes)					
318÷320	"	Repairs to sewers (2 schemes)					
		Removal of Debris (3 ")					
							TOTAL C)

Declassified E.O. 12356 Section 3.3/NND No. 785019

	" " " " n.4	165.000
	" " " " n.5	185.000
	" " " " n.6	195.000
	" " " " n.7	180.000
	" " " " n.8	190.000
	" " Hospital "Le Grazie"	100.000
	" " Casa Cantoniere	1.325
	" " Appartement at "Istituto Tecnico"	22.000
	" " " " " Banco d'Italia"	200.000
	" " Dispensario Antitubercolare	105.000
	" " Buildings Labour Office	450.000
CASTRILLI	" " Schools	550.000
	" " Buildings 1° Scheme	1.000.000
	" " 2	1.000.000
	" " 3	1.000.000
	" " 4	1.000.000
	" " 5	500.000
	" " In Viale del Cassero I° Scheme	100.000
	" " " " " " II "	100.000
	" " " " " " III "	80.000
	" " " " " " IV "	95.000
	" " " " " " V "	12.000
	" " " " " " VI "	7.000
	" " " " " " VII "	16.000
	TOTAL B)	10.423.925
	C) Other Works (excluding roads a bridges)	
ROVINCE	Removal of debris in various communes (6 schemes)	1.200.000
	Repair to sewer system	900.000
	Debris removal from Palazzo del Governo	160.000
	Repair to fontana	18.000
	Removal debris at Quartiere Battisti	100.000
	" " " " Fonderia	100.000
	" " " " Giardino	100.000
	" " " " Flaminio	100.000
VALLOCCI	" "	200.000
LAIA	" "	200.000
	" " (5 schemes)	5.000.000
	Repairs to sewers (2 schemes)	1.800.000
	Removal of Debris (3 ")	3.000.000
	TOTAL C)	12.878.000

P.T.O

57

Declassified E.O. 12356 Section 3.3/NND No. 785019

LAZIO-UMBRIA REGION A.M.G.

Report for Month of October 1944
Works approved during month at Regional Level

Territory R O M A Province

Approved by Comp.Insp. Genio Civile

Limit L. 500.000 (no control.

REF	L O C A T I O N	PROJECT AND DESCRIPTION
		a) Water supply
	LANUVIO	Sistemazione acquedotto
	FRASCATI	Riparazione acquedotto Algidosia
		TOTAL A)
		b) Repairs to buildings and -Re-housing
	CAVE	Riparazione Chiesa Parrocchiale
	CAMPAGNO	" " S.Giovanni
	PALESTRINA	Sistemazione locali Convento dei Cappuccini
	FRASCATI	" palazzo vescovile
	GENAZZANO	Riparazione tetto Chiesa Parrocchiale
	CIVITAVECCHIA	Sistemazione fabbricato P.Galaletta
	PALESTRINA	" locali da adibire a scuole
	ARICCIA	Riparazione edificio scolastico
		TOTAL B)
		c) Other works (excluding roads and bridges)
	ZAGAROLO	Sgombro macerie nell'abitato
	ROMA	" " in località La Storta
	GALLICANO	" " nell'abitato
	S.GREGORIO DI S.	" " fabbricato in Piazza Brancaccio n.1
	ZAGAROLO CAVE	" " nel Corso V.E.
	ROMA	Pagamento operai al ricupero,Bonifica di Ostia
	CAVE	Sgombro nell'abitato
	CAVE	" strade e piazze
	VELLETRI	" di V.Basilio Magni
	FRASCATI	" lungo Via Villa Falconiera
	FRASCATI	" macerie ,stabile dei RR.PP.
	ZAGAROLO	" " fabbricati nell'abitato
	CAPRANICA PRENESTINA	" " " "
	FIUMICINO	Riparazione Molo Nord del Porto Canale
	VELLETRI	Sgombro macerie Via Paolina
	FIUMICINO	Riparazione Molo Sud del Porto Canale
	CIVITAVECCHIA	Manutenzione spese portuali
	MENTANA	Sgombro fabbricati Via 3 Novembre
	FIUMICINO	" macerie
	CASTEL S.PIETRO	" nell'abitato
	ARICCIA	" "
	CIVITAVECCHIA	Riparazione fognature

Declassified E.O. 12356 Section 3.3/NND No. 785019

CON A.M.

Report for Month of October 1944
Works approved during month at Regional Level

Territory R O M A Province

Limit L. 500.000 (no control.mat.)

mp.Insp. Genio Civile

OCATION	PROJECT AND DESCRIPTION	ESTIMATED COST
VIO	a) Water supply	
CATI	Sistemazione acquedotto	150.000
	Riparazione acquedotto Algidosia	500.000
	TOTAL A)	650.000
	b) Repairs to buildings and -Re-housing	
AGNO	Riparazione Chiesa Parrocchiale	360.000
STRINA	" " S.Giovanni	495.000
ATI	Sistemazione locali Convento dei Cappuccini	470.000
ZANO	" palazzo vescovile	200.000
AVECCHIA	Riparazione tetto Chiesa Parrocchiale	335.000
STRINA	Sistemazione fabbricato P.Galametta	200.000
IA	" locali da adibire a scuole	220.000
	Riparazione edificio scolastico	159.000
	TOTAL B)	2.439.000
	c) Other works (excluding roads and bridges)	
OLO	Sgombro macerie nell'abitato	325.000
CANO	" " in località La Storta	225.000
NORTO DI S.	" " nell'abitato	150.000
LO CAVE	" " fabbricato in Piazza Brancaccio n.1	200.000
	" " nel Corso V.E.	385.000
	Pagamento operai al ricupero,Bonifica di Ostia	200.000
	Sgombro nell'abitato	450.000
RI	" strade e piazze	276.000
TI	" di V.Basilio Magni	126.000
TI	" lungo Via Villa Falconiera	150.000
LO	" macerie ,stabile dei RR.PP.	110.000
ICA PRENESTINA	" " fabbricati nell'abitato	240.000
INO	" " " "	490.000
RI	Riparazione Molo Nord del Porto Canale	200.000
NO	Sgombro macerie Via Paolina	195.000
ECCHIA	Riparazione Molo Sud del Porto Canale	300.000
	Manutenzione spese portuali	365.000
NO	Sgombro fabbricati Via 3 Novembre	440.000
S.PIETRO	" macerie	200.000
	" nell'abitato	40.000
ECCHIA	" "	70.330
	Riparazione fognature	200.000

Declassified E.O. 12356 Section 3.3/NND No. 785019

	CAPRANICA PRENESTINA	" " " "
	FIUMICINO	Riparazione Molo Nord del Porto Canale
	VELLETRI	Sgombro macerie Via Paolina
	FIUMICINO	Riparazione Molo Sud del Porto Canale
	CIVITAVECCHIA	Manutenzione spese portuali
	MENTANA	Sgombro fabbricati Via 3 Novembre
	FIUMICINO	" macerie
	CASTEL S.PIETRO	" nell'abitato
	ARICCIA	" "
	CIVITAVECCHIA	Riparazione fognature
		TOTAL c)
	ROMA	d) Non military roads and bridges
	"	Sistemazione strada per ricollegare Ariccia alla V.Appia
	"	Riparazione strada Tiberina Km.16 - Km.24
	"	Ricostruzione ponte al Km.24.960, Maremmana 1
	"	" chiavicotto Km. 1,090, Tivoli - S.Polo
	"	" ponticello Km. 13,800, Tiburtine - S.Angelo M
	"	Strada Sambuci -ponte Km. 7,313
	"	Ricostruzione ponticello Km. 0,748, Empolitana 2°
	"	Riparazione cantoniera n.26, Maremmana 2°
	"	Ricostruzione chiavicotto e fogne Km.11.840-Tivoli S.Paolo Marcellin
	"	Riparazione cantoniera Km. 2,000 Montelibretti
	"	Ricostruzione ponticelli Km. 13.500, Tiburtina S.Angelo -Mentana
	"	" Km. 7.500 " " "
	"	Strada Subiacense, ripristino tratto fra la statale Tiburtina Bivio Apultina
	"	Ricostruzione chiavicotto Km. 10,025, Tiburtina S.Angelo Mentana
	"	" Km. 0,300, Nerolo-Montorio
	"	Riparazione ponte Km. 9.355, Prenestina
	"	Ricostr.ponticello Km.32.000, Palombarense
	"	Riparazione cantoniera Km. 59.000, Subiacense
	"	Manutenzione capo strada alla strada dei Laghi
	"	Ricostruzione due manufatti, S.Cavigranese
	"	Sgombro materiali entro Monte Canico
	"	Ricostruzione chiavicotto Km. 3.095, S.Traianno
	"	" Km. 3.398 S.Traianero
	"	muro di sostegno Km.2,250, Quieifiglione
		TOTAL D)
		GRAND TOTAL (a+b+c+d) . . . . £

Declassified E.O. 12356 Section 3.3/NND No. 785019

RANICA PRENESTINA	" " " "	490.000
ICCINO	Riparazione Molo Nord del Porto Canale	200.000
LETRI	Sgombro macerie Via Paolina	195.000
ICINO	Riparazione Molo Sud del Porto Canale	300.000
ITAVECCHIA	Manutenzione spese portuali	365.000
TANA	Sgombro fabbricati Via 3 Novembre	440.000
ICINO	" macerie	200.000
EL S.PIETRO	" nell'abitato	40.000
CCIA	" "	70.330
ITAVECCHIA	Riparazione fognature	200.000
	TOTAL c)	5.347.000
	d) Non military roads and bridges	
	Sistemazione strada per ricollegare Ariccia alla V.Appia	300.000
	Riparazione strada Tiburtina Km.16 - Km.24	50.000
	Ricostruzione ponte al Km.21.960, Maremmana 1	150.000
	" chiavicotto Km. 1,090, Tivoli - S.Polo	99.000
	" ponticello Km. 13,800, Tiburtine - S.Angelo R	125.000
	Strada Sambuci -ponte Km. 7,393	100.000
	Ricostruzione ponticello Km. 0,748, Empolitana 2°	140.000
	Riparazione cantoniere n.26, Maremmana 2°	43.000
	Ricostruzione chiavicotto e fogne Km.14.840-Tivoli S.Paolo Marcellina	80.000
	Riparazione cantoniere Km. 2,000 Montelibretti	58.000
	Ricostruzione ponticelli Km. 13.500, Tiburtina S.Angelo -Mentana	129.000
	" " Km. 7.600 " " "	108.000
	Strada Subiacense, ripristino tratto fra la statale Tiburtina Bivio Apulina	28.000
	Ricostruzione chiavicotto Km. 10,025, Tiburtina S.Angelo Mentana	56.000
	" " Km. 0,300, Nerola-Montorio	50.000
	Riparazione ponte Km. 9.365, Prenestina	160.000
	Ricostr.ponticello Km.32.000, Palombarense	100.000
	Riparazione cantoniera Km. 59.000, Subiacense	41.800
	Manutenzione capo strade alla strada dei Laghi	200.000
	Ricostruzione due manufatti, S.Cavigrenose	110.000
	Sgombro materiali ebtro Monte Cavico	35.000
	Ricostruzione chiavicotto Km. 3.095, S.Trainara	109.800
	" " Km. 3.398 S.Trainara	126.000
	" muro di sostegno Km.2,250, Quietifiglioco	250.000
	TOTAL D)	2.658.600
	GRAND TOTAL (subsid) . . . . .£	11.094.930

56

Declassified E.O. 12356 Section 3.3/NND No. 785019

REGION LAZIO & UMBRIA A.M.G.

REPORT FOR MONTH of O C T O B E R / 1944. (P.W. (P.)

Works approved during month at Regional Level

I T A L I A N G O V E R N M E N T TERRITORY R O M A Province

Approved by REGIONAL ENGINEER LIMIT £. 1,000.000

(no controlled material

REF.	LOCATION	PROJECT and DESCRIPTION	ES
		a) Water supply	
		NIL	
		Total a)	
	CIVITAVECCHIA	b) Repairs to buildings and Re-housing	
101.221	"	Repairs to school at Via Buonarroti	
222	"	" dwelling	
278	ALBANO	" to Civil Hospital	
298	ROCCA DI PAPA	" to Chiesa Parrocchiale	
327	LANUVIO	Erections wood's booths	
332	VALMONTONE	" " "	
359	Velletri	Repairs to prisons	
		Total b)	
		c) Other works (excluding roads and bridges)	
101.179/180	GROTTAFERRATA	demolitions and removal of debris (2 schemes)	
101.181/183	FRASCATI	" " " " " (3 schemes)	
101.219	ALBANO	repairs to sewerage system	
101.220	ROCCA DI PAPA	" " " "	
101.223	FRASCATI	Demolitions and removal of debris (1 scheme)	
101.224	"	" " " " " (2 schemes)	
101.225	"	" " " " " (3 schemes)	
101.228	PALESTRINA	Demolitions and removal debris	
101.229	GROTTAFERRATA	" " " "	
101.230	MONTELANICO	" " " "	
101.231	NETTUNO	" " " "	
101.241	CIAMPINO		
101.243	SUBIACO	" " " " to Mon.of Scolastico	
101.244	ARDEA - PRATICA - POMEZIA	" " " "	
101.245	FIANO ROMANO	" " " "	

Declassified E.O. 12356 Section 3.3/NND No. 785019

LAZIO & UMBRIA A.M.G.

REPORT FOR MONTH of O C T O B E R / 1944. (P.W. (P.)

Works approved during month at Regional Level

I T A L I A N G O V E R N M E N T TERRITORY R O M A Province

Approved by REGIONAL ENGINEER LIMIT £. 1,000.000

(no controlled materials)

LOCATION	PROJECT and DESCRIPTION	ESTIMATED COST
	a) Water supply	
	NIL	
	Total a)	
CIVITAVECCHIA	b) Repairs to buildings and Re-housing	
"	Repairs to school at Via Buonarroti	825.000
"	" dwelling	650.000
ALBANO	" to Civil Hospital	819.000
ROCCA DI PAPA	" to Chiesa Parrocchiale	69.480
LANUVIO	Erections wood's booths	507.000
VALMONTONE	" " "	950.000
Velletri	Repairs to prisons	1,000.000
	Total b)	4,820.480
	c) Other works (excluding roads and bridges)	
GROTTAFERRATA	demolitions and removal of debris (2 schemes)	1,294.000
FRASCATI	" " " " " (3 schemes)	2,652.000
ALBANO	repairs to sewerage system	992.000
ROCCA DI PAPA	" " " "	192.000
FRASCATI	Demolitions and removal of debris (1 scheme)	993.000
"	" " " " " (2 schemes)	930.000
"	" " " " " (3 schemes)	940.000
PALESTRINA	Demolitions and removal debris	940.000
GROTTAFERRATA	" " " "	735.000
MONTELANICO	" " " "	610.000
NETTUNO	" " " "	990.000
CIAMPINO		
SUBIACO	" " " " to Mon.of Scolastico	970.000
ARDEA - PRATICA - POMEZIA	" " " "	992.000
FIANO ROMANO	" " " "	760.000

Declassified E.O. 12356 Section 3.3/NND No. 785019

101.219	ALBANO	repairs to sewerage system	
101.220	ROCCA DI PAPA	" " " "	
101.223	FRASCATI	Demolitions and removal of debris (1 scheme)	
101.224	"	" " " " " (2 schemes)	
101.225	"	" " " " " (3 schemes)	
101.228	PALESTRINA	Demolitions and removal debris	
101.229	GROTTAFERRATA	" " " "	
101.230	MONTELANICO	" " " "	
101.231	NETTUNO	" " " "	
101.241	CIAMPINO		
101.243	SUBIACO	" " " " to Mon.of Scolastico	
101.244	ARDEA - PRATICA - POMEZIA	" " " "	
101.245	FIANO ROMANO	" " " "	
101.300	TIVOLI	Demolitions and removal of debris	
101.328	GENZANO	" " " " "	
101.329	"	" " " " "	
101.330	CIVITAVECCHIA	Repairs to sewers	
101.331	"	" " "	
		Total c)	
d)	non military roads and bridges.		
102.36	PRENESTINA ROAD	LANDSLIP near "CAVE"	
103.109	BRACIANESE 2°	Repairs to ~~building~~ Bridge at km 56,600 Sht/17/28.96	
103.110	"	Repairs to ~~building~~ Bridge N°5 at km 72,300 sht 17/910	
		Total d)	
		Grand total (a + b + c + d)	

Declassified E.O. 12356 Section 3.3/NND No. 785019

		repairs to sewerage system	992.000
ALBANO	"	" " " "	192.000
ROCCA DI PAPA	"	Demolitions and removal of debris (1 scheme)	993.000
FRASCATI	"	" " " " " (2 schemes)	930.000
"	"	" " " " " (3 schemes)	940.000
"	"	" " " "	940.000
PALESTRINA	"	Demolitions and removal debris	735.000
GROTTAFERRATA	"	" " " "	610.000
MONTELANICO	"	" " " "	990.000
NETTUNO	"		
CIAMPINO	"	" " " " to Mon.of Scolastico	970.000
SUBIACO	"	" " " "	992.000
ARDEA - PRATICA - POMEZIA	"	" " " "	760.000
FIANO ROMANO	"	Demolitions and removal of debris	1,000.000
TIVOLI	"	" " " " "	910.000
GENZANO	"	" " " " "	800.000
"	"		800.000
CIVITAVECCHIA	"	Repairs to sewers	610.000
"	"	" " "	
		Total c)	18,110.000
		d) non military roads and bridges.	
		LANDSLIP near "CAVE"	1,050.000
PRENESTINA ROAD		Repairs to ~~building~~ Bridge at km 56,600 Sht/17/28.96	360.000
BRACIANESE 2°		Repairs to ~~building~~ Bridge N°5 at km 72,300 sht 17/910	1,150.000
"		Total d)	2,560.000
		Grand total (a + b + c + d)	25,490.480 Lire

Declassified E.O. 12356 Section 3.3/NND No. 785019

LAZIO-UMBRIA REGION A.M.G.

REPORT for MONTH of OCTOBER/44 (P.W. (P)

Works approved during month at Regional Level

ITALIAN GOVERNMENT Territory ROMA Province

Approved by Regional Engineer Limit L. NONE

(approval in principl

REF.	LOCATION	PROJECT and DESCRIPTION		ESTIM
		a) Water supply		
101.302	VELLETRI	water supply		4.300.
		Total a)		4.300.
		b) Repairs to building & Rehousing		
101.249	FRASCATI	Repairs to "Conventi P.P.Minori		1.260.
101.275	ARICCIA	" " "Istituto Ortopedico"		2.475.
		Total b)	L.	3.735.
		c) other works (excluding roads & bridges		
101.246	ARTENA	Demolitions & removal debris & sewers repairs		3.800.
101.266	MACCARESE	Bonifica		11.500.00
101.227	PAGLIETE	"		4.200.
101.296	CIVITAVECCHIA	Dredges salvages		200.
101.299	PALESTRINA	Repairs to sewerage		1.700.
		Total c)	L.	21.400.
		d) non military roads & bridges		
102.43	SETTEVENE R. PALO 1°	Repairs to provincial road		5.880.
		Total d)	L.	5.880.
		GRAND TOTAL (a+b+c+d)	L.	35.315.

Declassified E.O. 12356 Section 3.3/NND No. 785019

MBRIA REGION A.M.G. — REPORT for MONTH of OCTOBER/44 (P.W. (P)

Works approved during month at Regional Level

LIAN GOVERNMENT — Territory — ROMA Province

d by Regional Engineer — Limit L. NONE

(approval in principle only)

	LOCATION	PROJECT and DESCRIPTION		ESTIMATED COST
		a) Water supply		
02	VELLETRI	water supply		4.300.000
		Total a)		4.300.000
		b) Repairs to building & Rehousing		
49	FRASCATI	Repairs to "Conventi P.P.Minori		1.260.000
75	ARICCIA	" " "Istituto Ortopedice"		2.475.000
		Total b)	L.	3.735.000
		c) other works (excluding roads & bridges		
46	ARTENA	Demolitions & removal debris & sewers repairs		3.800.000
66	MACCARESE	Bonifica		11.500.000
27	PAGLIETE	"		4.200.000
96	CIVITAVECCHIA	Dredges salvages		200.000
99	PALESTRINA	Repairs to sewerage		1.700.000
		Total c)	L.	21.400.000
		d) non military roads & bridges		
3	SETTEVENE R. PALO 1°	Repairs to provincial road		5.880.000
		Total d)	L.	5.880.000
		GRAND TOTAL (a+b+c+d)	L.	35.315.000

Declassified E.O. 12356 Section 3.3/NND No. 785019

Lazio Umbria Region A.M.G.

REPORT for MONTH of October 44 EW. (P)

Works approved during month Regional Level

A.M.G.

Approved by Regional Engineer

Territory R I E T I Provi

Limit L.
(no cont

REF	LOCATION	PROJECT and DESCRIPTION
		A) Water supply
		Nil
		TOTL A)
		B) Repairs buildings and Re-housing
101.195	RIETI	Repairs to " Caserma Vigili del fuoco"
196	"	" " " Convitto S.Caterina"
334	PASSO CORESE	" " " Caserma Carabinieri"
		TOTL B)
		C) Other works (excluding roads & bridges)
101.194	RIETI PROV.	Clearing bed of River Velino
101.250	RIETI	Repairs to " Cimitery "
335	RIETI PROV.	" " " Bonifica reatina"
		TOTAL C)
		D) Non military roads &.bridges
102.30	TONTECERRO/FINOCCHIETTO	Repairs works on road
103.88	SALTO/CICOLANA R.	Repair Passerella on Fischiaduro
103.89	PICENTE ROAD	" " " Castellano R.N° 22/16/42/46
103.90	CITTADUCALE/FIAMIGNANO	and " Delle Case
		Repair Caporio Bdg. N° 18 - 16/15.19
103.94	STRADA SABINA	on; Velino River
	PART OF STRADA MAGLIAN SABINA	Repair to roads

Declassified E.O. 12356 Section 3.3/NND No. 785019

gion A.M.G.

REPORT for MONTH of October 1944 FW. (P)

Works approved during month at Regional Level

gional Engineer

Territory T I E T I Province

Limit I. 1.000.000
(no control.mat.)

LOCATION	PROJECT and DESCRIPTION	ESTIMATED COST
	A) Water supply Nil	
	TOTAL A)	----
	B) Repairs buildings and Re-housing	
RIETI	Repairs to " Caserma Vigili del fuoco"	105.000
"	" " " Convitto S.Caterina"	23.000
PASSO CORESE	" " " Caserma Carabinieri"	570.000
	TOTAL B)	698.000
	C) Other works (excluding roads & bridges)	
RIETI PROV.	Clearing bed of River Velino	45.000
RIETI	Repairs to " Cimitery "	375.000
RIETI PROV.	" " " Bonifica reatina"	400.000
	TOTAL C)	820.000
	D) Non military roads &.bridges	
PONTECERRO/FINOCCHIETTO	Repairs works on road	775.000
SALTO/CICCLANA R.	Repair Passarella on Fischiaduro	640.000
PICENTE ROAD	" " " Castellano R.N° 22/15/42/46	
CITTADUCALE/FIAMIONANO	and " Delle Cese	280.000
	Repair Caporio Bdg. N° 18 - 16/15.19 on:Velino River	520.000
STRADA SABINA		
PART OF STRADA MAGLIAN SABINA	Repair to roads	1.000.000

Declassified E.O. 12356 Section 3.3/NND No. 785019

102.30	PONTECERRO/PINOCCHIETTO	Repairs works on road
103.88	SALTO/CICOLANA R.	Repair Passerella on Fischiaduro
103.89	PICENTE ROAD	" " " Castellano R.N° 22/16/42/46
		and " Delle Cese
103.90	CITTADUCALE/FIAMIGNANO	Repair Caporio Bdg. N° 18 - 16/15.19
		on; Velino River
103.94	STRADA SABINA	
	PART OF STRADA MAGLIAN	
	SABINA	Repair to roads

TOTAL D)

GRAND TOTAL (e+b+c+d) L.

1754

Declassified E.O. 12356 Section 3.3/NND No. 785019

FORTEZZARO/FINOCCHIETTO	Repairs works on road	775.000
SALTO/CICOLANA R. PICENTE ROAD	Repair Passerella on Fiochiaduro	640.000
	" " " Castellano R.N° 22/16/42/45 and " Delle Cese	
CITTADUCALE/FIAMIGNANO	Repair Caporio Bdg. N° 18 - 16/15.19 on Velino River	280.000
STRADA SABINA PART OF STRADA MAGLIAN SABINA	Repair to roads	520.000
		1.000.000
	TOTAL n)	3.215.000
	GRAND TOTAL (a+b+c+d)	L. 4.733.000

Declassified E.O. 12356 Section 3.3/NND No. 785019

LAZIO & UMBRIA REGION A.M.G.

REPORT FOR MONTH OF O C T O B E R / 1944. P.W. (P).

Works approved during month at Regional Level

A.M.G. Territory PERUGIA PR.

Approved by Regional Engineer

Limit £. 1,
(No controlled

REF.	LOCATION	PROJECT AND DESCRIPTION	ESTIMATED CO
		a) Water supply	
		NIL	
		Total a)	
		b) Repairs buildings and Re-housing	
101.345	PERUGIA	Repairs to "Mercato Coperto"	573.0
354	ASSISI	" " "Convento S. Damiano"	783.0
355	"	" " "Convento S. Chiara"	600.0
360	FOLIGNO	" " "ex Sanatorio ora Scuole Medie"	500.0
		Total b)	2,467.0
		c) Other works (excluding roads & bridges)	
		Total c)	
		d) Non military roads and bridges	
103.116	OSCANO Torrent	Repairs on "Camullino"bdg N°115 sht.13/642.980	700.0
103.117	MAGIONE/MIGIANA R.	" " Bdg.N°117 sht.13/660/963	600.0
103.118	CAINA Torrent	" " "COLLE UMBERTO" Bdg.N°27 sht.13/633/995	885.0
		Total d)	2,185.0
		GRAND TOTAL (A+b+c+d) Lire	4,652.0

Declassified E.O. 12356 Section 3.3/NND No. 785019

UMBRIA REGION A.M.G.

REPORT FOR MONTH OF O C T O B E R / 1944. P.W. (P).

Works approved during month at Regional Level

A.M.G. Territory PERUGIA PR.

d by Regional Engineer

Limit £. 1,000.000
(No controlled materials)

EF.	LOCATION	PROJECT AND DESCRIPTION	ESTIMATED COST
		a) Water supply	
		NIL	
		Total a)	
		b) Repairs buildings and Re-housing	
345	PERUGIA	Repairs to "Mercato Coperto"	573.000
354	ASSISI	" " "Convento S. Damiano"	783.000
355	"	" " "Convento S. Chiara"	600.000
360	FOLIGNO	" " "ex Sanatorio ora Scuole Medie"	500.000
		Total b)	2,467.000
		c) Other works (excluding roads & bridges)	
		Total c)	
		d) Non military roads and bridges	
116	OSCANO Torrent	Repairs on "Camullino"bdg N°115 sht.13/642.980	700.000
117	MAGIONE/MIGIANA R.	" " Bdg.N°117 sht.13/660/963	600.000
118	CAINA Torrent	" " "COLLE UMBERTO" Bdg.N°27 sht.13/633/995	885.000
		Total d)	2,185.000
		GRAND TOTAL (A+b+c+d) Lire	4,652.000

Declassified E.O. 12356 Section 3.3/NND No. 785019

LAZIO-UMBRIA REGION - A.M.G.

REPORT FOR MONTH OF OCTOBER 44 P.W. (P)

Works approved during month at Regional Level

Italian Government Territory - LITTORIA PROVINCE.

Approved by Compartiment Inspector Genio Civile - Limit £. 500.000 - (no controlled mate

REF.	LOCATION	PROJECT AND DESCRIPTION		£
		a) Water supply		
		NIL		
		TOTAL a)	£.	
		b) Repairs to buildings and re-housing		
---	S E Z Z E	Riparazione Ufficio del Registro	"	
	"	" Ospedale	"	
		TOTAL b)	"	
		c) Other works (excluding roads and bridges)		
	LITTORIA	Pagamento operai luglio/Settembre		
	PRIVERNO	Demolizioni e sgombri		
	APRILIA	" " "		
		TOTAL c)	"	
		d) Non military roads and bridges		
	LITTORIA	Riparazione strada Prov. Formia (Gaeta)	"	
		TOTAL d)	"	

Declassified E.O. 12356 Section 3.3/NND No. 785019

RIA REGION - A.M.G.

REPORT FOR MONTH OF OCTOBER 44 P.W. (P)

Works approved during month at Regional Level

Government Territory - LITTORIA PROVINCE.

d by Compartiment Inspector Genio Civile - Limit £. 500.000 - (no controlled materials).

LOCATION	PROJECT AND DESCRIPTION		ESTIMATED COST
	a) Water supply		
	NIL		
	TOTAL a)	£.	
	b) Repairs to buildings and re-housing		
S E Z Z E	Riparazione Ufficio del Registro	"	85.000
"	" Ospedale	"	226.000
	TOTAL b)	"	311.000
	c) Other works (excluding roads and bridges)		
LITTORIA	Pagamento operai luglio/Settembre		55.000
PRIVERNO	Demolizioni e sgombri		280.000
APRILIA	" " "		365.000
	TOTAL c)	"	700.000
	d) Non military roads and bridges		
ITTORIA	Riparazione strada Prov. Formia (Gaeta)	"	199.000
	TOTAL d)	"	199.000

Declassified E.O. 12356 Section 3.3/NND No. 785019

		TOTAL c)	"
		d) Non military roads and bridges	
	LITTORIA	Riparazione strade Prov. Formia (Gaeta)	"
		TOTAL d)	"
		GRAND TOTAL (a + b + c + d)	"

Declassified E.O. 12356 Section 3.3/NND No. 785019

	TOTAL c)	"	700.000
	d) Non military roads and bridges		
LITTORIA	Riparazione strada Prov. Formia (Gaeta)	"	199.000
	TOTAL d)	"	199.000
	GRAND TOTAL (a + b + c + d)	"	1.210.000

Declassified E.O. 12356 Section 3.3/NND No. 785019

Region LAZIO-UMBRIA A.M.G.

REPORT FOR MONTH OF OCTOBER 1944 P.W. (P)

Works approved during month at Regional level

Italian Government - Territory LITTORIA Province
Approved by Regional Engineer - Limit £. None - approval in principle only.

REF.	LOCATION	PROJECT AND DESCRIPTION
		a) water supply
		NIL
		Total (a)
101.303	L I T T O R I A	b) Repairs buildings and Re-housing Repairs to buildings "Istituto Case Popolari
		Total b)
		c) Other works (excluding roads and bridges)
		NIL
		Total c)
		d) non military roads and bridges
103.97	TERRACINA/S.FELICE CIRCEO	Repairs to PERNARELLA Bridge N°8 Sheet 19/20.99
103.98	LITTORIA/MASSIANO	" " VALVISCIOLA Bdg. N°5 Sht. 17/15.30
103.106	LITTORIA/SERMONETTA	Repair Bdg. N° 2 Sht. 17/13.27
103.107	SETTIMA Road	" " " 3 Sht. 17/205.220
103.108	MISCELLNT CHANNEL	" " " 4 Sht. 17/115/295

Declassified E.O. 12356 Section 3.3/NND No. 785019

O-UMBRIA A.M.G.

REPORT FOR MONTH OF OCTOBER 1944 P.W. (P)

Works approved during month at Regional Level

ernment - Territory LITTORIA Province

Regional Engineer - Limit S. None - approval in principle only.

LOCATION	PROJECT AND DESCRIPTION	ESTIMATED COST
	a) water supply	
	NIL	
	Total (a)	
	b) Repairs buildings and Re-housing	
L I T T O R I A	Repairs to buildings "Istituto Case Popolari	14.937.000
	Total b)	14.937.000
	c) Other works (excluding roads and bridges)	
	NIL	
	Total c)	
	a) non military roads and bridges	
TERRACINA/S.FELICE CIRCEO	Repairs to PETRARELLA Bridge Nº6 Sheet 19/29.99	3.400.000
LITTORIA/LASCIANO	" " VALVISCIOLA Bdg. Nº5 Sht. 17/15.30	7.750.000
LITTORIA/SERMONETTA	Repair Bdg. Nº 2 Sht. 17/15.27	999.000
SEZZA Road	" " " 3 Sht. 17/205.220	2.900.000
MUSSOLINI CANAL	" " " 4 Sht. 17/145/295	3.640.000

Declassified E.O. 12356 Section 3.3/NND No. 785019

		d) non military roads and bridges	
103.97	TERRACINA/S.FELICE CIRCEO	Repairs to PERNARELLA Bridge N°8 Sheet 19/29.99	
103.98	LITTORIA/BADSIANO	" " VALVISCIOLA Bdg. N°5 Sht. 17/15.20	
103.106	LITTORIA/SERMONETTA	Repair Bdg. N° 2 Sht. 17/13.27	
103.107	SETIMA Road	" " " 3 Sht. 17/205.220	
103.108	MUSSOLINI CHANNEL	" " " 4 Sht. 17/145/205	
		Total d)	£.
		GRAND TOTAL (a + b + c + d)	£.

Declassified E.O. 12356 Section 3.3/NND No. 785019

TERRACINA/S.FELICE CIRCEO	d) non military roads and bridges		
ITTORIA/LASSLANO	Repairs to TERRACINA Bridge N°8 Sheet 19/29.59		2.400.000
ETTORIA/SERRONETTA	" " VALVISCIOLA Bdg. N°5 Sht. 16/15.30		7.750.000
ENINA Road	Repair Bdg. N° 2 Sht. 17/13.27		998.000
SCOLINI CHANNEL	" " " 3 Sht. 17/205.220		2.900.000
	" " " 4 Sht. 17/145/295		3.640.000
	Total d)	L.	18.689.000
	GRAND TOTAL (a + b + c + d)	L.	33.626.000

Declassified E.O. 12356 Section 3.3/NND No. 785019

Region - LAZIO-UMBRIA A.M.G.

REPORT FOR MONTH OF OCTOBER 44 (P.W. (F)

Works approved during month at Regional Level

Italian Government - Territory LITTORIA Province

Approved by Regional Engineer Limit £. 1.000.000 - (no controlled mater

REF.	LOCATION	PROJECT AND DESCRIPTION
		a) Water supply NIL
		b) Repairs buildings and Re-housing
101.345	FORMIA	Repairs to houses
.346	"	" " "
.347	MINTURNO	" " "
.348	TERRACINA	" " "
.349	MINTURNO	" " "
.350	APRILIA	" " "
.351	TERRACINA	" " "
.333	LITTORIA	" " Palazzo delle Poste
.361	TERRACINA	" " private houses requisitioned
		Total b) £.
		c) Other works (excluding roads and bridges)
101.209	TERRACINA	Debris removal
.210	CISTERNA	" "
.293	TERRACINA	" "
.294	CORI BASSO	" "
.295	CORI ALTO	" "
.336	FORMIA	" "
.358	TERRACINA	" "
		Total c) £.
		d) Non military roads & Bridges NIL

Declassified E.O. 12356 Section 3.3/NND No. 785019

- LAZIO-UMBRIA A.M.G.

REPORT FOR MONTH OF OCTOBER 44 (T.W. (P)

Works approved during month at Regional Level

n Government - Territory LITTORIA Province

ed by Regional Engineer Limit £. 1.000.000 - (no controlled materials)

LOCATION	PROJECT AND DESCRIPTION	ESTIMATED COST
	a) Water supply NIL	
	b) Repairs buildings and Re-housing	
FORMIA	Repairs to houses	997.000
"	" " "	995.000
MINTURNO	" " "	506.000
TERRACINA	" " "	988.000
MINTURNO	" " "	995.000
APRILIA	" " "	815.000
TERRACINA	" " "	992.000
LITTORIA	" " Palazzo delle Poste	830.000
TERRACINA	" " private houses requisitioned	990.000
	Total b) £.	8.108.000
	c) Other works (excluding roads and bridges)	
TERRACINA	Debris removal	995.000
CISTERNA	" "	956.000
TERRACINA	" "	965.000
CORI BASSO	" "	710.000
CORI ALTO	" "	855.000
FORMIA	" "	998.000
TERRACINA	" "	973.000
	Total c) £.	6.450.000
	d) Non military roads & Bridges NIL	

Declassified E.O. 12356 Section 3.3/NND No. 785019

Total c) £.

d) Non military roads & Bridges
NIL

GRAND TOTAL (a+b+c+d) £.

Declassified E.O. 12356 Section 3.3/NND No. 785019

TERRACINA	" "		973.000
		Total c) £.	6.450.000
	d) Non military roads & Bridges NIL		
	GRAND TOTAL (a+b+c+d)	£.	14.560.000

Declassified E.O. 12356 Section 3.3/NND No. 785019

LAZIO-UMBRIA REGION A.M.G.

REPORT FOR MONTH OF OCTOBER 44 P.W. (P)

Works approved during month at Regional Level

Italian Government Territory - FROSINONE Province.

Approved by Compartiment Inspector Genio Civile - Limit £. 500.000 - (no controlled materials

REF.	LOCATION	PROJECT AND DESCRIPTION	EST
		a) Water supply	
		Total a)	£.
	CASSINO	b) Repairs to buildings and re-housing	
	A R C E	Riparazione casa F.lli Ferraioli	
		Sistemazione Ufficio del G.C.	
		Total b)	£.
		c) Other works (excluding roads and bridges	
	S. GIOVANNI CAMPANO	Sgombri nell'abitato	"
	S O R A	" " "	"
	ROCCA D'ARCE	" " "	"
	A C U T O	" " "	"
	CASTRO DEI VOLSCI	" del F. Sacco	"
	STRANGOLAGALLI	" nell'abitato	"
	FONTECHIARI	" " "	"
	CASTELLIRI	" " "	"
	ISOLA LIRI	Sgombro del F. Liri	"
	BROCCO	" nell'abitato	"
	S O RA	Rimozione rottami del ponte in ferro	"
	ALATRI	Sgombro strade urbane	"
		Total c)	"
		d) Non military roads and bridges	
	FROSINONE	Ricostruzione ponte in legno sul Fibreno	
	FROSINONE	Costruzione passerella Nº 35 comune di Bromo	
	"	Sistemazione rampe d'accesso del F. Sacco Comune Pofi	
	"	Costruzione Ponte nº 76	
	"	Costruzione Ponte sul Rio Zaffreda Comune Fontana Liri	
		Total d)	£.

Declassified E.O. 12356 Section 3.3/NND No. 785019

ERIA REGION A.M.G.

REPORT FOR MONTH OF OCTOBER 44 P.W. (F)

Works approved during month at Regional Level

Government Territory - FROSINONE Province.

by Compartiment Inspector Genio Civile - Limit £. 500.000 - (no controlled materials)

LOCATION	PROJECT AND DESCRIPTION	ESTIMATED COST
	a) Water supply	NIL
	Total a)	£. ----
CASSINO	b) Repairs to buildings and re-housing	
A R C E	Riparazione casa F.lli Ferraioli	320.000
	Sistemazione Ufficio del G.C.	55.000
	Total b)	£. 375.000
S. GIOVANNI CAMPANO	c) Other works (excluding roads and bridges	
S O R A	Sgombri nell'abitato	" 157.500
ROCCA D'ARCE	" " "	" 415.000
A C U T O	" " "	" 162.000
CASTRO DEI VOLSCI	" del F. Sacco	" 340.000
STRANGOLAGALLI	" nell'abitato	" 300.000
FONTECHIARI	" " "	" 450.000
CASTELLIRI	" " "	" 175.000
ISOLA LIRI	Sgombro del F. Liri	" 212.000
BROCCO	" nell'abitato	" 220.000
S O R A	Rimozione rottami del ponte in ferro	" 106.000
ATRI	Sgombro strade urbane	" 285.000
	Total c)	" 84.000
		" 2.906.000
FROSINONE	d) Non military roads and bridges	—
FROSINONE	Ricostruzione ponte in legno sul Fibreno	300.000
"	Costruzione passerella N° 35 comune di Bromo	400.000
"	Sistemazione rampe d'accesso del F. Sacco Comune Pofi	180.000
"	Costruzione Ponte nº 76	490.000
	Costruzione Ponte sul Rio Zaffreda Comune Fontana Liri	480.000
	Total d)	£. 1.850.000

Declassified E.O. 12356 Section 3.3/NND No. 785019

	FROSINONE	Ricostruzione ponte in legno sul Fibreno	
	FROSINONE	Costruzione passerella Nº 35 comune di Bromo	
	"	Sistemazione rampe d'accesso del F. Sacco Comune Pofi	
	"	Costruzione Ponte nº 76	
	"	Costruzione Ponte sul Rio Zaffreda Comune Fontana Liri	
		Total d)	£. 1.
		GRAND TOTAL (a + b + c + d)	" 5.

Declassified E.O. 12356 Section 3.3/NND No. 785019

ROSINONE	Ricostruzione ponte in legno sul Fibreno	300.000
ROSINONE	Costruzione passerella N° 35 comune di Bromo	400.000
"	Sistemazione rampe d'accesso del F. Sacco Comune Pofi	180.000
"	Costruzione Ponte n° 76	490.000
"	Costruzione Ponte sul Rio Zaffrede Comune Fontana Liri	180.000
	Total d)	£. 1.850.000
	GRAND TOTAL (a + b + c + d)	" 5.131.500

Declassified E.O. 12356 Section 3.3/NND No. 785019

LAZIO-UMBRIA REGION A.M.G.

REPORT FOR MONTH OF OCTOBER 44 (P.M. (P)

Works approved during month at Regional Level

Italian Government - Territory FROSINONE Province

Approved by Regional Engineer Limit £. 1.000.000 - (no controlled materials)

REF.	LOCATION	PROJECT AND DESCRIPTION	
		a) Water supply	
101.257	ALVITO	Repairs to aqueduct	
.259	VICALVI	" " "	
.261	SUPINO	" " "	
.350	ROCCASECCA	" " "	
		Total a)	£.
		b) Repairs to buildings & Re-housing.	
101.277	ANAGNI	Repairs to "Seminario"	
.297	PONTECORVO	" " "Hospital"	
.256	ROCCASECCA	" " "Edificio Comunale"	
		" " "Schools"	
		Total b)	£.
		c) Other works (excluding roads & bridges)	
101.211	AQUINO	Removal of debris I lotto	
.212	ARCE	" " "	
.213	CASTENA	" " "	
.214	FONTANA LIRI	" " "	
.215	S.GIOVANNI INCARICO	" " "	
.216	CEPRANO	" " "	
.217	ISOLA LIRI	" " "	
.218	PICO	" " "	
.251	TIBURTINA ROAD	" " "	
.252	ALATRI	" " "	
.253	SUPINO	" " " from streets	
.254	SUPINO	Repairs to sewerage	
.255	ANAGNI	Removal of debris from streets	
.256	PRENESTINA ROAD	" " " " "	
.258	ALVITO	" " "	
.260	ALATRI	" " "	
.262	S. GIORGIO A LIRI	" " "	
.263	VICALVI	" " "	
.264	S. GIORGIO A LIRI	Repairs to sewerage	
.265	ALATRI	Removal of debris	
.280	ESPERIA	Demolitions and Debris Removal	
.281		II Zona	
.282	PONTECORVO	III "	
		"	

Declassified E.O. 12356 Section 3.3/NND No. 785019

RIA REGION A.M.G. REPORT FOR MONTH OF OCTOBER 44 (P.W. (P)

Works approved during month at Regional level

overnment - Territory FROSINONE Province

by Regional Engineer Limit £. 1.000.000 - (no controlled materials)

LOCATION	PROJECT AND DESCRITTION		ESTIMATED COST
	a) Water supply		
ALVITO	Repairs to aqueduct		5.085
VICALVI	" " "		18.000
SUPINO	" " "		10.000
ROCCASECCA	" " "		564.000
	Total a)	£.	597.085
	b) Repairs to buildings & Re-housing.		
ANAGNI	Repairs to "Seminario"		530.000
PONTECORVO	" " "Hospital"		902.000
ROCCASECCA	" " "Edificio Comunale"		805.000
	" " "Schools"		600.000
	Total b)	£.	2.837.000
	c) Other works (excluding roads & bridges)		
AQUINO	Removal of debris I lotto		960.000
ARCE	" " "		510.000
CASTENA	" " "		996.000
FONTANA LIRI	" " "		540.000
S.GIOVANNI INCARICO	" " "		800.000
CEPRANO	" " "		960.000
ISOLA LIRI	" " "		670.000
RICO	" " "		972.000
TIBURTINA ROAD	" " "		113.000
ALATRI	" " " from streets		24.000
SUPINO	Repairs to sewerage		17.000
SUPINO	Removal of debris from streets		65.000
ANAGNI	" " " " "		198.000
PRENESTINA ROAD	" " "		28.417,50
ALVITO	" " "		77.667,50
ALATRI	" " "		12.495
S. GIORGIO A LIRI	" " "		52.841,70
VICALVI	" " "		30.420
S. GIORGIO A LIRI	Repairs to sewerage		67.890
ALATRI	Removal of debris		521.500
ESPERIA	Demolitions and Debris Removal		996.000
	II Zona		960.000
PONTECORVO	III "		595.000
	"		942.000

Declassified E.O. 12356 Section 3.3/NND No. 785019

RLA REGION A.M.G. REPORT FOR MONTH OF OCTOBER 44 (P.W. (P)

Works approved during month at Regional Level

overnment - Territory FROSINONE Province

by Regional Engineer Limit £. 1.000.000 - (no controlled materials)

LOCATION	PROJECT AND DESCRIPTION		ESTIMATED COST
	a) Water supply		
ALVITO	Repairs to aqueduct		5.085
VICALVI	" " "		18.000
SUPINO	" " "		10.000
ROCCASECCA	" " "		564.000
	Total a)	£.	597.085
	b) Repairs to buildings & Re-housing.		
ANAGNI	Repairs to "Seminario"		530.000
PONTECORVO	" " "Hospital"		902.000
ROCCASECCA	" " "Edificio Comunale"		805.000
	" " "Schools"		600.000
	Total b)	£.	2.837.000
	c) Other works (excluding roads & bridges)		
AQUINO	Removal of debris I lotto		960.000
ARCE	" " "		510.000
PASTENA	" " "		996.000
FONTANA LIRI	" " "		540.000
S.GIOVANNI INCARICO	" " "		830.000
CEPRANO	" " "		960.000
ISOLA LIRI	" " "		670.000
PICO	" " "		972.000
TIBURTINA ROAD	" " "		113.000
ALATRI	" " " from streets		24.000
SUPINO	Repairs to sewerage		17.000
SUPINO	Removal of debris from streets		65.000
ANAGNI	" " " " "		198.000
PRENESTINA ROAD	" " "		28.417,50
ALVITO	" " "		77.667,50
ALATRI	" " "		12.495
S. GIORGIO A LIRI	" " "		52.841,70
VICALVI	" " "		30.420
S. GIORGIO A LIRI	Repairs to sewerage		67.890
ALATRI	Removal of debris		521.500
ESPERIA	Demolitions and Debris Removal		996.000
	II Zona		960.000
PONTECORVO	III "		995.000
	"		642.000

Declassified E.O. 12356 Section 3.3/NND No. 785019

.253	SUTINO	Repairs to sewerage
.254	SUPINO	Removal of debris from streets
.255	ANAGNI	" " " " "
.256	PRENESTINA ROAD	" " "
.258	ALVITO	" " "
.260	ALATRI	" " "
.262	S. GIORGIO A LIRI	" " "
.263	VICALVI	" " "
.264	S. GIORGIO A LIRI	Repairs to sewerage
.265	ALATRI	Removal of debris
.280	ESPERIA	Demolitions and Debris Removal
.281		II Zona
.282	PONTECORVO	III "
.283		IV "
.284		V "
.341	S. VITTORE	Demolitions and removal of debris
.342	PIEDIMONTE	" " " " "
		Total c) £.
		d) Non military roads & bridges
102.44	ARAGNI-ACUTO	Repairs to road
103.87	S O R A	Repairs to bridge N° 44 17/68.46
.96	P I C O	" " " " 71 17/62.17
.99	TOMACELLA	" " passerella N°20 17/41.34
.102	CASALATTICO	" " " " 74 17/79.37
.103	PORANO	" " bridge "La Molinella 15/44.55
.105	S.AMBROGIO-S.APOLLINARE	" " " N. 87 17/88.10
.119	CAVALIERI-FONTECHIARA	" " " N° 83 17/725.435
.120	ROCCASECCA - CASTROCIELO	" " " " 85 17/725.275
.121	GUARCINO	" " " " 9 17.417.563
		Total d) £.
		GRAND TOTAL (a+b+c+d) "

Declassified E.O. 12356 Section 3.3/NND No. 785019

UTINO	Repairs to sewerage		17.000
UPINO	Removal of debris from streets		65.000
NAGNI	" " " " "		198.000
PRENESTINA ROAD	" " "		28.417,50
LVITO	" " "		77.667,50
IATRI	" " "		12.495
. GIORGIO A LIRI	" " "		52.841,70
VICAIVI	" " "		30.420
. GIORGIO A LIRI	Repairs to sewerage		67.850
IATRI	Removal of debris		521.500
SPERIA	Demolitions and Debris Removal		996.000
	II Zona		960.000
ONTECORVO	III "		995.000
	IV "		942.000
	V "		890.000
. VITTORE	Demolitions and removal of debris		675.000
IEDIMONTE	" " " " "		900.000
	Total c)	£.	14.004.231,70
	d) Non military roads & bridges		
NAGNI-ACUTO	Repairs to road		750.000
O R A	Repairs to bridge Nº 44 17/68.46		800.000
I C O	" " " " 71 17/62.17		950.000
OMACELIA	" " passerella Nº20 17/41.34		806.000
ASAIATTICO	" " " " 74 17/79.37		642.000
PORANO	" " bridge "La Molinella 15/44.55		300.000
.AMBROGIO-S.APOLLINARE	" " " N. 87 17/88.10		530.000
CAVALIERI-FONTECHIARA	" " " Nº 83 17/725.435		500.000
ROCCASECCA - CASTROCIELO	" " " " 85 17/725.275		540.000
UARCINO	" " " " 9 17.417.563		650.000
	Total d)	£.	6.468.000
	GRAND TOTAL (a+b+c+d)	"	23.906.316,70

Declassified E.O. 12356 Section 3.3/NND No. 785019

Lazio-Umbria Region A.M.G.

REPORT for MONTH of OCTOBER/44 (P.W. (P)

Works approved during month at Regional Level

ITALIAN GOVERNMENT — Territory FROSINONE — Provinc

Approved by REGIONAL ENGINEER — Limit L. NONE

(approval in principle or

REF.	LOCATION	PROJECT and DESCRIPTION	ESTIMATED
		a) water supply	
101.340	CASSINO	Repairs to Aqueduct	3.930.000
		Total a)	3.930.000
		b) Repairs to building & Rehousing	
101.207	PONTECORVO	Repairs to "Case Popolari"	700.000
.208	"	" " " "	635.000
.301	ISOLA LIRI	Repairs to 2 buildings of "Istituto Case Popolari"	14.937.000
.352	SORA	Repairs to houses	6.790.000
		Total b)	23.062.000
		c) other works (excluding roads and bridges	
101.211	AQUINO	Debris removal (1° lotto)	960.000
101.212	ARCE	" "	510.000
101.213	PASTENA	" "	990.000
101.214	FONTANA LIRI	" "	540.000
101.215	S.GIOVANNI.. INCARICO	" "	830.000
101.216	CEPRANO	" "	960.000
101.217	ISOLA LIRI	" "	670.000
101.218	PICO	" "	972.000
		Total c)	6.432.000
		d) non military roads and bridges	
103.60	ISOLA LIRI	Construction temporary bridge	

Declassified E.O. 12356 Section 3.3/NND No. 785019

Region A.M.G.

REPORT for MONTH of OCTOBER/44 (P.W. (P)

Works approved during month at Regional Level

ALIAN GOVERNMENT — Territory: FROSINONE — Province

REGIONAL ENGINEER — Limit L. NONE

(approval in principle only)

LOCATION	PROJECT and DESCRIPTION	ESTIMATED COST
	a) water supply	
CASSINO	Repairs to Aqueduct	3.930.000
	Total a)	3.930.000
	b) Repairs to building & Rehousing	
PONTECORVO	Repairs to "Case Popolari"	700.000
"	" " " "	635.000
ISOLA LIRI	Repairs to 2 buildings of "Istituto Case Popolari"	14.937.000
SORA	Repairs to houses	6.790.000
	Total b)	23.062.000
	c) other works (excluding roads and bridges	
AQUINO	Debris removal (1° lotto)	960.000
ARCE	" "	510.000
PASTENA	" "	990.000
FONTANA LIRI	" "	540.000
S.GIOVANNI INCARICO	" "	830.000
CEPRANO	" "	960.000
ISOLA LIRI	" "	670.000
PICO	" "	972.000
	Total c)	6.432.000
	d) non military roads and bridges	
ISOLA LIRI	Construction temporary bridge	

Declassified E.O. 12356 Section 3.3/NND No. 785019

		INCARICO		
101.216		CEPRANO	" "	960.000
101.217		ISOLA LIRI	" "	670.000
101.218		PIGO	" "	972.000
			Total c)	6.432.000
		d) non military roads and bridges		
103.60		ISOLA LIRI	Construction temporary bridge N°4 or 5(MR.17/65.42)	750.00
.61		ANAGNI	Repairs to 2 bridges N°19 (MR.17/30.49)	300.00
.62		"	Repairs to bridge N°18 (MR.17/30.49)	1.100.00
.63		OLEVANO	Repairs to bridge N°73 (MR.17/18.58):	2.300.00
.64		ANAGNI-PALIANO	Repairs to bridge N°16 (MR.17/27.51)	2.000.00
.104		S.AMBROGIO-S.APOLLINARE	Repairs to bridge N°86 (MR.17/865.105)	1.990.00
.122		ANAGNI-PALIANO	Repairs to bridge N°17 (MR.17/255;525)	1.300.00
.123		RIO MOLLO RIVER	Repairs to bridge N°38 (MR.17/795.385)	1.230.00
			Total d)	10.970.00
			GRAND TOTAL(a+b+c+d)	4.394.00

Declassified E.O. 12356 Section 3.3/NND No. 785019

	INCARICO		
	CEPRANO	" "	960.000
	ISOLA LIRI	" "	670.000
	PIGO	" "	972.000
			Total c) 6.432.000
	d) non military roads and bridges		
ISOLA LIRI	Construction temporary bridge N°4 or 5(MR.17/65.42)		750.000
ANAGNI	Repairs to 2 bridges N°19 (MR.17/30.49)		300.000
"	Repairs to bridge N°18 (MR.17/30.49)		1.100.000
OLEVANO	Repairs to bridge N°73 (MR.17/18.58):		2.300.000
ANAGNI-PALIANO	Repairs to bridge N°16 (MR.17/27.51)		2.000.000
S.AMBROGIO-S.APOLLINARE	Repairs to bridge N°86 (MR.17/865.105)		1.990.000
ANAGNI-PALIANO	Repairs to bridge N°17 (MR.17/255;525)		1.300.000
RIO MOLLO RIVER	Repairs to bridge N°38 (MR.17/795.385)		1.230.000
			Total d) 10.970.000
	GRAND TOTAL(a+b+c+d)		44.394.000

Declassified E.O. 12356 Section 3.3/NND No. 785019

AEM/dpe

Appendix A

LAZIO-UMBRIA REGION, ENGINEERING DIVISION (PUBLIC WORKS (R.C.) SECTION)

Statistical Summary Month of Oct. 1944

WORKS APPROVED		Approved in principle (& not final)	DEFINITE APPROVAL
(1) Value of work approved up to 30 Sept.44			
a)Rome Comune-Prog.n.1-Urgent work requested by Allied Command but not classified as Military projects. Approved, money rcvd. 19 Aug.	30,800,000		
b)Rome Comune-Prog.n.2-Urgent work requested by Pu.Wks.Dept.of R.C. requiring little or no critical mtrls. Approved, money rcvd. 19 Aug.	25,300,000		
c)Rome Comune-Six Hwy.& br.proj.-ACC/1 & ACC/2 appvd.by P.W.S.C.-ACC 31 Aug.	9,950,000		
d)Seven Hwy.& br.proj.-ACC/1 & ACC/2 appvd.by P.W.S.C.-ACC 9 Sept.	13,645,000		
e)P.W.(R.C.)Proj.45,46,47-P.W.S.C. appvl. 15 Sept.	2,440,000		
Total (1)	82,135,000		82,135,000
(1A)Value of works approved up to 30 Sept. not included in (1) above:56 proj.-Total	61,510,000	61,510,000	
(2) Value of works approved during Oct. (exc. as noted below)			
a)By Regional Engr.			
a1 - 500,000 to 1,000,000 - 7 proj.	6,304,000		
a2 - over 1,000,000 16 "	39,647,000		
	45,951,000	45,951,000	
b)By Compartment Inspector -under 500,000. Oct.report for mo.of Sept.	11,032,700		11,032,700
51 projects	3,025,000		3,025,000
c)By HQ/ACC-proj.42-appvd. 2 Oct.			
Grand Total	203,653,700	107,461,000	96,192,700

Declassified E.O. 12356 Section 3.3/NND No. 785019

A(a) AEM/dpe

Lazio - Umbria Region - ACC

Report for Month of Oct.1944- Public Works (Rome Comune)

Works approved during month at Regional Level

ITALIAN GOVERNMENT TERRITORY - ROME COMUNE

All Project approved by Regional Engineer

REF. P.W.(R.C.) assigned No.	LOCATION	PROJECT AND DESCRIPTION	ESTIMATED COST
PROJECT between 500,000 L. and 1,000,000 L.			
68	Rome City	Sewers	1,000,000 L.
69	" "	"	924,000 "
71	" "	"	820,000 "
79	Magliana	Salvage of dredge	1,000,000 "
85	Rome Comune	Bridge-Coord.597 - 764	830,000 "
108	Rome City	Clearing of Tiber	900,000 "
113	" "	"Regina Coeli" Prison	830,000 "
		T O T A L	6,304,000 L.

RECAPITULATION

One Proj. Requiring critical materials
Bridge over 3 m. .....830,000 L.
Six Proj. Not requiring critical materials 5,474,000 "

T O T A L 6,304,000 L.

PROJECTS over 1,000,000 L.

66	Rome City	Sewers	1,030,000 L.
67	" "	"	4,400,000 "
70	" "	"	1,385,000 "
72	" "	"	1,540,000 "
73	" "	"	1,100,000 "
74	" "	"	1,130,000 "
75	" "	University	1,340,000 "

17

Declassified E.O. 12356 Section 3.3/NND No. 785019

REF. P.W.(R.C.) assigned No.	LOCATION	PROJECT AND DESCRIPTION	ESTIMATED COST
76	Rome City	University	4,270,000 L.
86	Rome Comune	Bridge-Coord.597 - 746	1,820,000 "
87	Rome City	"Policlinico" Hospital	1,282,000 "
88	" "	" "	5,600,000 "
90	Fiumicino	Repair N. mole	5,000,000 "
105	Rome Comune	" main collector N.	1,200,000 "
106	" "	" " " S.	2,700,000 "
107	Rome City	Clearing of Tiber	1,150,000 "
118	Fiumicino	Repair S. mole	4,700,000 "
		T O T A L	39,647,000 L.
	Grand Total	approved in October	45,951,000 L.

17?

Declassified E.O. 12356 Section 3.3/NND No. 785019

a(b) AEM/dpe

Lazio-Umbria Region - ACC

Report for Month of Oct.'44-Pu.Works (Rome Comune)

ITALIAN GOVERNMENT TERRITORY - ROME COMUNE

Approved by COMPARTMENT INSPECTOR (Genio Civile) -Limit. 500,000

A complete list of Projects Under 500,000 L., approved by Compartment Inspector (G.C.) has been furnished your office direct, by the Genio Civile. Following is a recap of the approvals for Rome Comune area:

Water Supply - 1 proj.	85,000 L.
Other Works - 74 proj.	16,360,700 "
Non Military Roads & Bridges - 1 proj.	50,000 "
Total - 76 proj.	16,495,700 L.

. . . . . .

The above is broken down into the following categories for purposes of information:
Project that went direct from source to Genio Civile's Office for Compartment Inspector approval:

Water Supply	none
Other Works - 50 proj.	10,982,700 L.
Non Military Roads & Bridges - 1 proj.	50,000 "
Total - 51 Proj.	11,032,700 L.

- -x

Projects being processed as Pu.Wks.(R.C.) work projects with ACC-1 (some with ACC-2) documentation and started before Genio Civile had and/or understood his authority of approval up to 500,000 L.

Water Supply - 1 proj.	85,000 L.
Other Works - 24 proj.	5,378,000 "
Non Military Roads & Bridges	none
Total - 25 proj.	5,463,000 L.

(This total of 5,463,000 L. is carried in statistical summary as work approved on Reg.level basis and not included in figure of Compartment Inspector to avoid any duplication of figures.)

Grand Total (76 proj.)	16,495,700 L.	16,495,700 L.

HEADQUARTERS REGION IV
ALLIED CONTROL COMMISSION
ENGINEERING DIVISION

AEM/dpe

Ref.
Region IV-Rome Comune-Tu.Works Project N.62
Genio Civile Letter N.2058
" " Estimate N.385

Rome, 15 September 1944

30

Subject: University of Rome - Project for repair of the Orthopedic Clinic.

To : Genio Civile.
Attn. Chief Eng.Nicoli.

1. Scope of work: The project contemplates repair of the orthopedic building and adjoining machine shop, damaged by bombs exploding inside and around the buildings. The work principally consists of:
   a. Rebuilding of reinforced concrete columns and floor systems.
   b. Reconstruction of walls and partitions.
   c. Repair of fixtures and interior finishing.
   d. Whitewashing and painting.

2. Estimated cost: The total estimated cost is 3,000,000 L, divided as follows:

a. Amount estimate	2,848,000,00 L
b. Extra	152,000.00 L
T O T A L	3,000,000.00 L

3. Controlled materials: The controlled materials necessary, but not requested by Genio Civile are:
   a. Cement 95 Ql.
   b. Iron 30 "
   c. Paint 30 "

4. Recommendation: I recommend approval of the project to facilitate special cure and assistance to wounded soldiers.

5. Remarks: This work is the continuation of previous work already finished for an amount of 3,824,897 L. The present work is begun and 1/10 done. Estimated completion time: 5 months.

6. Enclosures: 3 copies of Genio Civile estimate.

Declassified E.O. 12356 Section 3.3/NND No. 785019

Region IV-Rome Sector-Pu.Works Project N.02
Genio Civile Letter N.2058
" " Estimate N.385

30

Subject: University of Rome - Project for repair of the Orthopedic Clinic.

To : Genio Civile.
Attn. Chief Eng.Nicoli.

1. Scope of work: The project contemplates repair of the orthopedic building and adjoining machine shop, damaged by bombs exploding inside and around the buildings. The work principally consists of:
   a. Rebuilding of reinforced concrete columns and floor systems.
   b. Reconstruction of walls and partitions.
   c. Repair of fixtures and interior finishing.
   d. Whitewashing and painting.

2. Estimated cost: The total estimated cost is 3,000,000 L, divided as follows:

a. Amount estimate	2,848,000,00 L
b. Extra	152,000.00 L
T O T A L	3,000,000.00 L

3. Controlled materials: The controlled materials necessary, but not requested by Genio Civile are:
   a. Cement 95 Ql.
   b. Iron 30 "
   c. Paint 30 "

4. Recommendation: I recommend approval of the project to facilitate special cure and assistance to wounded soldiers.

5. Remarks: This work is the continuation of previous work already finished for an amount of 3,824,897 L. The present work is begun and 1/10 done. Estimated completion time: 5 months.

6. Enclosures: 3 copies of Genio Civile estimate.
   3 copies of Form ACC/1.

A.E.Michel

A.E.MICHEL, Major
Pu.Works Sec. - Rome Comune

Distribution:

Genio Civile	3
Col.Jenny-attn. P.W.Sub-Commission	1 ✓
Col. Findlay	1
Major Michel	1
Files	2

Declassified E.O. 12356 Section 3.3/NND No. 785019

AEM/dpc

HEADQUARTERS REGION IV
ALLIED CONTROL COMMISSION
ENGINEERING DIVISION

Ref.
Region IV-Rome Comune-Pu.Wks.Project N.64
Genio Civile Letter N.2318
" " Estimate N.390

Rome, 18 September 1944

29

Subject: University of Rome- Project for repair of the Hygiene Institute

To : Genio Civile - Attn. Chief. Eng.Niccoli.

1. Scope of work: The project contemplates repair of the Lecture Wall and Antirabbic Section, damaged by bombs exploding inside and around the building. The work principally consists of:

a. Demolition and reconstruction of walls, partitions, concrete columns and floor systems.
b. Repair of fixtures and interior finishing.
c. Furnishing of special seats for the Lecture Wall.
d. Reconstruction of electrical and water installations.
e. Whitewashing and painting.

2. Estimated cost: The total estimated cost is 2,312,000 L. In this figure is the sum of 717,346.24 L which represents an increase of 45% to compensate for present increased cost.

3. Controlled materials: The controlled and blocked materials necessary but not requested by Genio Civile are:

a. Controlled materials:

Cement	350	Ql.
Iron	80	"
Lead	2	"
Paint	3	"

b. Blocked materials:

Bricks	60,000	N.

Declassified E.O. 12356 Section 3.3/NND No. 785019

Region IV-Rome Comune-Pu.Wks.Project N.64
Genio Civile Letter N.2318
" " Estimate N.390

29

Subject: University of Rome- Project for repair of the Hygiene Institute

To : Genio Civile - Attn. Chief. Eng.Niccoli.

1. Scope of work: The project contemplates repair of the Lecture Wall and Antirabbic Section, damaged by bombs exploding inside and around the building. The work principally consists of:

a. Demolition and reconstruction of walls, partitions, concrete columns and floor systems.
b. Repair of fixtures and interior finishing.
c. Furnishing of special seats for the Lecture Wall.
d. Reconstruction of electrical and water installations.
e. Whitewashing and painting.

2. Estimated cost: The total estimated cost is 2,312,000 L. In this figure is the sum of 717,346.24 L which represents an increase of 45% to compensate for present increased cost.

3. Controlled materials: The controlled and blocked materials necessary but not requested by Genio Civile are:

a. Controlled materials:

Cement	350 Ql.
Iron	80 "
Lead	2 "
Paint	3 "

b. Blocked materials:

Bricks	60,000 N.
Lime	200 Ql.

4. Recommendation: I recommed approval of the project.

5. Remarks: Some essential work for antirabbic Section is already done, but is not included in the present estimate.

6. Enclosures: 3 copies of Genio Civile estimate
3 copies of Form ACC/1.

A.E.MICHEL, Major
Pu.Wks.Section-Rome Comune

173

Distribution:

Genio Civile	3
Col.Jenny-attn.P.W.Sub-Commission	1 ✓
Col.Findlay	1
Maj.Michel	1
Files	1

Declassified E.O. 12356 Section 3.3/NND No. 785019

HEADQUARTERS
ALLIED MILITARY GOVERNMENT
LAZIO- UMBRIA REGION
(Engineering Division)
APO 394

ABF/dpe

P.W. (R.C.) Project n.88
Genio Civile Letter n.2852
" " Estimate n.398

Rome, 11 October 1944

Subject: Project for repair of several war damaged buildings of Poli-clinic Hospital "Umberto I" Rome.

To : Genio Civile - Attn. Chief Engineer Nicoli.

1. Scope of work: The project contemplates the most urgent repairs necessary to put in working efficiency the "Umberto I" Hospital damaged by bombing on 18th/3/44. The buildings more seriously hit are:

Three surgery pavilions, the X Ray Institute, the Paediatric pavilion, the central thermic and laundry buildings. All the other buildings have been more or less damaged especially as regards fixtures and window panes. The work mainly consists of:

a. Demolition and reconstruction of walls, floor systems and partitions.

b. Reconstruction or repair of roofs and terraces.

c. Reconstruction or repair of radiologic, telephonic, electric systems.

d. Water installation repair, white washing and painting.

2. Estimated cost: The total estimated cost is 5,600,000 L. Prices are based on current market costs.

3. Controlled materials: The controlled materials necessary, but not requested by Genio Civile are:

a. Controlled materials:

-Cement	300	Ql.	-	Brass	0.50	Ql.
-Iron	30	"	-	Paint	12	"
-Lead	1.75	"				

b. Blocked materials:

Declassified E.O. 12356 Section 3.3/NND No. 785019

P.W. (R.C.) Project n.88
Genio Civile Letter n.2852
" " Estimate n.398

Rome, 11 October 1944

Subject: Project for repair of several war damaged buildings of Poli-clinic Hospital "Umberto I" Rome.

To : Genio Civile - Attn. Chief Engineer Nicoli.

1. Scope of work: The project contemplates the most urgent repairs necessary to put in working efficiency the "Umberto I" Hospital damaged by bombing on 18th/3/44. The buildings more seriously hit are:

Three surgery pavilions, the X Ray Institute, the Paediatric pavilion, the central thermic and laundry buildings. All the other buildings have been more or less damaged especially as regards fixtures and window panes. The work mainly consists of:

a. Demolition and reconstruction of walls, floor systems and partitions.

b. Reconstruction or repair of roofs and terraces.

c. Reconstruction or repair of radiologic, telephonic, electric systems.

d. Water installation repair, white washing and painting.

2. Estimated cost: The total estimated cost is 5,600,000 L. Prices are based on current market costs.

3. Controlled materials: The controlled materials necessary, but not requested by Genio Civile are:

a. Controlled materials:

-Cement	300	Ql.	- Brass	0.50	Ql.
-Iron	30	"	- Paint	12	"
-Lead	1.75	"			

b. Blocked materials:

-Bricks	70,000	n.	- Lime	500	Ql.
-Tiles	1,200	"			

4. Recommendation: This project is approved in principle. Work is mostly let out and part of it is already done. Forms ACC/1 and ACC/2 relative to 16 stipulated contracts totalling 3,215,600 L. are returned approved. The remaining work will be done by direct labor.

5. Enclosures: 3 copies approved Form ACC/1.
3 copies approved of Form ACC/2
for each of 16 contracts.

A.B.MICHEL, Major, S.R.
for Regional Engineer
Lazio-Umbria Region (PW-RC)

Distribution:
Col. Jenny - Att.P.W.Sub-Commission 1
Col. Findlay 2

173

Declassified E.O. 12356 Section 3.3/NND No. 785019

AEW/dpe

HEADQUARTERS
ALLIED MILITARY GOVERNMENT
LAZIO- UMBRIA REGION
(Engineering Division)
APO 394

Ref.
P.W. (R.C.) Project n.76
Genio Civile Letter n.2316
" " Estimate n.389

Rome, 5 October 1944

Subject: University of Rome - Project for repair of "Phisiology Institute"

To : Genio Civile - Att. Chief Engineer Niccoli.

1. Scope of work: The project contemplates repair of the left anterior wing of the building, damaged by bombs on 19th/7/43. The work principally consists of:

a. Demolition and reconstruction of walls, partitions, concrete columns and floor systems in order to avoid further damages of the building.

b. Repair of fixtures.

c. Furnishing of panes.

d. Repair of installations of several scientific laboratories.

2. Estimated cost: The total estimated cost is 4,270,000 L. In this figure is the sum of 796,111,05 L which represents an increase of 45% to compensate for present increased prices.

3. Controlled materials -

	Requested by Genio Civile	Judged as necessary according to the estimate
a. Cement	300 ql.	150 ql.
b. Iron	60 "	50 "
c. Lead	40 "	40 "
d. Tin	1 "	0,3"
e. Paint	5 "	5 "

4. Recommendation: This project is approved in principle.

5. Remarks: This work is the continuation of previous work already

Declassified E.O. 12356 Section 3.3/NND No. 785019

A.R. (R.O.) Project n.75
Genio Civile Letter n.2316
" " Estimate n.389

Subject: University of Rome - Project for repair of "Phisiology Institute"

To : Genio Civile - Att. Chief Engineer Niccoli.

1. Scope of work: The project contemplates repair of the left anterior wing of the building, damaged by bombs on 19th/7/43. The work principally consists of:

a. Demolition and reconstruction of walls, partitions, concrete columns and floor systems in order to avoid further damages of the building.

b. Repair of fixtures.
c. Furnishing of panes.
d. Repair of installations of several scientific laboratories.

2. Estimated cost: The total estimated cost is 4,270,000 L. In this figure is the sum of 798,111,05 L which represents an increase of 45% to compensate for present increased prices.

3. Controlled materials -	Requested by Genio Civile	Judged as necessary according to the estimate
a. Cement	300 Ql.	150 Ql.
b. Iron	60 "	50 "
c. Lead	40 "	40 "
d. Tin	1 "	0,3"
e. Paint	5 "	5 "

4. Recommendation: This project is approved in principle.

5. Remarks: This work is the continuation of previous work already finished for an amount of 582,000 L. The original estimate of 5,000,000 L was reduced to 4,270,000, with detraction of some not indispensable work of finishing, as painting, plastering, etc.

6. Enclosures: 3 copies approved Form ACC/1.

A.R.MICHEL 17/37

A.R.MICHEL, Major
for Regional Engineer
Lazio - Umbria Region

Distribution:
Col. Jenny-Att.P.W.Sub-Comm. 1 ✓
Col. Findlay 2

Declassified E.O. 12356 Section 3.3/NND No. 785019

AEM/dpe

HEADQUARTERS
ALLIED MILITARY GOVERNMENT
LAZIO- UMBRIA REGION
(Engineering Division)
APO 394

Ref.
P.W. (R.C.) Project n.75
Genio Civile Letter n.2317
" " Estimate n.391

Rome, 5 October 1944

Subject: R.University of Rome. Project for repair of the "Literature" building with annexed Gypsum Museum.

To : Genio Civile - Att. Gen.Inspector Niccoli.

1. Scope of work: The building was damaged by bombs on 19th/7/43 and 9th/8/43. The work of repair consists principally of:
a. Demolitions.
b. Reconstruction of walls, partitions and floor systems.
c. Repair of fixtures and interior finishing, reduced to the most indispensable necessary.

2. Estimated cost: The estimated cost is 1,340,000 L divided as follows:

- Amount estimated	923,927 L.
- 45% Increase on amount to compensate for present increased cost	415,767 "
- Extras	306 "
T O T A L	£,340,000 L.

3. Controlled materials: Only small quantities and no request by Genio Civile. Iron necessary is salvaged material.

4. Recommendation: I recommend approval of the project.

5. Remarks: The original estimate of 1,610,000 L was reduced to 1,340,000 L, with detraction of some not indispensable work of finishing as varnishing, plastering etc. Estimated completion time: 4 months.

6. Enclosures: 3 copies approved Form ACC/1.

Declassified E.O. 12356 Section 3.3/NND No. 785019

Subject: R.University of Rome. Project for repair of the "Literature" building with annexed Gypsum Museum.

To : Genio Civile - Att. Gen.Inspector Riccoli.

1. Scope of work: The building was damaged by bombs on 19th/7/43 and 9th/8/43. The work of repair consists principally of:

a. Demolitions.

b. Reconstruction of walls, partitions and floor systems.

c. Repair of fixtures and interior finishing, reduced to the most indispensable necessary.

2. Estimated cost: The estimated cost is 1,340,000 L divided as follows:

- Amount estimated	923,927	L.
- 45% Increase on amount to compensate for present increased cost	415,767	"
- Extras	306	"
T O T A L	1,340,000	L.

3. Controlled materials: Only small quantities and no request by Genio Civile. Iron necessary is salvaged material.

4. Recommendation: I recommend approval of the project.

5. Remarks: The original estimate of 1,610,000 L was reduced to 1,340,000 L. with detraction of some not indispensable work of finishing as varnishing, plastering etc. Estimated completion time: 4 months.

6. Enclosures: 3 copies approved Form ACC/1.

A.E.Michel

A.E.MICHEL, Major
for Regional Engineer
Lazio - Umbria Region

1736

Distribution:

Col. Jenny - Att.P.W.Sub-Commission 1
Col. Findlay 2

Declassified E.O. 12356 Section 3.3/NND No. 785019

ANN/dpe

HEADQUARTERS
ALLIED MILITARY GOVERNMENT
LAZIO- UMBRIA REGION
(Engineering Division)
APO 394

Roma, 17 October 1944

Ref.
P.W. (R.C.) Project n.86
Rome Comune Estimate n.55124

Subject: Project for rebuilding the reinforced concrete bridge over the "Arrone" river on the "Boccea" road. (Coord. 597 - 746).

To : Att. General Inspector Granoni.

1. Scope of work: The work contemplated in this project on the above mentioned bridge which was damaged by mines, consists principally of:

a. Demolition and clearing of the materials heaped in the canal bed.
b. Rebuilding of the damaged parts of the two masonry abutments.
c. Building of the bridge beams in reinforced concrete.
d. Finishing work and approaches.

2. Estimated cost: L. 1,655,000 + 165,000 (extras) = L. 1,820,000.

3. Controlled materials:

a. Cement	Ql.	360
b. Reinforcing steel	"	100

Blocked materials:

a. Lime	Ql.	240	-	d. Gasoline	L. 8,000
b. Bitumen	"	9	-	e. Lubricant	Ql. 2.50
c. Asphalt	"	12	-		

4. Recommendation: This project is approved in principle. The clearing of the canal bed is urgent in order to avoid a flood situation [illegible] and the reconstruction of the bridge is urgently

Declassified E.O. 12356 Section 3.3/NND No. 785019

Roz.
F.W. (R.C.) Project n.86
Rome Commune Estimate n.55124

Roma, 17 October 1944

Subject: Project for rebuilding the reinforced concrete bridge over the "Arrone" river on the "Boccea" road. (Coord. 597 - 746).

To : Att. General Inspector Crononi.

1. Scope of work: The work contemplated in this project on the above mentioned bridge which was damaged by mines, consists principally of:

a. Demolition and clearing of the materials heaped in the canal bed.
b. Rebuilding of the damaged parts of the two masonry abutments.
c. Building of the bridge beams in reinforced concrete.
d. Finishing work and approaches.

2. Estimated cost: L. 1,655,000 + 165,000 (extras) = L. 1,820,000.

3. Controlled materials:

a. Cement	Ql.	360
b. Reinforcing steel	"	100

Blocked materials:

a. Lime	Ql.	240	-	d. Gasoline	L.	8,000
b. Bitumen	"	9	-	e. Lubricant	Ql.	2.50
c. Asphalt	"	12	-			

4. Recommendation: This project is approved in principle. The clearing of the canal bed is urgent in order to avoid a flood situation during the wet season, and the reconstruction of the bridge is urgently needed for traffic reasons.

5. Remarks: The bridge will be rebuilt with reinforced concrete beams, in order to lighten the dead load and to employ the existing foundation which are not apt to sustain an arched structure. Time requested: 120 days.

6. Enclosures: 3 copies approved Form ACO/1.
3 copies of plan.

A.E.Michel 1735

A.E.MICHEL, Major, C.E.
for Regional Engineer
Lazio - Umbria Region

Distribution:

Col.Jenny-Att.P.W.Sub-Comm. 1 ✓
Col. Findlay 1

Declassified E.O. 12356 Section 3.3/NND No. 785019

AEM/dpe

HEADQUARTERS
ALLIED MILITARY GOVERNMENT
LAZIO- UMBRIA REGION
(Engineering Division)
APO 394

Ref.
P.W. (R.C.) Project n.66
Genio Civile Letter n.2148

Rome, 4 October 1944

Subject: Repair of parts of the sewers in "Via Casilina" and "Via Acqua Bulicante" (Plan n.65092).

To : Rome Commune: Att.: Gen.Inspector Granoni.

1. Scope of work: The above sewers were damaged by bombs on 20/1 1944. The repair consists principally of:
   a. Total rebuilding of the destroyed parts of the sewers.
   b. Clearing of the sewers.

2. Estimated cost: L. 1,030,000 (extras included).

3. Controlled materials: None needed as work is completed.

4. Recomendation: This project is approved in principle. Work has been done in order to avoid backing up of sewerage wastes and to permit the repair of the damaged streets.

5. Enclosures: 3 copies approved Form ACC/1.

A.E.MICHEL, Major
for Regional Engineer
Lazio - Umbria Region

Distribution:
Col. Jenny - Att. P.W. Sub-Commission 1

Declassified E.O. 12356 Section 3.3/NND No. 785019

Genie Civile Letter n.2148

Subject: Repair of parts of the sewers in "Via Casilina" and "Via Acqua Bulicante" (Plan n.65092).

To : Roma Comune: Att.: Gen.Inspector Granoni.

1. Scope of work: The above sewers were damaged by bombs on 20/1 1944. The repair consists principally of:
   a. Total rebuilding of the destroyed parts of the sewers.
   b. Clearing of the sewers.
   c.

2. Estimated cost: L. 1,030,000 (extras included).

3. Controlled materials: None needed as work is completed.

4. Recomendation: This project is approved in principle. Work has been done in order to avoid backing up of sewerage wastes and to permit the repair of the damaged streets.

5. Enclosures: 3 copies approved Form ACC/1.

A.B.Michel

A.B.MICHEL, Major
for Regional Engineer
Lazio - Umbria Region

Distribution:

Col. Jenny - Att. P.W. Sub-Commission 1 ✓
Col. Findlay 2

1734

Declassified E.O. 12356 Section 3.3/NND No. 785019

AEM/dpe

HEADQUARTERS
ALLIED MILITARY GOVERNMENT
LAZIO-UMBRIA REGION
(Engineering Division)
APO 394

Ref.
P.W. (R.C.) Project n. 67
Genio Civile Letter n.2149
" " Estimate n.1819

Rome, 4 October 1944

Subject: Repair of the "Marranella" sewer-collector in its part near "Via Baldissera" and "Via di Villa Mercucci" (Plan n.65096).

To : Rome Commune - Att. Chief Inspector Granone.

1. Scope of work: The above sewer-collector was badly damaged by bombs on 14th/3/44. The repair consists principally of:
a. Total rebuilding of 140 m. of collector (III ed V type).
b. Rebuilding of 40 m. of the collector vault.
c. Rebuilding of three inspection wells.
d. Clearing of the collector from "Via Livorno" (near Tiburtina Station), to "Via Baldissera" (near Prenestina Station).

2. Estimate cost: L. 4,400,000 (extras included).

3. Controlled materials: The required controlled material is already in store for the works.

4. Recommendation: This project is approved in principle. The work is already begun in order to avoid back water and ower flow of sewerage wastes. At present works are 1/3 completed.

5. Remarks: Probable completion time: 180 days.

6. Enclosures: 3 copies approved Form ACC/1.

C.E. Michel

Declassified E.O. 12356 Section 3.3/NND No. 785019

Ref.
P.W. (R.C.) Project n. 67
Genio Civile Letter n.2149
" " Estimate n.1819

Rome, 4 October 1944

Subject: Repair of the "Marranella" sewer-collector in its part near "Via Baldissera" and "Via di Villa Nerducci" (Plan n.65096).

To : Rome Comune - Att. Chief Inspector Granone.

1. Scope of work: The above sewer-collector was badly damaged by bombs on 14th/3/44. The repair consists principally of:
   a. Total rebuilding of 140 m. of collector (III ed V type).
   b. Rebuilding of 40 m. of the collector vault.
   c. Rebuilding of three inspection wells.
   d. Clearing of the collector from "Via Livorno" (near Tiburtina Station), to "Via Baldissera" (near Prenestina Station).

2. Estimate cost: L. 4,400,000 (extras included).

3. Controlled materials: The required controlled material is already in store for the works.

4. Recommendation: This project is approved in principle. The work is already begun in order to avoid back water and ower flow of sewerage wastes. At present works are 1/3 completed.

5. Remarks: Probable completion time: 180 days.

6. Enclosures: 3 copies approved Form ACC/1.

A.E. Michel

A.E. MICHEL, Major
for Regional Engineer
Lazio - Umbria Region

Distribution:

Col. Jenny - Att. P.W. Sub-Commission 1 ✓
Col. Findley 2

1733

Declassified E.O. 12356 Section 3.3/NND No. 785019

AMW/dpo

HEADQUARTERS
ALLIED MILITARY GOVERNMENT
LAZIO -UMBRIA REGION
(Engineering Division)
APO 394

Rome, 4 October 1944

Ref.
P.W. (R.C.) Project n.70
Genio Civile Letter n.2152
" " Estimate n.1822

Subject: Repair of parts of sewers in Via Nazzaro, Piazza Biffi, Via Lasagna , Circonvallazione Ostiense. (Plan. n.63093).

To : Comune di Roma: Att. Gen.Inspector Grassoni.

1. Scope of work: Reconstruction and repair of sewers damaged by bombs, mainly consisting of:
a. Excavation, clearing and transport of debris.
b. Reconstruction of 280 ml. of sewers type VII and 6 bis.
c. Refilling of excavation etc.

2. Estimated cost: The estimated cost is L.1,260,000 plus L. 125,000 for extras. Total L. 1,385,000.

3. Controlled materials: None needed as work is completed.

4. Recommendation: This project is approved in principle. Work has been completed because of urgent necessity of doing at once in order to avoid back water and overflow of sewage wates.

5. Enclosures: 3 copies approved Form ACC/1.
3 " " " ACC/2

A.B.Michel

A.B.MICHEL, Major
for Regional Engineer
Lazio - Umbria Region

Distribution:
Sel. Issue - Att. P.W. Sub-Commission 1

Declassified E.O. 12356 Section 3.3/NND No. 785019

Subject: Repair of parts of sewers in Via Nascaia, Piazza Rifil, Via Lasagna , Circonvallazione Catiense. (Plan. n.65053).

To : Comune di Roma: Att. Gen.Inspector Cranoni.

1. Scope of work: Reconstruction and repair of sewers damaged by bombs, mainly consisting of:
   a. Excavation, clearing and transport of debris.
   b. Reconstruction of 280 ml. of sewers type VII and 6 bis.
   c. Refilling of excavation etc.

2. Estimated cost: The estimated cost is L.1,260,000 plus L. 125,000 for extras. Total L. 1,385,000.

3. Controlled materials: None needed as work is completed.

4. Recommendation: This project is approved in principle. Work has been completed because of urgent necessity of doing at once in order to avoid back water and overflow of sewage wastes.

5. Enclosures: 3 copies approved Form ACC/1.
   3 " " ACC/2

A.E.MICHEL, Major
for Regional Engineer
Lazio - Umbria Region

Distributions:

Col. Jenny - Att. P.W. Sub-Commission 1
Col. Findley 2

1732

Declassified E.O. 12356 Section 3.3/NND No. 785019

AMB/dpe

HEADQUARTERS
ALLIED MILITARY GOVERNMENT
LAZIO- UMBRIA REGION
(Engineering Division)
APO 394

Ref.
P.W. (R.C.) Project n.74
Genio Civile Letter n.2252
" " Estimate n.1849

Rome, 5 October 1944

Subject: Repair of parts of sewers in Via Giovanni da Empoli, Via dei Conciatori, Via delle Conce, Viale del Re. (Plan. n.65095).

To : Rome Comune: Att. Gen.Inspector Granoni.

1. Scope of work: Reconstruction and repair of sewers damaged by bombs, mainly consisting of:
a. excavation, clearing and transport of debris.
b. Reconstruction of 200 ml. sewers type VIII, VII and VI.
c. Refilling of excavation etc.

2. Estimated cost: The estimated cost is L. 1,030,000 plus L. 100,000 for extras. Total L. 1,130,000.

3. Controlled materials: None needed as work is almost finished.

4. Recommendation: This project is approved in principle. Work has been done because of urgent necessity of repairs being completed at once in order to avoid back water and overflow of sewerage wastes.

5. Enclosures: 3 copies approved Form ACC/1.
3 " " " ACC/2

A.E.MICHEL, Major
for Regional Engineer
Lazio - Umbria Region

Distribution:

Col. Jenny - Att.P.W.Sub-Commission 1
Col. Findlay 2

Declassified E.O. 12356 Section 3.3/NND No. 785019

AEM/dpe

HEADQUARTERS
ALLIED MILITARY GOVERNMENT
LAZIO- UMBRIA REGION
(Engineering Division)
APO 394

Ref.
P.W. (R.C.) Project n.90
Genio Civile File n.2487

Rome, 5 October 1944

Subject: Repair of the North Mole of "Fiumicino" harbour.

To : Genio Civile - Att.Chief Engineer Bellomo.

1. Scope of work: The work consists principally of: Construction and settlement of concrete blocks (821 mc.) for the repair of breaks in the above mole.

2. Estimated cost: L. 5,000,000.

3. Controlled material:
   a. Timbers mc. 20
   b. Cement ql. 280

4. Recommendation: This project is approved in principle. Work is urgently needed in order to avoid further damage to the mole and reestablish navigation in-to Fiumicino Harbor.

5. Remarks: Estimate time required: 90 days.

6. Enclosures: 3 copies approved Form ACO/1.

A.E.MICHEL, Major
for Regional Engineer
Lazio - Umbria Region

Distribution:

Col. Jenny - Att.P.W.Sub-Commission 1
Col. Findlay 2

Declassified E.O. 12356 Section 3.3/NND No. 785019

AEM/dpe

HEADQUARTERS
ALLIED MILITARY GOVERNMENT
LAZIO- UMBRIA REGION
(Engineering Division)
APO 394

Ref.
P.W. (R.C.) Project n.87
Genio Civile Letter n.2387
" " Estimate n.392

Roma, 5 October 1944

Subject: "Policlinico Umberto I" Hospital. Repair of war damages in the Radiology, Medical Pathology and Chemical Patology Sections.

To : Genio Civile - Att. Gen.Inspector Alicata.

1. Scope of work: The project contemplates repair and painting of fixtures and wall partitions.

2. Estimated cost: The total amount of the estimate is 1,282,000 L. In this figure is the sum of 398,278 L which represents an increase of 45% over the original figures, to compensate for present increased cost.

3. Controlled materials: Controlled materials necessary but not requested by Genio Civile:
a. Paint 20 Ql.

4. Recommendation: This project is approved in principle.

5. Remarks: The work has started partially by contracts (awarded in June 1944) and partially by direct labour. Probable time for completion: 3 months.

6. Enclosures: 3 copies approved Form ACC/1.

A.E.Michel

A.E.MICHEL, Major
for Regional Engineer
Lazio - Umbria Region

Distribution:

Col. Jenny - Att. P.W.Sub-Commission 1
Col. Findlay 2

Declassified E.O. 12356 Section 3.3/NND No. 785019

AEM/dpe

HEADQUARTERS
ALLIED MILITARY GOVERNMENT
LAZIO- UMBRIA REGION
(Engineering Division)
APO 394

Ref.
P.W. (R.C.) Project No.72
Genio Civile Letter No.2250
" " Estimate No.1847

Rome, 4 October 1944

Subject: Repair of parts of the sewers in "Nomentana", "Pola", "C.Fea", "G.B. De Rossi", streets - (Plan No.65100).

To : Rome Comune: att. Chief Engineer Cranconi.

1. Scope of work: The above sewers were damaged by bombs on 16/3/44. The repairs consist principally of:
a. Total rebuilding of 330 m. of sewers (miscellaneous types).
b. Cleaning of the sewers.

2. Estimated cost: L. 1,540,000 (extras included).

3. Controlled material: None needed as work is completed.

4. Recommendation: This project is approved in principle. Work has been done in order to avoid backing up of sewerage wastes and to permit the repair of the damaged streets.

5. Enclosures: 3 copies approved Form ACC/1.

A.E.MICHEL, Major
for Regional Engineer
Lazio - Umbria Region

Distribution:

Col. Jenny & att.P.W. Sub-Commission 1
Col. Findlay 2

Declassified E.O. 12356 Section 3.3/NND No. 785019

AEM/dpe

HEADQUARTERS
ALLIED MILITARY GOVERNMENT
LAZIO- UMBRIA REGION
(Engineering Division)
APO 394

Ref.
P.W. (R.C.) Project n.73
Genio Civile Letter n.2251
" " Estimate n.1848

Rome, 5 October 1944

Subject: Repair of parts of the sewers in "Via Matteucci" and "Via Bonsoni".

To : Rome Commune. Att. Gen.Inspector Granconi.

1. Scope of work: The above sewers were damaged by bombs on 7/3/44. The repair principally consist of:
a. Rebuilding of the destroyed parts of the sewers.
b. Clearing of the sewers.

2. Estimated cost: L. 1,100,000 (extras included).

3. Controlled material: The required controlled materials are already in store for the works.

4. Recommendation: This project is approved in principle. The work is already begun and 1/2 completed in order to avoid sewerage wastes and to re-establish the traffic in the damaged streets.

5. Remarks: Probable time for completion: 100 days.

6. Enclosures: 3 copies approved Form ACC/1.

A.R.Michel

A.R.MICHEL, Major
for Regional Engineer
Lazio - Umbria Region

Distribution:

Col. Jenny - Att.P.W.Sub-Commission 1
Col. Findlay 2

Declassified E.O. 12356 Section 3.3/NND No. 785019

ALM/dpe

HEADQUARTERS
ALLIED MILITARY GOVERNMENT
LAZIO- UMBRIA REGION
(Engineering Division)
APO 394

16

Ref.
P.W. (R.O.) Project n.107
Genio Civile Letter n.2721

Rome, 20 October 1944

Subject: Clearing of the vegetation and alluvial materials deposited at the bottom of the Tiber wall, left side, between "Vittorio Emanuele" bridge and "Mazzini" bridge.

To : Genio Civile - Att.Chief Eng. Bellomo.

1. Scope of work: The work consists principally of the removal and dumping in the Tiber, of the above vegetation and alluvial materials.

2. Estimated cost: L. 1,150,000.

3. Controlled materials: None needed.

4. Recommendation: This project is approved in principle. The above is located at a bend in the Tevere which has caused a depositing of silt and vegetation growth, thus lowering the flood capacity of the channel.

5. Remarks: Probable time for completion: 30 days.

6. Enclosures: 3 copies approved of Form ACC/1.

A.L.Michel

A.L.MICHEL, Major, S.R.
for Regional Engineer
Lazio - Umbria Region

Distribution:

Col. Jenny - Att.P.W.Sub-Comm. 1
Col. Findley 1

Declassified E.O. 12356 Section 3.3/NND No. 785019

AEM/dpe

HEADQUARTERS
ALLIED MILITARY GOVERNMENT
LAZIO- UMBRIA REGION
(Engineering Division)
APO 394

15

Ref.
P.W. (R.C.) Project n.1;8
Genio Civile Letter n. 2772

Rome, 21 October 1944

Subject: Repair of the South (left) Mole of "Fiumicino" Harbor..

To : Genio Civile - Att. Chief Eng. Bellomo.

1. Scope of work: The work consists principally of construction and settlement of concrete blocks (670 mc.) for the repair of breaks in the above mole.

2. Estimated cost: L. 4,700,000.

3. Controlled materials:

a. Timbers	mc.	20	(Rationed)
b. Cement	ql.	670	(Rationed)
c. Gasoline	l.	7,000	(Rationed)

4. Recommendation: This project is approved in principle. Work is urgently needed in order to avoid further damage to the mole and reestablish navigation into Fiumicino Harbor.

5. Remarks: Estimated time required: 150 days.

6. Enclosures: 3 copies approved of Form AGO/1.

A.M.Michel

A.M.MICHEL, Major, S.R.
for Regional Engineer
Lazio - Umbria Region

Distribution:

Col. Jenny - P.W.Sub-Comm. 1
Col. Findlay 1

Declassified E.O. 12356 Section 3.3/NND No. 785019

ABM/dpe

HEADQUARTERS
ALLIED MILITARY GOVERNMENT
LAZIO- UMBRIA REGION
(Engineering Division)
APO 394

Ref.
P.W. (R.C.) Project n.105
Genio Civile Letter n.2719

Rome, 19 October 1944

Subject: Reconstruction of two tracts of the left main outfall sewer collector in Rome, up stream from the "Mezzocammino" bridge.

To : Genio Civile - Att.Chief Eng. Bellomo.

1. Scope of work: The work consists principally of:
a. Removal of the debris and clearing of the collector.
b. Reconstruction of two tracts (about m.15 and m.10 of the collector damaged by bombs.

2. Estimated cost: L. 1,200,000 (extras included).

3. Controlled materials: Cement Ql. 100.
Blocked materials: Gasoline l. 400
Lime Ql. 300
Bricks no40,000

4. Recommendation: This project is approved in principle. The work is urgent in order to reestablish the continuity of the collector.

5. Remarks: Estimate time required: 90 days.

6. Enclosures: 3 copies approved of Form ACC/1.

A.E.Michel

A.E.MICHEL, Major, S.R.
for Regional Engineer
Lazio - Umbria Region

Distribution:

Col. Jenny - Att.P.W.Sub-Comm. 1
Col. Findlay 1

Declassified E.O. 12356 Section 3.3/NND No. 785019

AEM/dpe

HEADQUARTERS
ALLIED MILITARY GOVERNMENT
LAZIO- UMBRIA REGION
(Engineering Division)
APO 394

13

Ref.
P.W. (R.C.) Project n.106
Genio Civile Letter n.2720

Rome, 19 October 1944

Subject: Reconstruction of two tracts of the left main outfall sewer collector in Rome down stream from the "Mezzocamino" bridge.

To : Genio Civile - Att. Chief Eng. Bellomo.

1. Scope of work: The work consists principally of:
a. Removal of the debris and clearing of the collector.
b. Reconstruction of two tracts (about m.20 and m.50) of the collector damaged by bombs.

2. Estimated cost: L. 2,700,000 (extras included).

3. Controlled materials: None requested by Genio Civile.

4. Recommendations: This project is approved in principle. The work is urgent in order to re-establish the continuity of the collector.

5. Remark: Estimate time required: 90 days.

6. Enclosures: 3 copies approved of Form AGC/1.

A.E. Michel

A.E. MICHEL, Major, S.R.
for Regional Engineer
Lazio - Umbria Region

Distribution:

Col. Jenny - Att. P.W. Sub-Comm. 1
Col. Findlay 1

Declassified E.O. 12356 Section 3.3/NND No. 785019

AEM/dpe

HEADQUARTERS
ALLIED MILITARY GOVERNMENT
LAZIO- UMBRIA REGION
(Engineering Division)
APO 394

Rome, 2 November 1944

P.W. (R.C.) Project n.116
Genio Civile Letter n.2654
Rome Commune Project n.65086

Subject: Repair of parts of P.P.S.S. galleries and sewers in "Prenestina" street and sewers in "Ettore Fieramosca" street.

To : Genio Civile - Att.General Inspector Facesda.

1. Scope of work: The above sewers and galleries were damaged by bombs. The work consists principally of:
a. Removal of the debris and clearing of the galleries.
b. Reconstruction of ml. 180 of P.P.S.S. and ml.190 of sewers in Prenestina street.
c. Reconstruction of ml.150 of sewers in Ettore Fieramosca street.

2. Estimated cost: L. 2,350,000 (extras included)

3. Controlled materials: None requested by Genio Civile.

4. Recommendation: This project is approved in principle. The work is urgent in order to reestablish the continuity of the gallery.

5. Remarks: Work is 70% completed. Estimated time required: 90 days.

6. Enclosures: 3 copies approved of Form ACC/1.
3 copies approved of Form ACC/2.

A.E.Michel

A.E.MICHEL, Major, S.R.
for Regional Engineer
Lazio - Umbria Region

Distribution:
P.W. Sub-Commission 1 ✓
Regional Engineer 1

1729

Declassified E.O. 12356 Section 3.3/NND No. 785019

AEM/dpe

HEADQUARTERS
ALLIED MILITARY GOVERNMENT
LAZIO- UMBRIA REGION
(Engineering Division)
APO 394

Ref.
P.W. (R.C.) Project n.121
Genio Civile Letter n.2865

Roma, 13 November 1944

Subject: Reconstruction of 250 m. of right quay of Fiumicino Harbor.

To : Genio Civile Tevere and Agro Romano.

1. Scope of work: The right quay of the Fiumicino navigation canal or harbor has been seriously damaged for an approximate lenght of 1200 m. The damage sustained was caused by mining the canal side of quay at 18 to 20 foot intervals. The left quay, having only a very few short stretches mined, is much less damaged. The left quay is not accesible for use because of complete destruction of the swing bridge at Fiumicino and the "Scafa" bridge over the Tiber connecting with the Rome-Ostia road. Most of the mines were placed above water level and apparently the reinforced concrete foundation piling has not been seriously damaged. This project contemplates repair of the quay starting at the east end of Pza.Garibaldi and extending toward the sea for a distance of 250 m. or the part of the quay serviced by rail road trackage.

2. Estimated cost: L. 5,900,000.

3. Controlled materials: Cement Ql1. 500 - Reinforcing steel Ql.100
Blocked Materials: Bricks 32,000 - Timber mc.10 - Lime Ql.400
Gasoline 10,000 l.

4. Recommendation: This project is approved in principle. It is urgent in order to prevent:
a. Further damage to the remaining part of the quay;
b. To provide dock facilities;
c. Repair part of the work that will ultimately have to be done in order to prevent future flooding of the town of Fiumicino.At presant a large number of the breaks permit water at high stage to pass thru the quay and into the town of Fiumicino.

5. Remarks: It is proposed to reconstruct the walls with "tufo" masonry with brick facing of which about half can be done with salvaged material. Estimated time of completion: 120 days.

6. Enclosures: 3 copies of approved form ACC/1. 1722

A.E.Michel

A.E.MICHEL, Major, S.R.

Declassified E.O. 12356 Section 3.3/NND No. 785019

Genio Civile Letter n.2965 , 13 November 1944

Subject: Reconstruction of 250 m. of right quay of Fiumicino Harbor.

To : Genio Civile Tevere and Agro Romano.

1. Scope of work: The right quay of the Fiumicino navigation canal or harbor has been seriously damaged for an approximate lenght of 1200 m. The damage sustained was caused by mining the canal side of quay at 18 to 20 foot intervals. The left quay, having only a very few short stretches mined, is much less damaged. The left quay is not accesible for use because of complete destruction of the swing bridge at Fiumicino and the "Scafa" bridge over the Tiber connecting with the Rome-Ostia road. Most of the mines were placed above water level and apparently the reinforced concrete foundation piling has not been seriously damaged. This project contemplates repair of the quay starting at the east end of Pza.Garibaldi and extending toward the sea for a distance of 250 m. or the part of the quay serviced by rail road trackage.

2. Estimated cost: L. 5,900,000.

3. Controlled materials: Cement Ql1. 500 - Reinforcing steel Ql.100
Blocked Materials: Bricks 32,000 - Timber mc.10 - Lime Ql.400
Gasoline 10,000 l.

4. Recommendation: This project is approved in prineiple. It is urgent in order to prevent:
a. Further damage to the remaining part of the quay;
b. To provide dock facilities;
c. Repair part of the work that will ultimately have to be done in order to prevent future flooding of the town of Fiumicino.At present a large number of the breaks permit water at high stage to pass thru the quay and into the town of Fiumicino.

5. Remarks: It is proposed to reconstruct the walls with "tufo" masonry with brick facing of which about half can be done with salvaged material. Estimated time of completion: 120 days.

6. Enclosures: 3 copies of approved form ACC/1.

1727

A.E.Michel

A.E.MICHEL, Major, S.R.
for Regional Engineer
Lazio - Umbria Region

Distribution:

P.W.Sub-Comm AC 1 ✓
Regional Engineer 1

Declassified E.O. 12356 Section 3.3/NND No. 785019

HEADQUARTERS
ALLIED MILITARY GOVERNMENT
LAZIO- UMBRIA REGION
(Engineering Division)
APO 394

ABM/dpe

Ref.
P.W. (R.C.) Project n.114
Rome Comune Project (1°, 2° lot) n.65087 and 65105

Rome, 11 November 1944

Subject: Repair of tracts of FF.SS. galleries and sewers in "Ostiense" street.

To : Rome Comune - Att.: General Inspector Faceends.

1. Scope of work: Both galleries and sewers are located on each side of the wide parkway street and were damaged by bombs. The project contemplates the reconstruction of the part of the FF.SS. galleries and sewers lying between Ostiense square and General Market. Total length of reconstruction approximately m.800.

2. Estimated cost: L. 3,590,000 (extras included).

3. Controlled materials: Not requested.

4. Recommendation: This project is approvediin principle. The work is started and at present is approximately 90% completed.

5. Remarks: Probable time of completion: 90 days.

6. Enclosures: 3 copies approved of Form ACC/1
3 copies approved of Form ACC/2 (1° lot)
3 copies approved of Form ACC/2 (2° lot)

A.E.MICHEL, Major, S.E.
for Regional Engineer

Declassified E.O. 12356 Section 3.3/NND No. 785019

Ref.
P.W. (R.C.) Project n.114
Rome Comune Project (1°, 2° lot) n.65087 and 65105

Rome, 11 November 1944

Subject: Repair of tracts of PP.SS. galleries and sewers in "Ostiense" street.

To : Rome Comune - Att.: General Inspector Faccenda.

1. Scope of work: Both galleries and sewers are located on each side of the wide parkway street and were damaged by bombs. The project contemplates the reconstruction of the part of the PP.SS. galleries and sewers lying between Ostiense square and General Market. Total length of reconstruction approximately m.600.

2. Estimated cost: L. 3,590,000 (extras included).

3. Controlled materials: Not requested.

4. Recommendation: This project is approvediin principle. The work is started and at present is approximately 90% completed.

5. Remarks: Probable time of completion: 90 days.

6. Enclosures: 3 copies approved of Form ACC/1
3 copies approved of Form ACC/2 (1° lot)
3 copies approved of Form ACC/2 (2° lot)

A.E.MICHEL, Major, S.R.
for Regional Engineer
Lazio- Umbria Region

Distribution:

Regional Engineer 1
Col.Jenny - P.W.Sub-Comm. 1 ✓

1720

Lt Col Thompson
These may reach you later for approval from Pizzano.
Lt. J. 17/11

Noted M. 22/11

Declassified E.O. 12356 Section 3.3/NND No. 785019

Declassified E.O. 12356 Section 3.3/NND No. 785019

RECEIVED
P.W. & D. S/C A.C.
25 NOV 1944
HQ ROME AREA ALLIED COMMAND
APO 794 US ARMY

078

Ref: 23A

24 Nov 44

Subject: Prevention of Accidents.

HQ Allied Commission

Ref the attached copy memo from DPM.

1. It would seem that the lack of a protective fence or wall inside the footpath skirting the Foro di Augusto has already caused a regrettable waste of life and, under present circumstances, will continue to do so.

2. It is requested that representations may be made to the Municipality to remedy this state of affairs as a matter of extreme urgency.

A.L. LOUDEN
Major
for Brigadier
Commander British Troops Rome

BV/1/ag

Declassified E.O. 12356 Section 3.3/NND No. 785019

COPY

OFFICE OF THE PROVOST MARSHAL
Rome Allied Area Command
Tel 478813 - 478675-6

Subject: Dangerous locality.

Our Ref: Pro 2 22 Nov 44

DAAG
HQ RAAC

The following accidents have been reported to Allied Police during the past two months, all of which have concerned members of the Allied Armies who have fallen from the footpath into the FORO DI AUGUSTO, VIA ALESSANDRINA.

1. 9 Oct 44. Polish soldier seen lying in the ruins at bottom of the wall. He was removed by other Polish soldiers prior to arrival of C.M.P.

2. 11 Nov 44. Major HARDING - New Zealand Forces found dead in the ruins at bottom of the wall.

3. 13 Nov 44. No.1837216 GNR TRIGODILL. J.C. - 224/78 HAA Regt, RA, found critically injured in the ruins at the bottom of the wall. It is understood that this soldier has since died.

4. 20 Nov 44. 3 British soldiers fell over the wall but were uninjured and dissappeared before arrival of the CMP

Foul play is not suspected. The place concerned is particularly dangerous, especially after dark and I recommend that arrangements be made for the area to be wired off.

??
Lt Col
Provost Marshal

GW/egl
ag

1718

Raggiani asked to put up fence immediately. Not an engineering problem and needs no approval.
M. 30/11

Declassified E.O. 12356 Section 3.3/NND No. 785019

Tel.489081.Ext.339

HEADQUARTERS ALLIED COMMISSION
APO 394
Public Works and Utilities Sub-Commission

RWS/rlv

078/L-U/9/PWU

18 November 1944

Subject: Repairs and Salvage - Civitavecchia Harbor

To : Regional Commissioner, Lazio - Umbria
(Att: Regional Engineer)

Reference letter R4/ENG/59 dated 11 Nov.44

1. All documents including from ACC/1 were received in this HQ., from the Ministry of Public Works on 16 Nov.44. The scheme was given immediate approval and an approved copy of form ACC/1 was returned to the Ministry on the same date.

2. Attached is your approved copy of form ACC/1 for this work.

V.S.THOMPSON.
Lt.Col. R.C.E.
Chief.Public.Wks.Div.

1717

Declassified E.O. 12356 Section 3.3/NND No. 785019

Tel.489081 Ext.335

HEADQUARTERS ALLIED COMMISSION
ATC 394
Public Works and Utilities Sub-Commission

DS/fr

078/L-U/9/PWU

16 November 1944

Subject: Rome University (and similar projects).

To : Regional Commissioner, Lazio-Umbria.
(Att: Regional Engineer).

1. We return herewith a group of projects relating to Rome University, without action, for the following two reasons.

Reason No. 1.

We are aware of a change in policy agreed upon between this Sub-Commission and the Italian Ministry of Public Works whereby future non-military projects in Liberated Areas under Italian Government jurisdiction will be entirely their own responsibility.

Fuller and more formal notice of this policy change will shortly be promulgated and forwarded to you.

Meanwhile, these returned projects, and any other similar type of project, should be the subject of careful restudy by the Italian Ministry of Public Works.

Reason No. 2.

Our considered opinion is that much of the work outlined in these projects could well be postponed to some future time when material and funds will not be so sorely required for the much more essential job of housing.

For example, the amount of glass required if these projects are carried out is tremendous, and it should be drastically reduced. Other material could be temporarily employed to close in most of the exterior openings. Activities housed in many buildings requiring repairs should be consolidated or moved

1716

;/;

Declassified E.O. 12356 Section 3.3/NND No. 785019

or compressed into fewer undamaged or lightly damaged buildings, and damaged unused buildings temporarily and cheaply protected against deterioration and nothing more at this time.

There exists little present likelihood that the entire facilities as to square footage of space of the University is actually now required. As if it were, it is still questionable as to whether or not priority of work, funds and material should not be given to more essential needs of the population.

If a restudy results in proper compression of activities, repairs to plant and utilities may also be concentrated over small areas and the balance of electricity, water and other services temporarily cut off, thus further reducing presently necessary work.

Where buildings are actually in use or critically required for hospital purposes, such projects should proceed speedily; all such received to date have been approved by this office.

V.S.THOMPSON
Lt. Col. R.C.E.
Chief, Public Wks. Div.

Copy to:
Ministry of Public Works.

31 OCT Recd

C.de CMF/gb

c/ow. CMB

W 1826

HEADQUARTERS
ALLIED MILITARY GOVERNMENT
LAZIO UMBRIA REGION
(Engineering Division)
APO 394

30 October 1944

TO : HQ.Region Lazio & Umbria (Attention Regional Commissioner)(2 copies)

SUBJECT: Works projects in action on projects in Italian Government Territory.

IN REPLY QUOTE : P4/ENG/A400

1. (a) Since the three Provinces of FROSINONE, LITTORIA and ROMA were handed over to Italian Government there have been 213 Projects for Repair of War Damage prepared by Genio Civile and approved by this office for onward transmission to Italian Minister of Works.

Of these 51 after Screening by Minister of Works required final approval of HQ.AC. (P.W.)

The remaining 162 being under a million lira only required approval by Minister of Works.

Out of the 51, 4 have received final approval by HQ.AC.(P.W.) NONE of the 162 have received approval of Minister.

(b) For Rome City 83 Projects have been "approved in principle" of which 17 has been received back approved. -

(c) These projects include:

Debris Removal
Bridge Reconstruction
Hospitals
Schools
Repairs to Houses
Water Supplies
Sewers.

noted dup 15/11

All of vital importance to the health and feeding of the Community - and in some cases 2½ months of building weather has already been lost. -

171

Declassified E.O. 12356 Section 3.3/NND No. 785019

30 October 1944

TO : HQ.Region Lazio & Umbria (Attention Regional Commissioner)(2 copies)

SUBJECT: Works projects in action on projects in Italian Government Territory.

IN REPLY QUOTE : R4/WEC/A400

1. (a) Since the three Provinces of FROSINONE, LITTORIA and ROMA were handed over to Italian Government there have been 213 Projects for Repair of War Damage prepared by Genio Civile and approved by this office for onward transmission to Italian Minister of Works.

Of these 51 after Screening by Minister of Works required final approval of HQ.AC. (P.W.)

The remaining 162 being under a million lire only required approval by Minister of Works.

Out of the 51, 4 have received final approval by HQ.AC;(P.W.) NONE of the 162 have received approval of Minister.

(b) For Rome City 83 Projects have been "approved in principle" of which 17 has been received back approved. -

(c) These projects include:

Debris Removal
Bridge Reconstruction
Hospitals
Schools
Repairs to Houses
Water Supplies
Sewers.

noted Dft 15/11 File

All of vital importance to the health and feeding of the Community - and in some cases 2½ months of building weather has already been lost. - 171

2. The only visible sign of action by the Ministry of Works is:

./. HE 31 OCT 1944 A.C.C.

Declassified E.O. 12356 Section 3.3/NND No. 785019

(a) Letter 1218 dated 11/X. permitting Ispettore Generale del Genio Civile del Lazio & Umbria to submit projects up to 200.000 Lire. - Detached allotment being made to each Province of this . Littoria Province one of the worst devastated only got 4,000000 Lire.

(b) Delegation to Regional Heads for acting at once in projects up to £. 500.000 approved by us and he has ~~carried~~ that in October most satisfactorily.

(c) Verbal Rumours that a sum of £. 350,000.000 for the Region may be made available sometime to last for a long period believed about a year.

(d) Definite approvals given for New Housing Schemes sufficient for 2.800 persons ammounting to about £. 300,000.000.

(e) It is NOT yet defined whether (d) has got to come out of (c), HQ.AC. (P.W.) think it will NOT.

As the total outstanding works "approved in principal" to date are approx. £.600,000.000 in any case it would only meet about half what has been prepared, and dealt with by Genio Civile and my office already and many more projects are under preparation. -

3. CONCLUSION and suggested line of action.

It is obvious that the Territory was handed over to Italian Government before they were ready to handle it.

The delay may be a technical one in Minister of Works Office but there are strong indications that he is blocked by FINANCE. -

Even in AMG Territory it took a long time to get straightened out and is NOT quite straight yet. -

ACTION. (a) Press for an immediate release of a block sum, the maximum they can approve NOW and Delegate to Ispettore Generale del Genio Civile per il Lazio & Umbria to agree with Regional Engineer Lazio & Umbria the most urgent projects to start. -

(My office has complete lists of all projects and I could go over list selected technically with your Executive officer for Provinces; if desired discuesing with each Provincial Commissioner.)

(b) Represent very strongly that HQ.AC. should in future deal with these problems in advance with foresight and settle policy and communicate it to those concerned. -

17.

Declassified E.O. 12356 Section 3.3/NND No. 785019

(b) Delegation to Regional Heads for acting at once in projects up to £. 500.000 approved by us and he has said that in October most satisfactorily.

(c) Verbal Rumours that a sum of £. 350,000.000 for the Region may be made available sometime to last for a long period believed about a year.

(d) Definite approvals given for New Housing Schemes sufficient for 2.600 persons amounting to about £. 300,000.000.

(e) It is NOT yet defined whether (d) has got to come out of (c), HQ.AC. (P.W.) think it will NOT.

As the total outstanding works "approved in principal" to date are approx. £.600,000.000 in any case it would only meet about half what has been prepared, and dealt with by Genio Civile and my office already and many more projects are under preparation. -

3. CONCLUSION and suggested line of action.

It is obvious that the Territory was handed over to Italian Covernment before they were ready to handle it.

The delay may be a technical one in Minister of Works Office but there are strong indications that he is blocked by FINANCE. -

Even in AMG Territory it took a long time to get straightened out and is NOT quite straight yet. -

ACTION. (a) Press for an immediate release of a block sum, the maximum they can approve NOW and Delegate to Ispettore Generale del Genio Civile per il Lazio & Umbria to agree with Regional Engineer Lazio & Umbria the most urgent projects to start. -

(My office has complete lists of all projects and I could go over list selected technically with your Executive officer for Provinces; if desired discussing with each Provincial Commissioner.)

(b) Represent very strongly that HQ.AC. should in future deal with these problems in advance with foresight and settle policy and communicate it to those concerned. -

./.

Declassified E.O. 12356 Section 3.3/NND No. 785019

To enable them to have time to do this HQ.AC.(P.W.) in my opinion requires to delegate to Regional Engineers much wider powers of approval (within block grants of money and material); I suggest £. 10,000.000 instead of £. 1,000.000 and so free their office of the clogging influence of approving masses of minor projects of which they cannot possibly have any knowledge whatsoever (e.g. such as all bridges over 10 foot span). -

At the conference in June at which the procedure was issued I expressed these views to the Director and at each conference have urged further delegation and decentralisation.

Projects submitted to HQ.AC.(P.W.) are normally dealt with very promptly and the resulting delay is a week to 10 days, but in distant regions it must be much longer. -

There have been long delays on POLICY over Repairs to Houses, Rehousing, FINANCE, MINES, BONIFICA, Definition of Military Road Policy, Supply of Materials especially BITUMEN, CEMENT, BRICKS.

(c) I agree that Regional Engineers should NOT have direct access to Minister but I feel strongly that when questions of Policy within the Region are being discussed by the Director or his staff with Representatives of the Minister that it would ensure full knowledge of facts and conditions if Regional Engineers was invited to attend meetings dealing with a Region like this so heavily devastated. -

Lt.Col.R.E.
Regional Engineer
Lazio Umbria Region AMG.

Copy for I.T.& T.B.(P.W.)

1719

Declassified E.O. 12356 Section 3.3/NND No. 785019

Declassified E.O. 12356 Section 3.3/NND No. 785019

Dr "Public Works"

Do see note by Lt Col White in top Rt Hd corner.

AL.

CA Sec
10 Nov 44.

1711

Declassified E.O. 12356 Section 3.3/NND No. 785019

TELEGRAM

NOV Recd
153 c2
10 NOV. 1944

MINISTRY OF INTERIOR

II865 - II853 - We re-write to the Allied Commission the following telegram sent on the same date to the Navy Office and Ministry of Public Works:

Some days ago the Tiber overflew in the Zone of Fiumicino and flooded the central villages reaching more than 60 cm. of height.

It was stated that such inundation was motivated by obstruction of the river mouth committed by the Nazis by sinking some big crafts.

To avoid that a similar inconvenient could happen again it is necessary to blow up as soon as possible these crafts in order to enlarge the river mouth . At the place of the destructed bridge a ferry boat must be set to connect the rural inhabitants who have been blocked up.

We trust you'll intervene on behalf of the above mentioned Offices if they'll ask for.

Lt Col Thompson

Will you please take this up with Findlay and give me a draft reply to this letter Thx 11/11

Col Findlay has this matter in hand.
He is receiving a report today from Brig Langrand will keep

Declassified E.O. 12356 Section 3.3/NND No. 785019

Mod. 841

Ministero dell'Interno

GABINETTO

UFFICIO DEL TELEGRAFO E DELLA CIFRA

Telegramma N.

COMMISSARIO CAPO COMMISSIONE ALLEATA = ROMA

II865 II853 Gab. Trascrivo codesta Commissione telegramma in pari data trasmesso Ministeri Marina et Lavori Pubblici :

"Nei giorni scorsi per eccessivo ingrossamento fiume Tevere straripava nella zona di Fiumicino allagando abitato centrale et ivi raggiungendo altezza di centimetri sessanta punto

Est stato accertato che causa inondazione est ostruzione della foce del fiume fatta dai tedeschi con affondamento alcuni grossi natanti punto Ad evitare ripetersi inconveniente occorre fare saltare subito natanti et allargare sbocco di fortuna già aperto punto

Recupero natanti secondo parere Genio Civile appare inopportuno et problematico mentre urge assicurare deflusso acque punto

Occorre inoltre stabilire traghetto tra Fiumicino et Isola Sacra in sostituzione ponte distrutto per collegare popolazione rurale rimasta bloccata punto

Ministeri cui presente est diretto prenderanno accordi per attuazione immediata quanto sopra assicurando telegrafo punto Qualora fosse necessario Ministeri potranno rivolgersi at Commissione Alleata alla quale viene comunicato presente dispaccio punto "

Faccio affidamento su pronto et cordiale appoggio qualora at Ministeri predetti occorresse intervento codesta Commissione et ringrazio .

PRESIDENTE CONSIGLIO MINISTRO INTERNO

BONOMI

MINISTERO
DEI
LAVORI PUBBLICI

Direzione Generale dei
Servizi Tecnici

Prot. N. 883/17 82 *Div.* .....
Allegati N. ./.
Risposta al foglio del .....
Div. ..... *Sez.* ..... *N.* .....

9 OCT 1944 194..

Al Lt. Col.L.A. JENNY
Direttore Sottocommissione Lavori
Pubblici e Pubblici Servizi dell'A.C.
R O M A

4

OGGETTO

Roma-Danni bellici. Riparazione Istituto di Ortepedia della R.Università.

Per l'approvazione definitiva dell'On. Quartier Generale, si trasmette il progetto 10 agosto 1944, dell'importo di L. 3.000.000, ridotto a L. 2.650.000, compilato dall'Ufficio del Genio Civile di Roma per le Opere Edilizie della Capitale e relativo ai lavori indicati all'oggetto.

Il progetto è stato preventivamente approvato dall'Ingegnere Regionale Alleato, come risulta dagli atti.

Si resta in attesa della cortese restituzione del progetto medesimo con l'approvazione definitiva.

IL DIRETTORE GENERALE

17/8

Lt Col Thompson

Declassified E.O. 12356 Section 3.3/NND No. 785019

Alligati N. .....

Risposta al foglio del .....

Div. ..... *Sez.* ..... *N.* .....

OGGETTO

Roma-Danni bellici. Riparazione Istituto di Ortepedia della R.Università.

Per l'approvazione definitiva dell'On. Quartier Generale, si trasmette il progetto 10 agosto 1944, dell'importo di L. 3.000.000, ridotto a L. 2.650.000, compilato dall'Ufficio del Genio Civile di Roma per le Opere Edilizie della Capitale e relativo ai lavori indicati all'oggetto.

Il progetto è stato preventivamente approvato dall'Ingegnere Regionale Alleato, come risulta dagli atti.

Si resta in attesa della cortese restituzione del progetto medesimo con l'approvazione definitiva.

IL DIRETTORE GENERALE

Lt Col Thompson

Rec'd 10/11

Dejan 17/8

Declassified E.O. 12356 Section 3.3/NND No. 785019

MINISTERO
DEI
LAVORI PUBBLICI

Direzione Generale dei
Servizi Tecnici

Prot. N. 1781 *Div.* .....
Allegati N. .....
Risposta al foglio del .....
Div. ..... *Sez.* ..... *N.* .....

OGGETTO

Roma - Riparazione Istituto
Regina Elena. Danni bellici.

9 NOV 1944 194

Al Lt. Col. L.A. JENNY
Direttore Sottocommissione Lavori
Pubblici e Pubblici Servizi dell'A.C.
R O M A

3

Per l'approvazione definitiva dell'On. Quartier Generale, si trasmette il progetto 3 agosto 1944, dell'importo di L. 3.200.000, ridotto a L. 3.125.000, compilato dall'Ufficio del Genio Civile di Roma per le Opere Edilizie della Capitale e relativo ai lavori indicati all'oggetto.

Il progetto è stato preventivamente approvato dall'Ingegnere Regionale Alleato come risulta dagli atti.

Si resta in attesa della cortese restituzione del progetto medesimo con l'approvazione definitiva.

IL DIRETTORE GENERALE

Lt Col Thompson

10/11

1707

Declassified E.O. 12356 Section 3.3/NND No. 785019

ROMA

Prot. N. 1781 Div. .....
Allegati N. .....
Risposta al foglio del .....
Div. ..... Sez. ..... N. .....

3

OGGETTO

Roma - Riparazione Istituto Regina Elena. Danni bellici.

Per l'approvazione definitiva dell'On. Quartier Generale, si trasmette il progetto 3 agosto 1944, dell'importo di L. 3.200.000, ridotto a L. 3.125.000, compilato dall'Ufficio del Genio Civile di Roma per le Opere Edilizie della Capitale e relativo ai lavori indicati all'oggetto.

Il progetto è stato preventivamente approvato dall'Ingegnere Regionale Alleato come risulta dagli atti.

Si resta in attesa della cortese restituzione del progetto medesimo con l'approvazione definitiva.

IL DIRETTORE GENERALE

Lt Col Thompson
10/11

1707

Declassified E.O. 12356 Section 3.3/NND No. 785019

Declassified E.O. 12356 Section 3.3/NND No. 785019

Ministero dei Lavori Pubblici
CONSIGLIO SUPERIORE
Direzione Generale dei
Servizi Tecnici
N° 1772

Roma, 5 NOV. 1944 XXII

Al T.C. Col. L.A. JENNY
Direttore Sottocommissione
Lavori Pubblici e Pubblici
Servizi dell'A.C. ROMA

Risposta alla nota del
N° Div.

OGGETTO: ROMA - Danni bellici-Riparazione all'oggio Suore e cucina ammalati dell'Istituto Fisioterapico Regina Elena.

Per l'approvazione definitiva dell'On. Quartier Generale, si trasmette il progetto 1° agosto 1944, dell'importo di L. 3.000.000, ridotto a lire 2.950.000, compilato dall'Ufficio del Genio Civile di Roma per le Opere Edilizie della Capitale e relativo ai lavori indicati all'oggetto.

Il progetto è stato preventivamente approvato dall'Ingegnere Regionale Alleato, come risulta dagli atti.

Si resta in attesa della cortese restituzione del progetto medesimo con l'approvazione definitiva.

IL DIRETTORE GENERALE

Ref. to Thompson
Nov 10/44

17

MINISTERO
DEI
LAVORI PUBBLICI

Direzione Generale dei
Servizi Tecnici

Prot. N. 1483 Div.
Allegati N. 1.
Risposta al foglio del
Div. Sez. N.

9 OTT 1944

Al Lt. Col.L.A. JENNY
Direttore Sottocommissione Lavori
Pubblici e Pubblici Servizi dell'A.C.
ROMA

078/2-0/9 Rome

OGGETTO

Roma- Danni bellici. Riparazione
Istituto Fisioterapico Regina Elena.

Per l'approvazione definitiva dell'On. Quartier Generale, si trasmette il progetto 31 luglio 1944, dell'importo di L. 5.300.000, ridotto a L. 5.000.000, compilato dall'Ufficio del Genio Civile di Roma per le Opere Edilizie della Capitale e relativo ai lavori indicati all'oggetto.

Il progetto è stato preventivamente approvato dall'Ingegnere Regionale Alleato, come risulta dagli atti.

Si resta in attesa della cortese restituzione del progetto medesimo con l'approvazione definitiva.

IL DIRETTORE GENERALE

Declassified E.O. 12356 Section 3.3/NND No. 785019

Risposta al foglio del .....

Div. ..... *Sez.* ..... *N.* .....

018/2-0/9 Parte

OGGETTO

Roma- Danni bellici. Riparazione
Istituto Fisioterapico Regina Elena.

Per l'approvazione definitiva dell'On. Quartier Generale, si trasmette il progetto 31 luglio 1944, dell'importo di L. 5.300.000, ridotto a L. 5.000.000, compilato dall'Ufficio del Genio Civile di Roma per le Opere Edilizie della Capitale e relativo ai lavori indicati all'oggetto.

Il progetto è stato preventivamente approvato dall'Ingegnere Regionale Alleato, come risulta dagli atti.

Si resta in attesa della cortese restituzione del progetto medesimo con l'approvazione definitiva.

IL DIRETTORE GENERALE

1705

Declassified E.O. 12356 Section 3.3/NND No. 785019

0607
