
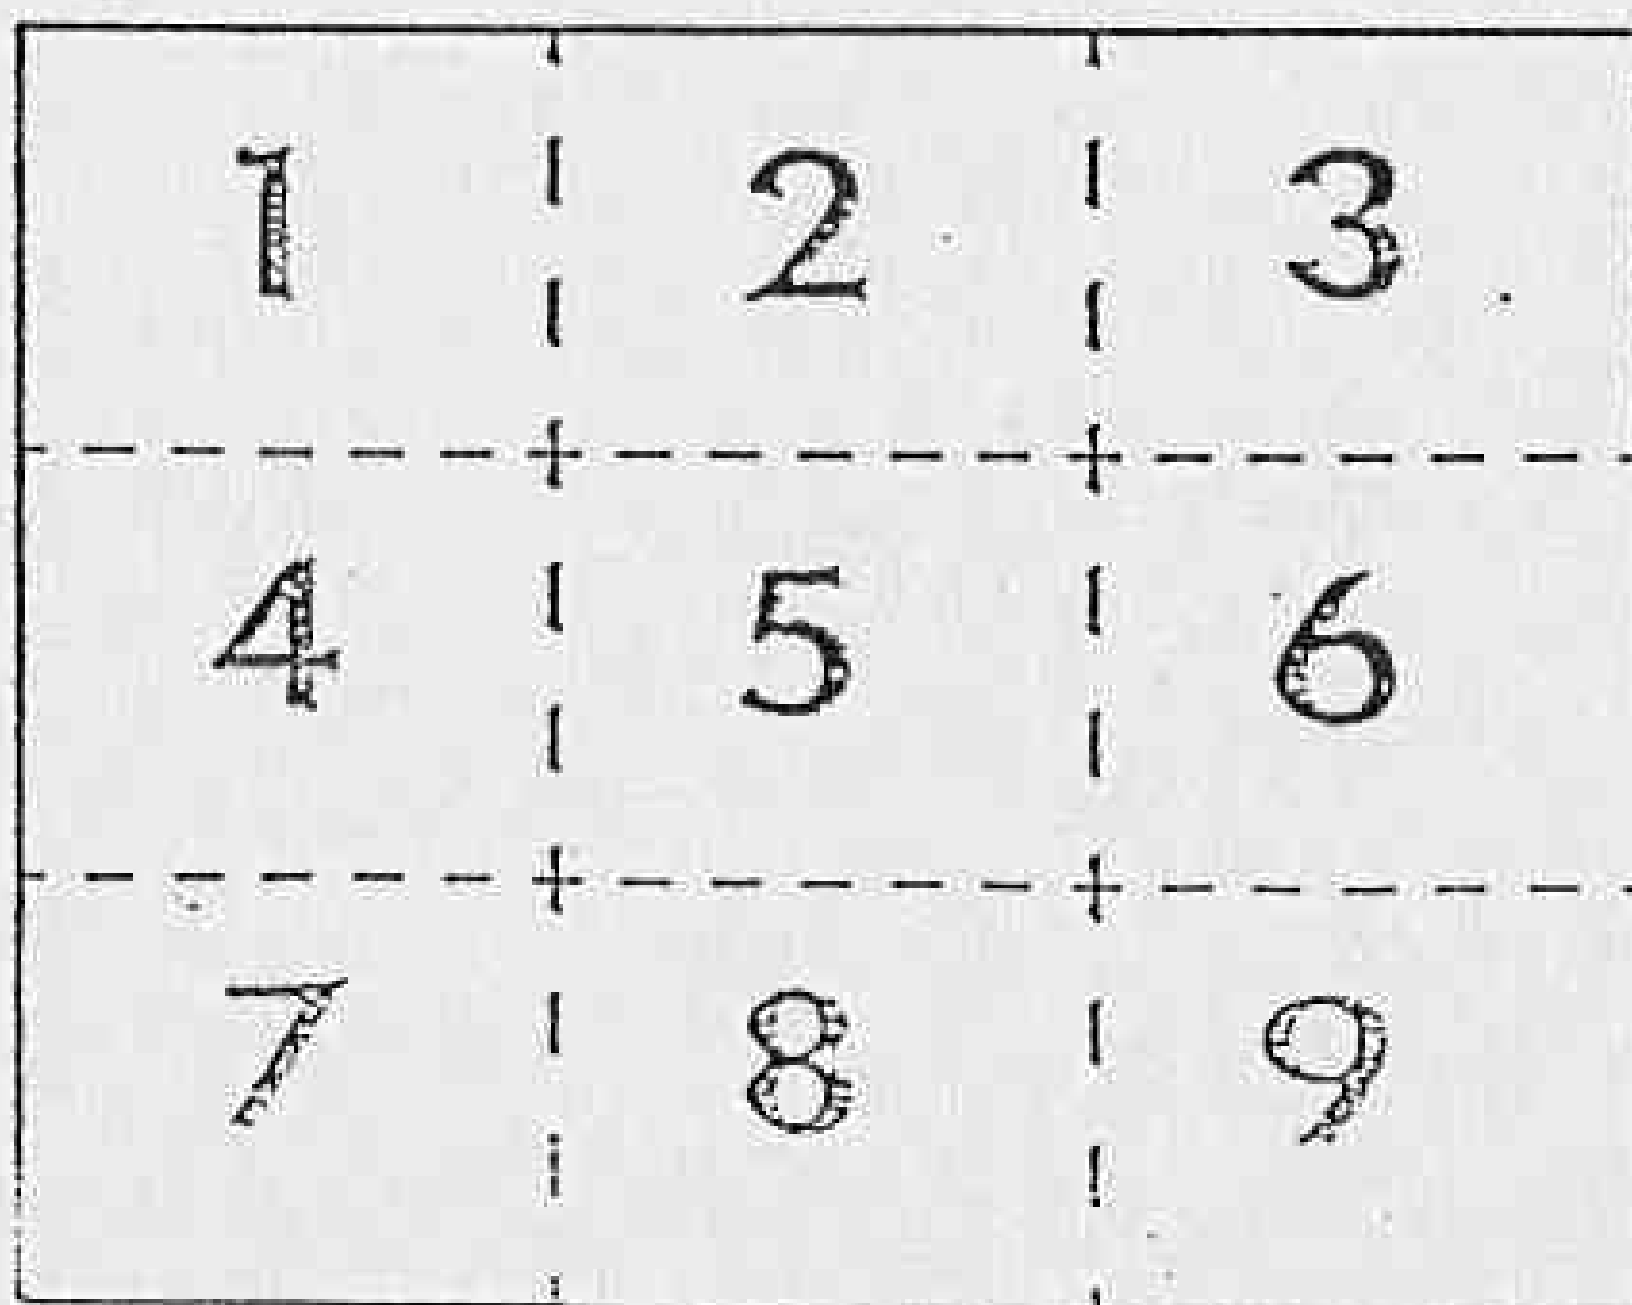
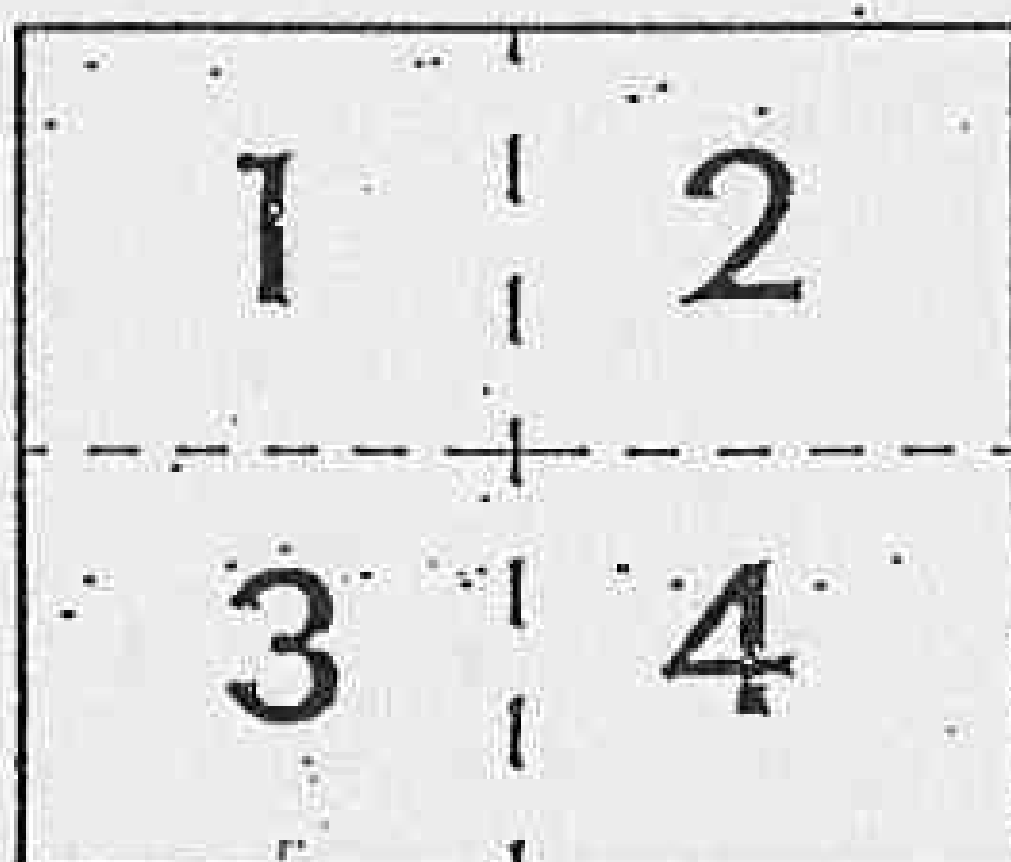


ACC AC 8/9/0 10000/148/1919 WEEKLY REP
JUN. 1945

WEEKLY REPORTS - GENOVA COMPARTMENT
JUN. 1945

MAPS AND CHARTS TOO LARGE TO FILM
ON ONE EXPOSURE ARE FILMED CLOCKWISE
BEGINNING IN THE UPPER LEFT CORNER,
LEFT TO RIGHT, AND TOP TO BOTTOM.

... SEE DIAGRAMS BELOW.

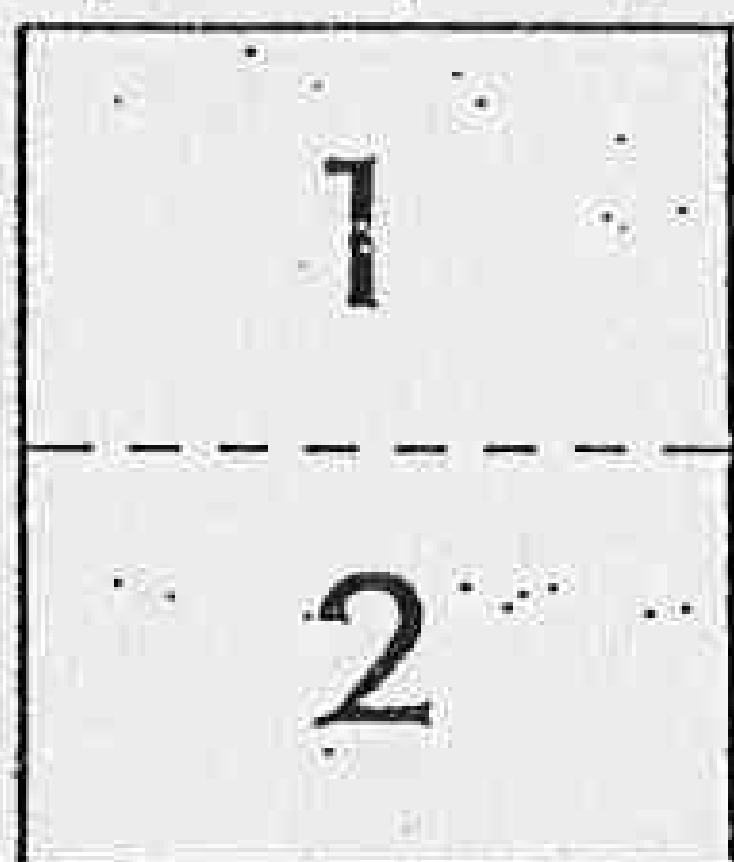

3.	Castello Tunnel Portal Genoa-side betw. Noli & 4,70 m S and length and abt. 50m inside re- ditch at Genoa-votomoni fallen in. noe-side betw. Ditch Genoa-side Celle Albino-encumbered with sols, km 54+600 materials due to landslip of the Aurelia Road	Removal of debris, Coopers-5/5 propping and con- rative tering of the Edilizia Savona tunnel	100	10/6	1.500.000	Completed
4.	Terminio Tunnel Portal Genoa-side betw. Noli & 4,70m (A, 70m) and bisopoli & 30m 40m of inside viana, 280,05 m revetment fal- length, at km 37+500	a) deviation of the line at the Asterzo sea-side) b) repairs of the tunnel	100	13/6	800.000	Completed
5.	Iron Bridge the frame (open betw. Savona & 24,60m. The two supported by heaps Avade, on the main beams were of cross-bars, the A firm Quigliano broken off short, track has been re-piazzando	5/5	100	15/5	350 000	Completed
6.	Noli tunnel the revetment of betw. Noli & 4,70 m span fal- Verigotti len in for abt. east-side 100 m. 1066,70 m l. at km 55+750	Removal of debris Ghi- and centering of the tunnel	100	15/6	1.000 000	Completed
7.	S. Donato the portal and a Tunnel betw. part of the tun- Verigotti & nel for abt. 30m Pinalpina, fallen in. A fur- 1018,65 m l. ther distance of km 60+400 50 m inside also fallen in, forming a cavity.	Removal of debris Ghi- and centering of the tunnel	65	15/7	1.800 000	Removal of debris pro- ceeding. Timber for the tunnel structure not yet supplied in the whole needed quantity Date of completion wi probably be delayed.
8.	S. Spirito Both tunnels fal- Tunnel betw. len in, spans: Borghetto & 4,70 & 5,20 m on Cerviale, km distance of abt.	Removal of debris Cerruti and centering of the tunnels. Manfredi	100	15/6	2.000 000	Completed.

6137

300

①

16/6/45.

613

299

2

1280

Declassified E.O. 12356 Section 3.3/NND No.

785021

6130

298

1281

Declassified E.O. 12356 Section 3.3/NND No.

785021

3

1282

Declassified E.O. 12356 Section 3.3/NND No.

785021

5



Weekly report: 16th June 1945

TION OF GENOA
(Sena B.)

Summary description of temporary re= pairs.	Agency	Initial date	Pro= gress	Est"ed date of com= pletion	Presumed tender	Remarks
Temporary bridge with laminated beams on temporary supports.	Sella & Granata	21/5	100	1/6	150.000=	

1292

DE LAVORI DI GENOVA
Monte-Bressana B.)

Rapporto settimanale al 16/6/1949

di nota di osservazioni e note-

6129

297

⑦

