


ACC 078/4/3/AM

10000/150/317

ACC/
JULY

10000/150/317

ACC/2, ABRUZZI - MARCHE
JULY - NOV. 1944



MINISTERO DELLE CORPORAZIONI

UFFICIO STUDI E RICERCHE

078/145/111

opened: 1 January 54
closed: 14 September 54

Abnuz



ABRUZZI - Marche - all/2

078/1/3/1/1/1

Operad: 1 January 44
Collected: 14 September 44



10000 / 150 / 317
THIS END

100 JAN 44
100 JULY 44
100 NOV 44

ALOGUE

HEADQUARTES

ALLIED ~~CONTROL~~ COMMISSION

Form. ACC/2

(Contract)

Public Works and Utilities Sub-Commission
APO 394

CONTRACTS

NOTE: This form to be submitted in triplicate through the Regional Engineer to Sub-Commission HQ, for approval. One copy to be retained by HQ, one copy returned to Regional Engineer, and one copy forwarded to Military Authority having jurisdiction.

(a) ~~Road~~ Bridge etc.: State r'd N.16 "Adriatica", partial reconstruction of the bridge at the km. 468 + 680 over Moro (C 344122). =

(b) Contractor: Battistella Giuseppe

(c) Address of Contractor: Lanciano

(d) Number of Bids Received: one

(e) Reason for Award: Available contractor on the place of the works

(f) Remarks: Works were ordered and approved by 84 C.R.E. and 21 CRE (270 Wks)

(g) Contractor's Warehouse, rendezvous: Lanciano

(h) Amount of Contract (Lire): 692.000 (see back)

(i) Nature of Contract: cost plus

(j) Contractor's Available Equipment: shovels, picks, barrows and timber. 4740

(k) Required Materials: Tns.119 of cement furnished by the R.E.

(l) Required Plant: nothing


(m) Required Transport: N.2 trucks furnished by the R.E.

APPROVAL RECOMMENDED:


Regional Engineer

Date 16/10/44

APPROVED:

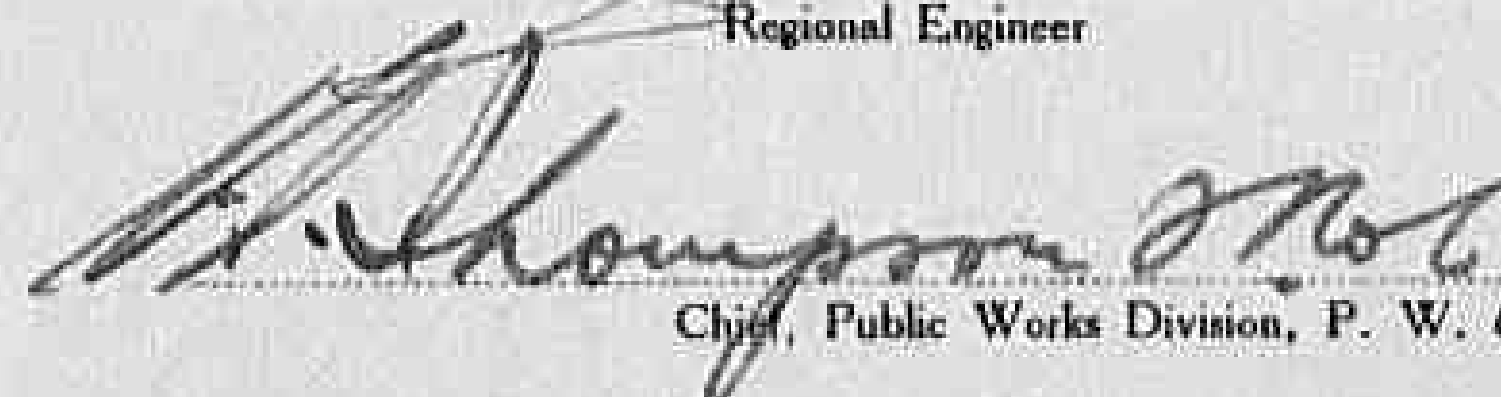
Chief, Public Works Division, P. W. & U. Sub-Commission

Date 1/11/44

- Amount of the estimate

L. 758.000

- To deduct from the cost of materials
directly purchased

" 66.250

Remainder

L. 691.750,00

In round figures L. 692.000,=

APPROVED:

HEADQUARTERS ALLIED CONTROL COMMISSION

Public Works and Utilities Sub-Commission

APO 394

Form. ACC12

(Contract)

Region ... Marche ...

Province Ascoli Piceno

CONTRACTS

(B - 906802; B- 900827)

NOTE: This form to be submitted in triplicate through the Regional Engineer to Sub-Commission HQ., for approval. One copy to be retained by HQ., one copy returned to Regional Engineer, and one copy forwarded to Military Authority having jurisdiction.

- (a) Road, Bridge etc.: over the Albula + Ragnola rivers on St. rd (milit.) No 16
- (b) Contractor: Ercolani Gianbattista
- (c) Address of Contractor: Ascoli Piceno
- (d) Number of Bids Received: one
- (e) Reason for Award: Urgency of works prevented more extensive taking of bids by the Genio Civile
- (f) Remarks: Works were initiated by order of the 1210 CRE -
Materials are furnished by the CRE -
- (g) Contractor's Warehouse, rendezvous: ASCOLI
- (h) Amount of Contract (Lire): 649,340
- (i) Nature of Contract: cos. plus
- (j) Contractor's Available Equipment: what is needed for such works
- (k) Required Materials: =
- (l) Required Plant: =
- (m) Required Transport: =

APPROVAL RECOMMENDED:




Date

24/10/42

Regional Engineer

APPROVED:



Date

1/11/42

Chief, Public Works Division, P. W. & U. Sub-Commission.

HEADQUARTERS ALLIED CONTROL COMMISSION

Public Works and Utilities Sub-Commission

APO 394

Form. ACC/2
(Contract)Region... Marche...
Province... Ascoli.P.

CONTRACTS

(B.905809; B.905805)

NOTE: This form to be submitted in triplicate though the Regional Engineer to Sub-Commission HQ., for approval. One copy to be retained by HQ., one copy returned to Regional Engineer, and one copy forwarded to Military Authority having jurisdiction.

- (a) ~~Road, Bridge~~ over the Acquaschiara + Brancadoro rivers on St. rd. (mil.)
No 16
- (b) Contractor: Ercolani Giambattista
- (c) Address of Contractor: Ascoli Piceno
- (d) Number of Bids Received: one
- (e) Reason for Award: Urgency of works prevented more extensive taking of bids by the Benio Civile.
- (f) Remarks: Works were initiated by order of the 1210 CRE - Materials are furnished by the CRE
- (g) Contractor's Warehouse, rendezvous: ASCOLI
- (h) Amount of Contract (Lire): 377,500
- (i) Nature of Contract: cost plus
- (j) Contractor's Available Equipment: what is needed for such works -
4738
- (k) Required Materials: =
- (l) Required Plant: =
- (m) Required Transport: =

APPROVAL RECOMMENDED:




Date

4/10/44

Regional Engineer

APPROVED:



Date

4/11/44

Chief, Public Works Division, P. W. & U. Sub-Commission.

HEADQUARTERS ALLIED CONTROL COMMISSION

Public Works and Utilities Sub-Commission

APO 394

Form. ACC/2
(Contract)

Region

Province

CONTRACTS

NOTE: This form to be submitted in triplicate though the Regional Engineer to Sub-Commission HQ., for approval. One copy to be retained by HQ., one copy returned to Regional Engineer, and one copy forwarded to Military Authority having jurisdiction.

- (a) Road, Bridge etc.: State r'd N.16 "Adriatica". Reconstruction of a small bridge at km. 462+850 over IOMERA (C.290108)
- (b) Contractor: Capozzi Michele fu Alfonso.
- (c) Address of Contractor Pescara - Castelfidardo street n.10.
- (d) Number of Bids Received: one
- (e) Reason for Award: Only available contractor on the place of works.
- (f) Remarks: Works were started by order of the 21° CRES (270 W.S.)
- (g) Contractor's Warehouse, rendezvous: Pescara - Castelfidardo street n.10
- (h) Amount of Contract (Lire): L.275.000 (see back)
- (i) Nature of Contract:
- (j) Contractor's Available Equipment: All the equipment necessary 4737
- (k) Required Materials: Tons 50 of cement already furnished by the CRES
- (l) Required Plant: Nothing
- (m) Required Transport: the same.

APPROVAL RECOMMENDED:



Date

14/10/44

Regional Engineer

APPROVED:



Date

1/11/44

Chief, Public Works Division, P. W. & U. Sub-Commission.

..... Amount for contract :

..... Estimate L. 400.000

To deduct from:

1°) Materials directly purchased
L. 65.110.-

2°) Unpreventable
expenses.....L. 60.362.-

Whole deductions..... " 125.472

Remainder L. 274.528

=====

Rounded L. 275.000

=====

HEADQUARTES

ALLIED ~~CONTROL~~ COMMISSION

Public Works and Utilities Sub-Commission

APO 394

Form: ACC/2

(Contract)

 Region: Abruzzi
 Province: Pescara

CONTRACTS

NOTE: This form to be submitted in triplicate through the Regional Engineer to Sub-Commission HQ, for approval. One copy to be retained by HQ, one copy returned to Regional Engineer, and one copy forwarded to Military Authority having jurisdiction.

(a) Road, Bridge etc.: State r'd n°16 - Rehabilitation of the road body between the Km. 448 + 800 and 450; and reconstruction of a temporary diversion at Km. 449 + 700 (C185283)

(b) Contractor: Casalena Battista of L. Zopito

(c) Address of Contractor: Vittorio Colonna street - Pescara

(d) Number of Bids Received: one

(e) Reason for Award: available contractor in the place of the work

(f) Remarks: (see back)

(g) Contractor's Warehouse, rendezvous: Pescara

(h) Amount of Contract (Lire): L. 155.500

(i) Nature of Contract: unit price

(j) Contractor's Available Equipment: shovels, picks, barrows, ecc.

4738

(k) Required Materials: nothing

(l) Required Plant: the same

(m) Required Transport: the same

APPROVAL RECOMMENDED:




Regional Engineer

Date

29/6/44

APPROVED:

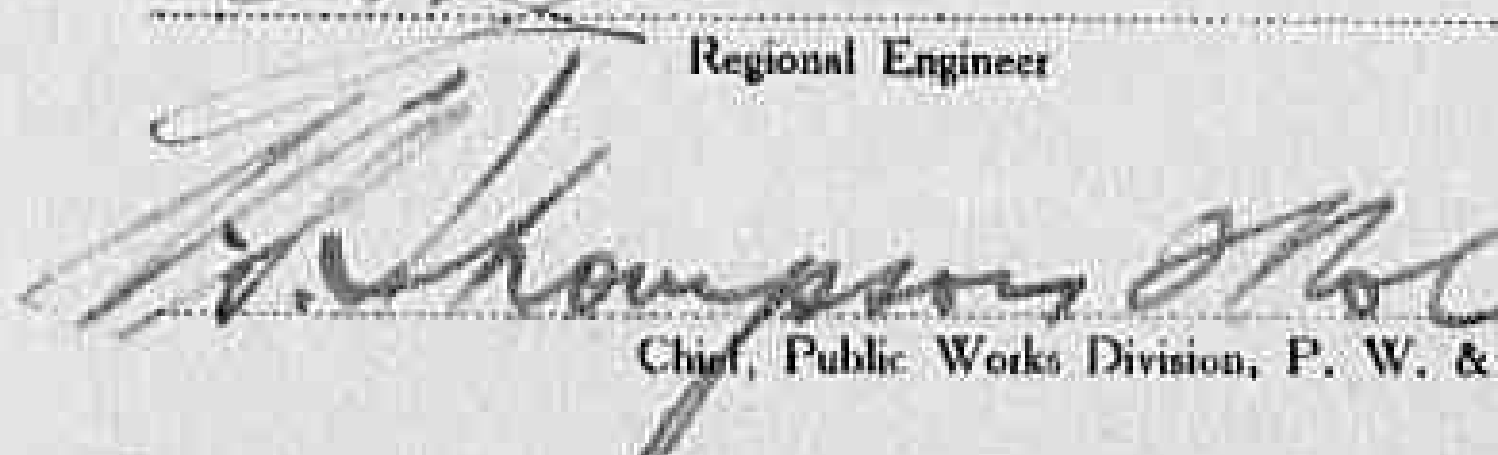

Date

1/11/44

Chief, Public Works Division, P. W. & U. Sub-Commission.

O
HEADQUARTERS
ALLIED COMMISSION

Amount of the estimate	L.	225.000,=
To deduct from the cost of materials directly purchased.	"	69.600,=
Remainder	L.	155.400,=
In round figures	L.	155.500,=

=====

HEADQUARTERS ALLIED CONTROL COMMISSION

Public Works and Utilities Sub-Commission

APO 394

Region AdriaticProvince Pescara

Form. ACC/2

(Contract)

CONTRACTS


NOTE: This form to be submitted in triplicate through the Regional Engineer to Sub-Commission HQ., for approval. One copy to be retained by HQ., one copy returned to Regional Engineer, and one copy forwarded to Military Authority having jurisdiction.

- (a) Road, Bridge etc.: St. r'd N.5 " Tiburtina Valeria ". Demolishing works
 (b) and removal of debris of the bridge over "Lavino". (C 008070).
 Contractor: Eng. De Pompeis Pompeo
 (c) Address of Contractor: Scafa (Pescara)
 (d) Number of Bids Received: one
 (e) Reason for Award: Only available contractor in the place of the works.
 (f) Remarks: No controlled materials required-Works were ordered by the CREs
(281 W.S.) - Military road.
 (g) Contractor's Warehouse, rendezvous: Scafa (Pescara)
 (h) Amount of Contract (Lire): 26.000
 (i) Nature of Contract: cost plus
 (j) Contractor's Available Equipment: shovels, picks, barrows and other small
equipment of workyard.
 (k) Required Materials: nothing
 (l) Required Plant: the same
 (m) Required Transport: the same

APPROVAL RECOMMENDED:


 Regional Engineer
Date 11/10/944

APPROVED:


 Chief, Public Works Division, P. W. & U. Sub-Commission.
Date 1/11/94

4735

HEADQUARTES

ALLIED ~~CONTROL~~ COMMISSION

Public Works and Utilities Sub-Commission
APO 394

Form. ACC/2

(Contract)

Region: Abruzzi
Province: Pescara

CONTRACTS

NOTE: This form to be submitted in triplicate through the Regional Engineer to Sub-Commission HQ. for approval. One copy to be retained by HQ, one copy returned to Regional Engineer, and one copy forwarded to Military Authority having jurisdiction.

(a) Road, Bridge etc.: State r'd n°5 - Construction of a culvert and new lifting of the temporary diversion at the bridge Alba (0036099)

(b) Contractor: Eng. Picchetti Salvatore

(c) Address of Contractor: Torre di Passeri (Pescara)

(d) Number of Bids Received: one

(e) Reason for Award: Available contractor in the place of the work

(f) Remarks:

(g) Contractor's Warehouse, rendezvous: Torre dei Passeri (Pescara)

(h) Amount of Contract (Lire): L. 155.000,=

(i) Nature of Contract: unit price

(j) Contractor's Available Equipment: shovels, picks, barrows, timber, decauville ecc.

(k) Required Materials: Tns. 1020 of cement and metallic net furnished by A M Eng.

(l) Required Plant: nothing

(m) Required Transport: the same

APPROVAL RECOMMENDED:

[Signature] Date 29/10/44
Regional Engineer

APPROVED:

[Signature] Date 1/11/44
Chief, Public Works Division, P. W. & U. Sub-Commission.

HEADQUARTES

ALLIED ~~CONTROL~~ COMMISSION

Public Works and Utilities Sub-Commission

APO 394

Form. ACC/2

(Contract)

Region: Abruzzi

Province: Chieti

CONTRACTS

NOTE: This form to be submitted in triplicate through the Regional Engineer to Sub-Commission HQ, for approval. One copy to be retained by HQ, one copy returned to Regional Engineer, and one copy forwarded to Military Authority having jurisdiction.

(a) Road, Bridge etc.: State r'd n°16 "Adriatica" - Portial reconstruction of the bridge over Alento river and arrangement of a Bailey bridge (C231246).

(b) Contractor: Di Carmine Domenico

(c) Address of Contractor: Palermo street- Pescara

(d) Number of Bids Received: one

(e) Reason for Award: available contractor in the place of the work.

(f) Remarks: (see back)

(g) Contractor's Warehouse, rendezvous: Palermo street -Pescara

(h) Amount of Contract (Lire): L. 572.000

(i) Nature of Contract: unit price

(j) Contractor's Available Equipment: shovels, picks, barrows, timber ecc.

4733

(k) Required Materials: Tns 92,50 of cement furnished by the A M Eng.

(l) Required Plant: nothing

(m) Required Transport: two motortruck

APPROVAL RECOMMENDED:

[Signature]

Regional Engineer

Date

29/6/44

APPROVED:

[Signature]

Date

1/11/44

Chief Public Works Division, P. W. & U. Sub-Commission

Amount of the estimate. L. 836.000,=

To deduct from:

a) for unpreventable expenses L. 139.356

b) for cost of materials directly

to purchase

L. 125.000

L. 264.356

Remainder

L. 571.644

In round figures

L. 572.000

=====

HEADQUARTERS ALLIED CONTROL COMMISSION

Form. ACC/2

(Contract)

Public Works and Utilities Sub-Commission

APO 394

Region: Abruzzi

Province: Chieti

CONTRACTS

NOTE: This form to be submitted in triplicate through the Regional Engineer to Sub-Commission HQ. for approval. One copy to be retained by HQ, one copy returned to Regional Engineer, and one copy forwarded to Military Authority having jurisdiction.

- (a) Road, Bridge etc.: State r'd n°16 "Adriatica".- Partial reconstruction of the bridge over Arielli and arrangement of a Bailey bridge (C295204)
- (b) Contractor: BATTISTELLA GIUSEPPE
- (c) Address of Contractor: Lanciano
- (d) Number of Bids Received: one
- (e) Reason for Award: available contractor in the place of the work.
- (f) Remarks: (see back)
- (g) Contractor's Warehouse, rendezvous: Lanciano
- (h) Amount of Contract (Lire): L. 547.000
- (i) Nature of Contract: unit price
- (j) Contractor's Available Equipment: shovels, picks, barrows, timber, etc.
- (k) Required Materials: Tns 65 of cement furnished by the A.M. Eng. 4732
- (l) Required Plant: nothing
- (m) Required Transport: Two motortruck " " " "

APPROVAL RECOMMENDED:

APPROVED:

Regional Engineer

Date

29/10/44

Chief, Public Works Division, P. W. & U, Sub-Commission

Date

1/11/44

Amount of the estimate

L. 597.000

Do deduct from the cost of materials
directly purchased

" 50.000

Remainder

L. 547.000

In round figures

L. 547.000

=====

HEADQUARTES
ALLIED ~~CONTROL~~ COMMISSION
Public Works and Utilities Sub-Commission
APO 394

Form. ACC/2

(Contract)

452

Region: Abruzzi
Province: Chieti

CONTRACTS

NOTE: This form to be submitted in triplicate through the Regional Engineer to Sub-Commission HQ, for approval. One copy to be retained by HQ, one copy returned to Regional Engineer, and one copy forwarded to Military Authority having jurisdiction.

(a) ~~Road, Bridge~~: State r'd n°16 "Adriatica" - Demolishing works and removal of debris in corrispondence of the bridge over Moro river at Km. 460 & 560 (C270218)

(b) Contractor: DI Carmine Domenico

(c) Address of Contractor: Palermo Street - Pescara -

(d) Number of Bids Received: one

(e) Reason for Award: Available contractor in the place of the work

(f) Remarks:

(g) Contractor's Warehouse, rendezvous: Palermo Street - Pescara

(h) Amount of Contract (Lire): L. 55.000

(i) Nature of Contract: unit price

(j) Contractor's Available Equipment: shovels, picks, barrows and timber

4731

(k) Required Materials: nothing

(l) Required Plant: the same

(m) Required Transport: the same

APPROVAL RECOMMENDED:

C. J. J. J.

Date

29/6/44

Regional Engineer

APPROVED:

W. Thompson

Date

1/8/44

Chief, Public Works Division, P. W. & U. Sub-Commission.

HEADQUARTERS ALLIED CONTROL COMMISSION

Public Works and Utilities Sub-Commission

APO 394

Region .. Abruzzi ...

Province Chieti

Form. ACC/2
(Contract)

CONTRACTS

NOTE: This form to be submitted in triplicate through the Regional Engineer to Sub-Commission HQ., for approval. One copy to be retained by HQ., one copy returned to Regional Engineer, and one copy forwarded to Military Authority having jurisdiction.

- (a) Road, Bridge etc.: over the Vallelunga (C-208270) on Mil. Highway No 16
- (b) Contractor: Savini
- (c) Address of Contractor: Pescara, Via Italica, 27.
- (d) Number of Bids Received: six
- (e) Reason for Award: lowest bid to reliable contractor
- (f) Remarks: Works are urgently needed by the 21CRE, who disposed the calling for tenders.
- (g) Contractor's Warehouse, rendezvous: Pescara
- (h) Amount of Contract (Lire): 275,488
- (i) Nature of Contract: unit price
- (j) Contractor's Available Equipment: Tools and carts, timber for scaffolding and centering.
- (k) Required Materials: to be furnished by the 21 CRE 4736
- (l) Required Plant: to be furnished by contractor
- (m) Required Transport: to be furnished by CRE.

APPROVAL RECOMMENDED:

[Signature] Date *2/10/44*
Regional Engineer

APPROVED:

[Signature] Date *1/11/44*
Chief, Public Works Division, P. W. & U. Sub-Commission.

HEADQUARTES

ALLIED CONTROL COMMISSION

Public Works and Utilities Sub-Commission

APO 394

Form. ACC/2

(Contract)

CONTRACTS

NOTE: This form to be submitted in triplicate through the Regional Engineer to Sub-Commission HQ., for approval. One copy to be retained by HQ, one copy returned to Regional Engineer, and one copy forwarded to Military Authority having jurisdiction.

(a) Road, Bridge, etc.: State r'd N.16 bis - Rehabilitation of the road body near Cappelle ~~carre~~ (C 090228).

(b) Contractor: Socciente Tullio

(c) Address of Contractor: Cappelle sul Tavo

(d) Number of Bids Received: one

(e) Reason for Award: Available contractor on the place of the works

(f) Remarks:

(g) Contractor's Warehouse, rendezvous: Cappelle sul Tavo

(h) Amount of Contract (Lire): L. 400.000

(i) Nature of Contract: cost plus

(j) Contractor's Available Equipment: shovels, picks, barrows, marriages etc.

(k) Required Materials: nothing

(l) Required Plant: the same

(m) Required Transport: the same

APPROVAL RECOMMENDED:

Chotime
Regional Engineer

Date

20/10/44

APPROVED:

Thompson
Chief, Public Works Division, P. W. & U. Sub-Commission.

Date

1/11/44

4729

HEADQUARTERS ALLIED CONTROL COMMISSION

Public Works and Utilities Sub-Commission

APO 394

Form. ACC/2

(Contract)


Region MarcheProvince Ascoli Piceno

CONTRACTS

NOTE: This form to be submitted in triplicate though the Regional Engineer to Sub-Commission HQ., for approval. One copy to be retained by HQ., one copy returned to Regional Engineer, and one copy forwarded to Military Authority having jurisdiction. (B-890860+ B-865904)

- (a) Road, Bridges etc.: over the Aiso and Tesino river on St. rd. (milit.) No. 16
- (b) Contractor: Gionfrini Giorgio
- (c) Address of Contractor: Ascoli Piceno
- (d) Number of Bids Received: one
- (e) Reason for Award: Urgency of works prevented more extensive taking of bids by the Genio Civile -
- (f) Remarks: Works were initiated by order of the 1210 CRE -
Materials are furnished by the CRE
- (g) Contractor's Warehouse, rendezvous: Ascoli
- (h) Amount of Contract (Lire): 1,300.000
- (i) Nature of Contract: cost plus
- (j) Contractor's Available Equipment: what is needed for such works
- (k) Required Materials: =
- (l) Required Plant: =
- (m) Required Transport: =

APPROVAL RECOMMENDED:




Regional Engineer

Date

4728

24/10/44

APPROVED:



Date

1/11/44

Chief Public Works Division, P. W. & U. Sub-Commission.

HEADQUARTERS ALLIED CONTROL COMMISSION

Public Works and Utilities Sub-Commission

APO 394

Form. ACC/2
(Contract)Region Marche
Province Ascoli Piceno

CONTRACTS


NOTE: This form to be submitted in triplicate though the Regional Engineer to Sub-Commission HQ., for approval. One copy to be retained by HQ., one copy returned to Regional Engineer, and one copy forwarded to Military Authority having jurisdiction.

- (a) ~~Road~~, Bridge etc.: over the S. Biagio on St. rd. no 16 - (B-850931) - Military -
- (b) Contractor: Gionfrini Giorgio
- (c) Address of Contractor: Ascoli Piceno
- (d) Number of Bids Received: one
- (e) Reason for Award: Urgency of works prevented more extensive taking of bids by the Genio Civile -
- (f) Remarks: Works were started by order of the 1210 CRE, HHQ -
Materials are furnished by the CRE -
- (g) Contractor's Warehouse, rendezvous: Ascoli
- (h) Amount of Contract (Lire): 470,000
- (i) Nature of Contract: cost plus
- (j) Contractor's Available Equipment: what is needed for such works
- (k) Required Materials: { =
- (l) Required Plant: { =
- (m) Required Transport: { =

APPROVAL RECOMMENDED:



Date



Regional Engineer

APPROVED:



Date



Chief, Public Works Division, P. W. & U. Sub-Commission.

HEADQUARTERS
ALLIED CONTROL COMMISSION
Public Works and Utilities Sub-Commission

Form ACC/2
(Contract)

(B620138) (B623130) (B619132)

Note: This form to be submitted in triplicate through the Regional Engineer to Sub-Commission HQ. for approval. One copy to be returned to Regional Engineer, and one copy forwarded to military authority having jurisdiction.

(a) Road, Bridge etc: Reconstruction of the bridges at the km. 48+900 and 49+510 and reinstatement of the transit in the varying road of FOSKIO PICEZZE

(b) Contractor: PIETROPAOLI VITTORINI

(c) Address of Contractor: Praturo (Aquila)

(d) Number of Bids Received: 1

(e) Reason for Award: It is treaty contractor of the office which gives assurance of good and strict execution of the works

(f) Remarks: Works were ordered by the 2810 C.R.E., who approved the drawings and are still supplying cement and transport.

(g) Contractor's Warehouse, rendezvous: Aquila

(h) Amount of Contract (lire): 1.222.000

(i) Nature of Contract: at schedule price

(j) Contractor's Available Equipment: timber, decanville, bacrows and other small equipment.

(k) Required materials: cement which is given from allied military Engineering

(l) Required Plant: 2810 C.R.E.

(m) Required

(c) Address of Contractor: PISTROPOLI VITTORINI
Prato (Aquila)

(d) Number of Bids Received: 1

(e) Reason for Award: It is trusty contractor of the office which
gives assurance of good and swift execution of the works

(f) Remarks: Works were ordered by the 2810 C.R.E., who approved
the drawings and are still supplying cement and transport.

(g) Contractor's Warehouse, rendezvous: Aquila

(h) Amount of Contract (Lire): 1.222.000

(i) Nature of Contract: at schedule price

(j) Contractor's Available Equipment: timber, decanville, barrows and
other small equipment.

(k) Required Materials: cement which is given from allied military Engineering
2810 C.R.E.

(l) Required Plant:

(m) Required Transport: 2 motor trucks put at disposal of the contractor
from the allied military Engineering. 2810 C.R.E.

4728

APPROVAL RECOMMENDED:

Ch. Lawrence Date 11/9/44

APPROVED:

W. Thompson Date 21/9/44

Chief, Public Works Division, P.W.S. U. Sub-Comm.

HEADQUARTERS
ALLIED CONTROL COMMISSION
Public Works and Utilities Sub-Commission

Form ACC/2
(Contract)

Note: This form to be submitted in triplicate through the Regional Engineer to Sub-Commission HQ. for approval. One copy to be returned to Regional Engineer, and one copy forwarded to Military Authority having jurisdiction.

(a) Road, Bridge etc: Reconstruction of retaining walls and of the small bridges n. 21 and 22 at the km. 4+200 and 4+400 of the state rd. n. 17 and repair of ware damages (B 260230)

(b) Contractor: Carlo Zambon fu Angelo

(c) Address of Contractor: Antrodoco (Rieti)

(d) Number of Bids Received: one

(e) Reason for Award: The works were begun by the above contractor for the order of the C.R.E. (1st District) Command and this office was charged of the continuance.

(f) Remarks:

(g) Contractor's Warehouse, rendezvous: Antrodoco (Rieti)

(h) Amount of Contract (Lire): one million two hundred eighty thousand

(i) Nature of Contract : by cost plus

(j) Contractor's Available Equipment: Timber, barrows and small equipment

(k) Required Materials: all 1661 of cement which is furnished by the

(l) Required Plant: C.R.E.s Command.

(m) Required Transport: The C.R.E.s have furnished n. 3 small motor trucks the 5th September 1944

(b) Contractor: Carlo Zambon fu Angelo

(c) Address of Contractor: Antrodoco (Rieti)

(d) Number of Bids Received: one

(e) Reason for Award: The works were begun by the above contractor for the order of the C.R.Es. Command and this office was charged of the continuance.

(f) Remarks: _____

(g) Contractor's Warehouse, rendezvous: Antrodoco (Rieti)

(h) Amount of Contract (lire): one million two hundred eighty eight thousand

(i) Nature of Contract: by cost plus

(j) Contractor's Available Equipment: Timber, barrows and small equipment

(k) Required Materials: all 1661 of cement which is furnished by the C.R.Es. Command.

(l) Required Plant: _____

(m) Required Transport: The C.R.Es. have furnished n.3 small motortruck which the 5th september inst. have been revoked. It is required at least four motortruck.

4725

APPROVAL RECOMMENDED:

Officer Date 11/9/44

APPROVED:

W. Thompson Date 11/9/44

Chief, Public Works Division, P.W. & U. Sub-Comm.

UNITED STATES GOVERNMENT
Public Works and Utilities Sub-Commission
CONTRACTS

Form 100/2
(Contract)
APO 194

Note: This form to be submitted in triplicate through the Regional Engineer to Sub-Commission for approval. One copy to be retained by HQ., one copy returned to Regional Engineer, and one copy forwarded to Military Authority having jurisdiction.

(a) Road Bridge etc.... Patch & Sealcoat road Ariano-Foggia Bay

(b) Contractor: S.I.C.E.L.P. *e. Ciapparelli*

(c) Address of contractor: BARI *e. Naples*

(d) Number of bids received: ON E

(e) Reason of award: N. o. other contractor available with adequate equipment

Price based on Messer SICELP alone
(f) Remarks: Price of part done by Ing. Ciapparelli still under discussion

(g) Contractor's warehouse, residence: BARI

(h) Amount of Lire: ¹² 2,747,500

(i) Nature of contract: Schedule Unit Price

(j) Contractor's available equipment: Crushers 2
Rollers 2 Sprayer 1

(k) Required Materials: Bitumen

(l) Required plants: NIL

(m) Required Transport: WD Tpt arranged

Approval Recommended: *e. Houchet* 5 Aug 44

Approved: *M. Thompson* 29/8/44 4721
Chief, Public Works Division, P. & U. Sub-Commission

2

HEADQUARTERS
ALLIED CONTROL COMMISSION
Public Works and Utilities Sub-Commission
APO 394

RWS/fr

11 July 1944

Subject: Contracts.

To : Regional Engineer Offr. Region V

1. Attached hereto are the following
approved documents.

<u>Number</u>	<u>Location</u>	<u>Cost</u>
161	Bridge over Cervaro River	£ 3,900,000

V.S. THOMPSON
Lt. Col. R.C.E.
Chief, Public Wks. Div.

472

HEADQUARTERS
ALLIED-CONTROL COMMISSION
Public Works and Utilities Sub-Commission
APO 394

16F
1
Form ACC/2
(Contract)

CONTRACTS

Note: This form to be submitted in triplicate through the Regional Engineer to Sub-Commission HQ. for approval. One copy to be retained by HQ., one copy returned to Regional Engineer, and one copy forwarded to Military Authority having jurisdiction.

- (a) Road, Bridge etc: Bridge over Cevere river Foggia-Cerignola road
- (b) Contractor: Quarato Giovanni
- (c) Address of Contractor: Piazza DE Sanctis N 3 Foggia
- (d) Number of Bids Received: 3
- (e) Reason for Award: Lowest bid
- (f) Remarks: Ref PW&U/LO/2 dated 12 MAY 44 from Major Knight to Major Perley copy to Lt Col Thompson. Plan has been approved by C E No 2 Dist and copy forwarded to Naples
- (g) Contractor's Warehouse, rendezvous: as in para (c)
- (h) Amount of Contract (Lire): L 3,900,000
- (i) Nature of Contract: SCHEDULE UNIT PRICE.
- (j) Contractor's Available Equipment: All necessary
- (k) Required Materials: Cement application made to Provincial supply officer for 180 tons.
- (l) Required Plant: NIL
- (m) Required Transport: WD or Genio Civili to supply all transport

APPROVAL RECOMMENDED:

E. Housley
for Regional Engineer. Date 1 Jan 46

APPROVED:

W. Thompson
Date 4722
Chief, Public Works Division, P.W.&U. Sub-Commission.

1672
